

# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF AUGUST 2022

### WORK COMPLETED AND ONGOING:

#### Site

- Mass grading ongoing at the building pad; retaining wall and parking areas complete
- Sanitary sewer complete
- Water line 85% complete
- Storm lines 76% complete
- Shoring of the retaining wall is complete
- Excavation of retaining walls ongoing

#### Building

- All Piers for the building have been completed
- Grade beams ongoing – Areas 1, 3, and 4
- MEP underground installation began on August 15



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF AUGUST 2022




# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF AUGUST 2022

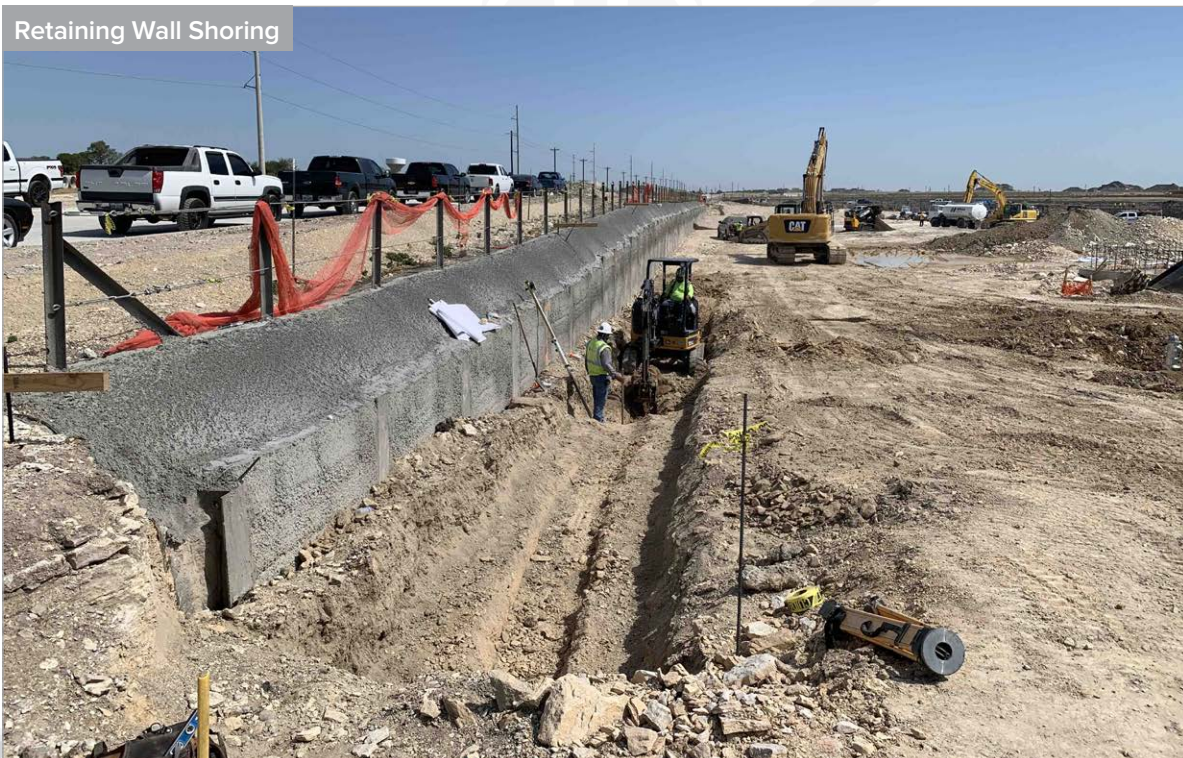

Retaining Wall Shoring

# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF AUGUST 2022

Grade Beam Formwork and Reinforcing



Grade Beam Formwork and Reinforcing



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF AUGUST 2022

Grade Beam Formwork and Reinforcing



Complete Grade Beams



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



**LILYANA ELEMENTARY SCHOOL (ES#16)**

AS OF AUGUST 2022

Back Filling at Grade Beams



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## DAN CHRISTIE ELEMENTARY SCHOOL (ES#17)

AS OF AUGUST 2022

### WORK COMPLETED AND ONGOING:

#### Permits

- Civil Permit – Permit to be issued by the middle of September
- Building Permit – Town has the documents for review
  - Building Permit will not be issued prior to the civil permit release

#### Pricing

- RFP for the Civil scope has been received and priced
  - Pogue to compile pricing and submit to the district and Huckabee for approval



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF AUGUST 2022

### WORK COMPLETED AND ONGOING:

#### Permits

- Civil Permit – issued
- Building Permit – Pending Town review

#### Site

- Installing sanitary sewer and storm sewer piping
- Site grading substantially complete
- Hauling off excess soil
- Established water service on site
- Exterior security fence complete

#### Building

- Need building permit so that underground MEP can begin
- Received grade beam permit
- Building pad to grade
- Moisture conditioning of soil complete
- Piers complete – Area A
- Drilling piers – Areas B and C
- Chemically treating soil – Area A





# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF AUGUST 2022



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF AUGUST 2022



Underground Site Utility Trenching



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF AUGUST 2022

Underground Site Utility Installation



Piers and Grade Beam Formwork



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF AUGUST 2022

Piers and Grade Beam Formwork



Grade Beam Formwork and Reinforcing



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF AUGUST 2022

Grade Beam Formwork and Reinforcing



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

### WORK COMPLETED AND ONGOING:

#### Site

- Baseball and softball fields are ready for turf (installation to occur in about six months)
- Detention pond irrigation ongoing
- Sports lighting installation ongoing at tennis courts
- Irrigation installation ongoing on the west and east side of the property

#### Building

- Steel erection complete – Areas A, B, C, E, L, M, P, Q, R, and S
- Steel erection ongoing – Areas D, F and N
- MEP/Fire Sprinkler overhead ongoing – Areas Q, R, P, S and D1
- Fire Sprinklers approved first and second floors – Areas A, B and C
- Framing complete – Areas A, A2, B, B2, C, C2, and D
- Framing ongoing – Areas E1, Q, and R
- Interior CMU walls ongoing – Areas M and P

- Roofing dried in – Areas A, B, C, P, Q, and R; ongoing in Area S
- Exterior waterproofing ongoing – Areas D and E
- Masonry veneer installation ongoing North side – Areas A, B and C
- Fireproofing ongoing – Areas D2 and E
- Fire alarm installation ongoing – Areas A1, B1 and C1
- Painting ongoing – Areas A1, A2, B1, and B2
- Low-voltage rough-in ongoing – Areas A1 and A2
- Security and access control ongoing – Areas A1 and B2
- Tile installation ongoing in A1 restrooms for mockup approval

#### Multipurpose Facility (MPF) and Ancillary Buildings

- Masonry ongoing – Areas U and V
- Masonry skin installation ongoing – Area T
- Waterproofing ongoing – Area V and concession stands



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022



PROSPER ISD CHILDREN'S HEALTH STADIUM

E 1ST ST

LOOKING NORTHWEST



E 1ST ST

LOOKING SOUTHEAST

# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022



ROCK HILL HIGH SCHOOL

E 1ST ST

LOOKING SOUTHWEST



Main Entry



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Student Commons from Library



Student Commons from Cafeteria



# BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Main Corridor at East Academic Wing

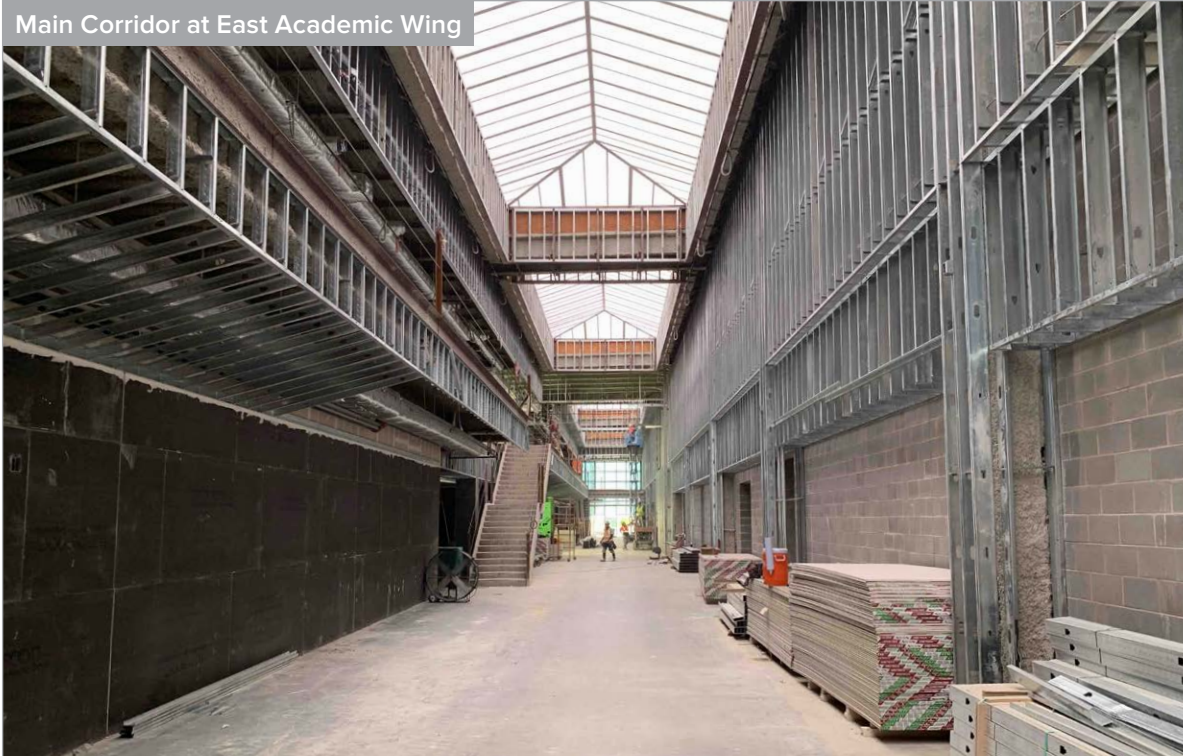

Entry Portal to Academic Corridor



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Ceramic Tile at East Academic Wing



Typical Academic Corridor

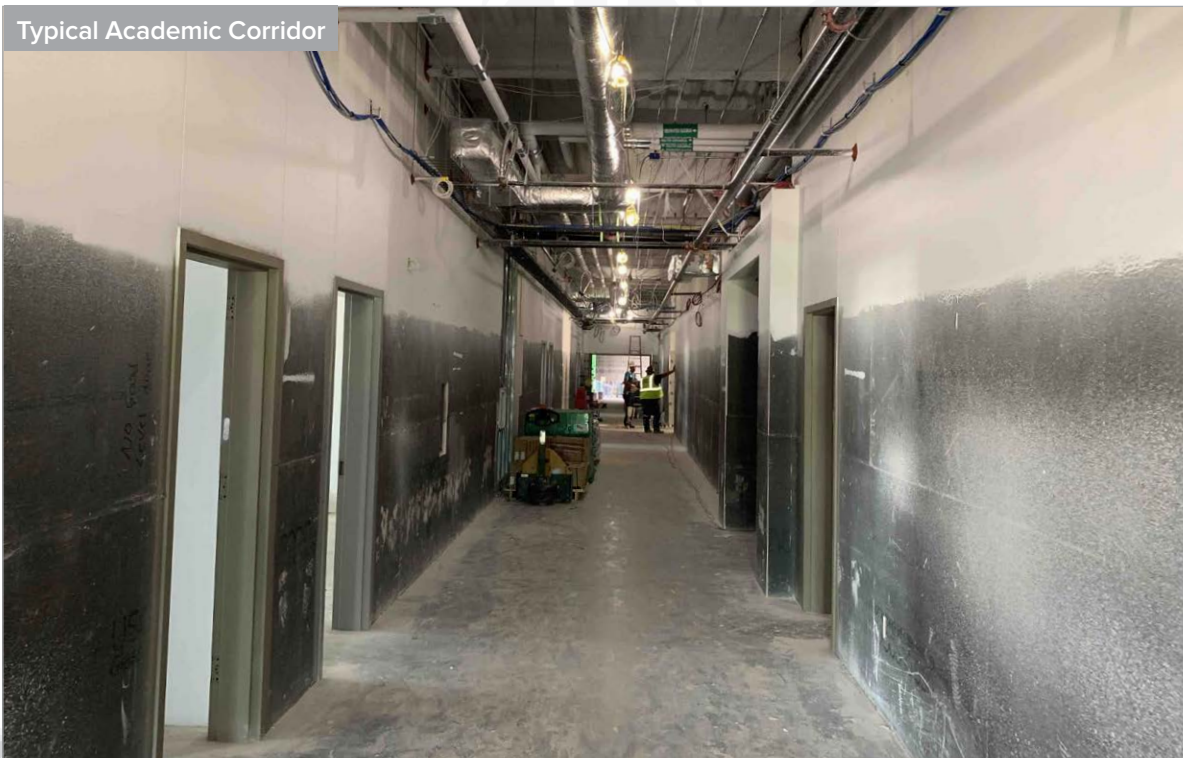

# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Courtyard at East Academic Wing



Exterior Masonry

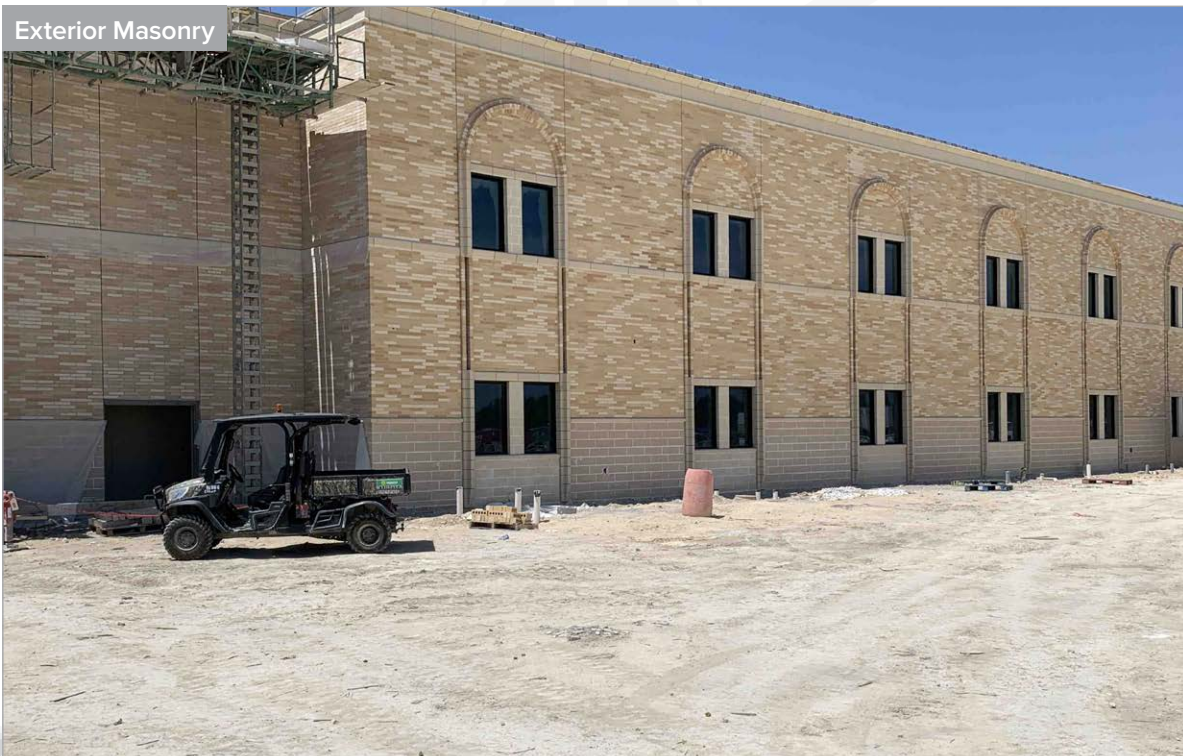

# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Auditorium Entry



Rear Entry



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Auxillary Gyms (Tornado Shelter)



Exterior Masonry at Multi-Purpose Facility Locker Rooms



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Interior Multi-Purpose Facility



Ticket Booth



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF AUGUST 2022

Drilling Irrigation Well

