



## BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



### WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF FEBRUARY 2023

#### WORK COMPLETED AND ONGOING:

##### Site

- Baseball and softball fields are ready for turf (March installation)
- Baseball and Softball bleacher seating foundations ongoing
- Detention pond turf planting to begin once subgrade has dried out
- Irrigation installation ongoing – north side of property
- Irrigation well holding tank to install in April
- Track excavation complete and installation of track & field components ongoing
- Football bleacher seating installation ongoing
- Final tennis court pour will be completed once subgrade has dried out

##### Building

- Steel erection complete – Areas A, B, C, D, E, F, G, J, K, L, M, N, P, Q, R, S, T, U and V
- Steel erection is ongoing – Area H
- Steel deck installation ongoing – Area J
- Precast seating installation complete – Area J
- Poured in place steps to begin on the precast risers once the weather allows
- MEP/Fire Sprinkler overhead ongoing – Areas F (2nd), G (2nd), J, T and V
- Framing ongoing – Areas G (2nd), K, L and N (entry)
- Plaster installation ongoing – Area J (high roof)
- Plaster ceilings ongoing – Area T (locker rooms)
- Painting ongoing – Areas D, E, M, N, T and U
- Interior CMU walls ongoing – Area J
- Roofing white cap ongoing – Areas P and R
- Terracotta tile roof installation ongoing – Area D
- Exterior waterproofing ongoing – Areas L and M
- Brick Veneer installation ongoing – Areas D, F, L and M

- Brick columns and arches are ongoing at the exterior – Area D
- Terracotta rain screen installation ongoing – Area C
- Interior storefront installation ongoing
- Fireproofing ongoing – Area J
- Fire alarm is ongoing – Areas D, E, F, M, T and U
- Low voltage rough-in ongoing – Areas D, E, F, M, Q, T and U
- Security and access control ongoing – Areas D, E, F, M, T and U
- Tile installation ongoing at 2nd floor – Areas A, B and C
- Carpet/LVT installation ongoing in A, B & C 1st and 2nd floors
- Display case framing installation in main corridor ongoing
- Wood wall and bench framing ongoing
- Millwork and science lab casework installation ongoing
- Colling door installation ongoing – Areas L and M
- Handrail installation ongoing – Areas D and N
- Courtyard has been graded and forming of flat work is ongoing
- Canopy installation of framing ongoing – Area C
- RTU installation has been completed up to – Areas H and J
- RTU's have been turned on for roughly half of the building

##### Multipurpose Facility (MPF) and Ancillary Buildings

- Masonry in Area V is ongoing nearing complete with CMU walls
- Masonry skin installation ongoing at Area U, V

# Construction Update - Walnut Grove High School #3



**LOOKING SOUTHEAST**  
Walnut Grove High School



**LOOKING SOUTH**  
Walnut Grove High School

Granite Shoal Drive





## BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



### LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF FEBRUARY 2023

#### WORK COMPLETED AND ONGOING:

##### Site

- Poured out concrete for retaining wall
- Poured all light pole bases on-site, except one
- Basketball court concrete complete
- Gas meter installation complete
- Sidewalks – 20% complete
- Dumpster area grade beams complete

##### Building – Area 1:

- Framing – 30% complete
- Electrical overhead – 30% complete (inspection pending)
- Ductwork – 70% complete
- Fire sprinkler rough-in – 70% complete
- Exterior brick/stone ongoing – 70 % complete
- Ceramic tile – 10% complete

##### Building – Area 2:

- Framing complete
- Electrical overhead complete
- Plumbing overhead complete
- Ductwork complete
- Drywall – 70% complete
- Exterior brick/stone ongoing – 70 % complete
- Roof dry in complete
- Ceramic tile – 75% complete

##### Building – Area 3:

- Framing complete
- Electrical overhead complete
- Electrical wall rough-in complete
- Plumbing overhead complete
- Plumbing wall rough-in complete
- Drywall complete
- Ductwork complete
- Exterior brick/stone – 95% complete
- Roof dry in complete
- Ceramic tile / flooring – 80% complete
- Tape and Bed – 50% complete

##### Building – Area 4:

- Ceramic tile / flooring – 70% complete
- CMU block in storm shelter - 25% complete
- Drywall complete
- Roofing membrane installation ongoing
- Tower CMU block complete
- Steel erection complete
- Tape and bed – 70% complete

# Construction Update - Lilyana Elementary School #16





## BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



### DAN CHRISTIE ELEMENTARY SCHOOL (ES#17)

AS OF FEBRUARY 2023

#### WORK COMPLETED AND ONGOING:

##### Site

- Concrete Inlets are ongoing
- Paving complete – Areas 3 and 4
- Southwest approach pour complete
- Electrical rough-in for pole lighting on west side waiting on inspection

##### Building

- ICF Walls complete – Area 3
- ICF walls ongoing – Areas 1 and 2
- Electrical rough-in ongoing – Area 4
- Plumbing rough-in ongoing – Area 4
- CMU walls ongoing
- Metal stud framing ongoing
- Structural steel and decking complete – Area 4
- Clerestory ongoing – Area 4
- Structural steel ongoing – Area 3 (east side)

# Construction Update - Dan Christie Elementary School #17





## BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



### BRENDA CALHOUN EARLY CHILDHOOD SCHOOL

AS OF FEBRUARY 2023

#### WORK COMPLETED AND ONGOING:


##### Site

- Irrigation and sod on east side of site
- Light pole bases and sign foundations
- Dumpster pad concrete

##### Building

- Structural steel is complete with the exception of the northwest exterior building canopy
- Exterior sheathing is substantially complete
- Masonry – Areas A, B and C
- Built-up roofing – Area D; last area for roofing
- Two-siding of gypsum board – Area C
- Window frames – Area C
- Interior wall framing – Area D; last area for interior studs
- MEP overhead and wall rough-in – Area D
- Tape, bed, and paint – Area A

# Construction Update - Brenda Calhoun Early Childhood School

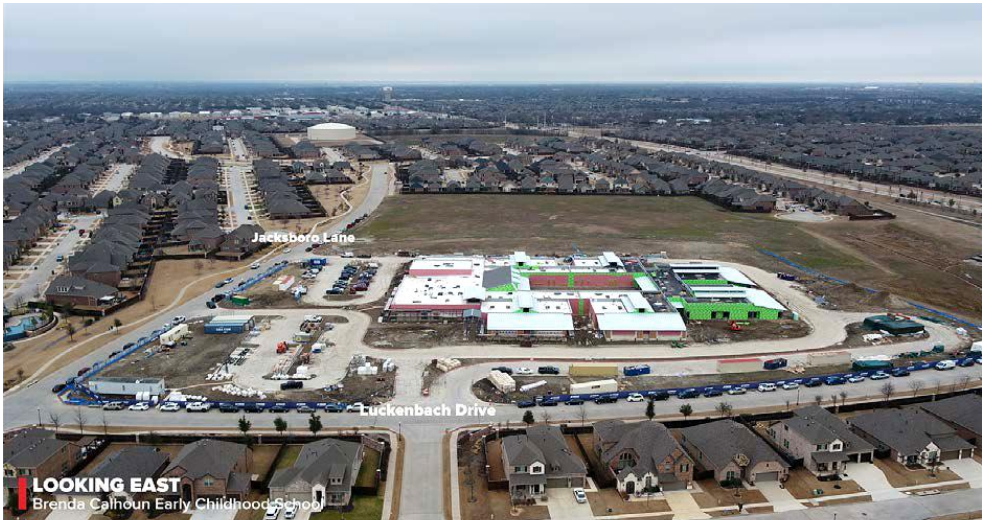





## BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



### DANIEL L. JONES MIDDLE SCHOOL (MS #5)

AS OF FEBRUARY 2023

#### WORK COMPLETED AND ONGOING:

##### Permits

- All permits have been approved and issued
- Currently no work is to be done within the Atmos Easement

##### Pre-Construction Meetings

- City Civil and City Building Pre-Con's – Complete
- Foundation – Complete
- Quality Control – Complete
- Utilities – Complete

##### Site

- Site grading is ongoing
- Building pad grading is complete
- Utilities to begin week of February 6 (weather permitting)
- Piers ongoing – Area 7; Pier drilling will resume once the weather allows
- Chemical injection to begin February 6 (weather permitting) and follow behind the pier drilling for each area

# Construction Update - Daniel L. Jones Middle School

