

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



AS OF APRIL 2024

BETTY JACKSON ELEMENTARY SCHOOL (ES #18)

WORK COMPLETED AND ONGOING:

Site

- Alvira Drive and Cassidy Street paving ongoing
- Irrigation complete
- Site paving complete
- Playground construction ongoing
- Landscape installation ongoing

Building

- Brick veneer complete
- Wall and floor tile installation ongoing
- Millwork ongoing – Areas 1 and 2
- Painting ongoing – All Areas
- Light fixture installation ongoing
- Toilet partition installation ongoing
- Main corridor interior brick ongoing
- MEP overhead inspections ready



BETTY JACKSON ELEMENTARY SCHOOL (ES #18)



AS OF APRIL 2024



LOOKING EAST
Betty Jackson Elementary School



LOOKING SOUTH
Betty Jackson Elementary School

BETTY JACKSON ELEMENTARY SCHOOL (ES #18)



AS OF APRIL 2024



LOOKING WEST
Betty Jackson Elementary School



MAIN ENTRY


BETTY JACKSON ELEMENTARY SCHOOL (ES #18)



AS OF APRIL 2024



MAIN ENTRY CORRIDOR

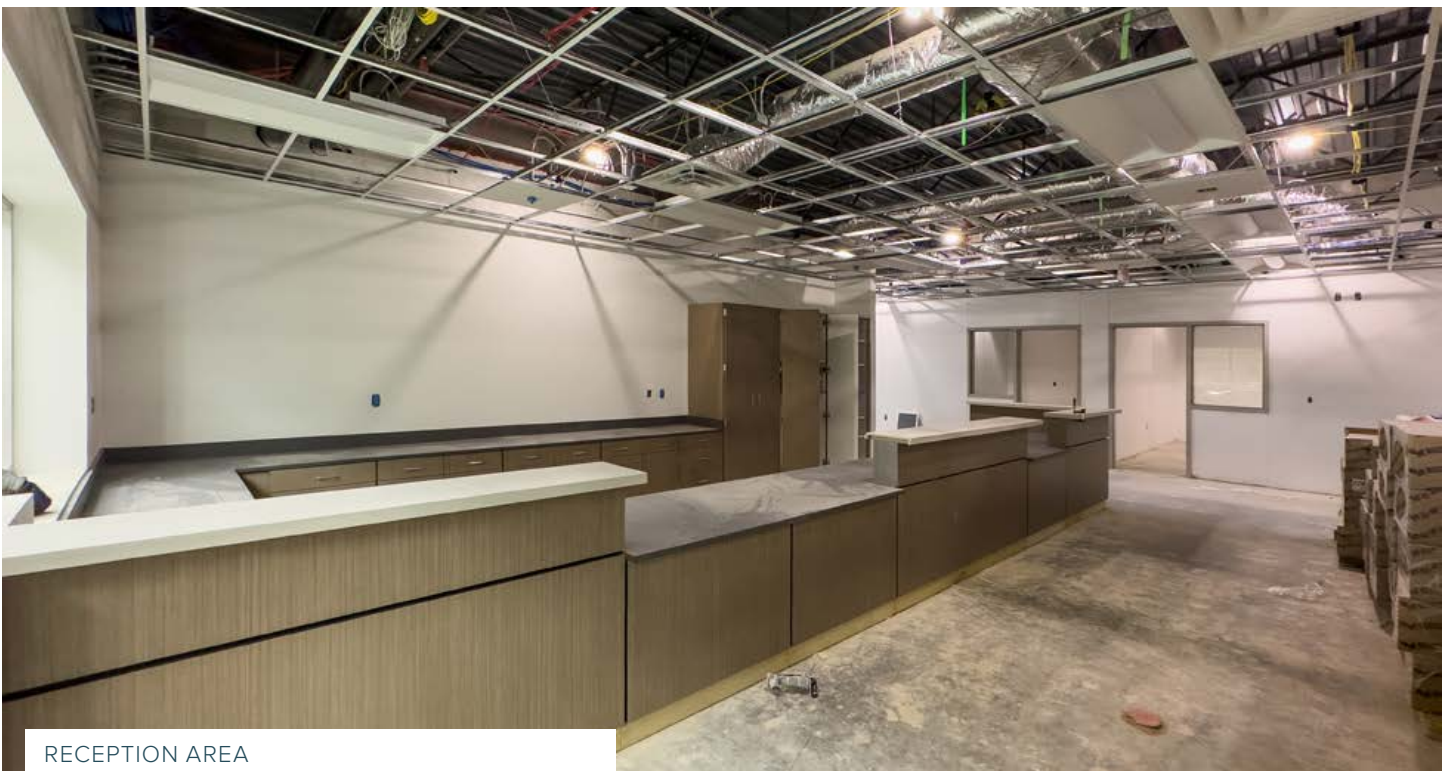

RECEPTION AREA

BETTY JACKSON ELEMENTARY SCHOOL (ES #18)



AS OF APRIL 2024



ACADEMIC CORRIDOR




CLASSROOM


BETTY JACKSON ELEMENTARY SCHOOL (ES #18)



AS OF APRIL 2024

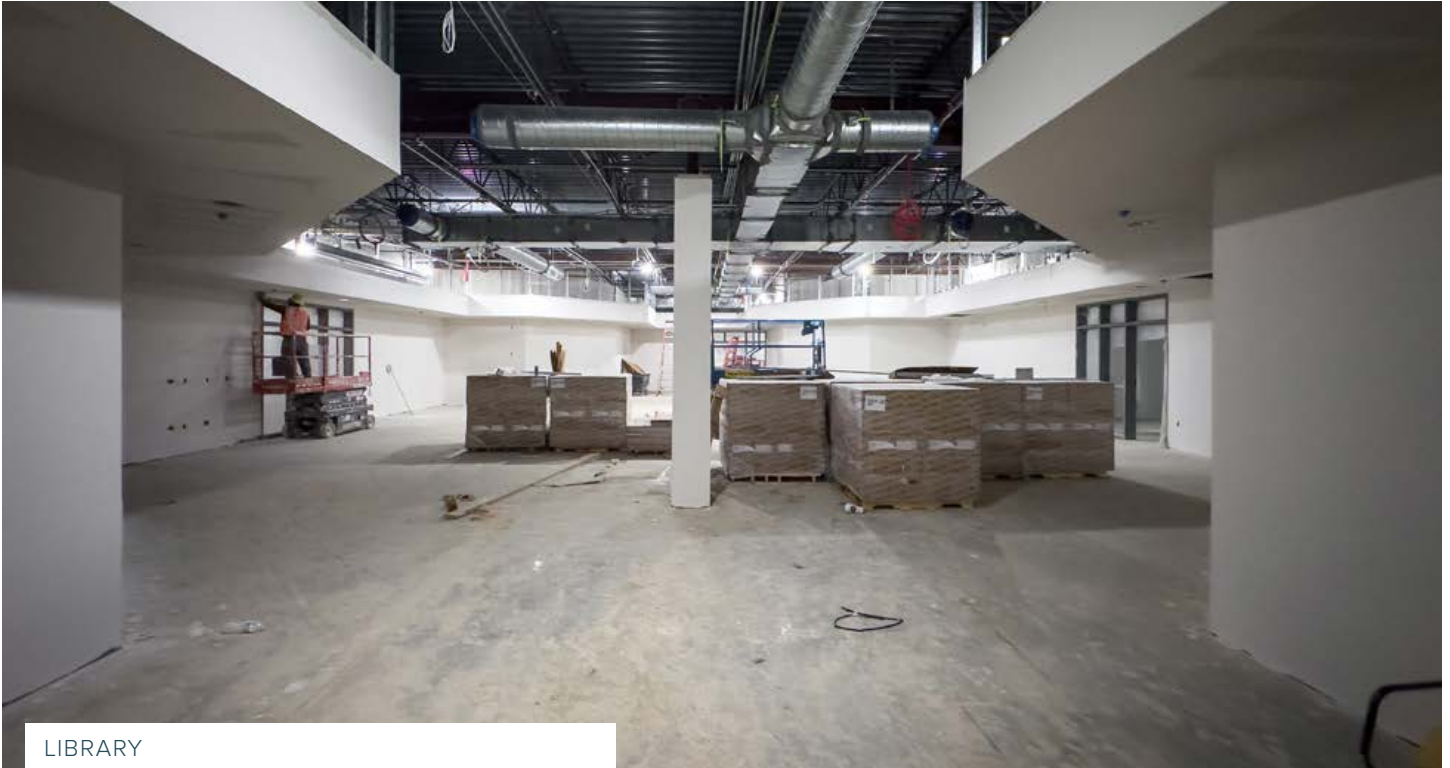

LIBRARY

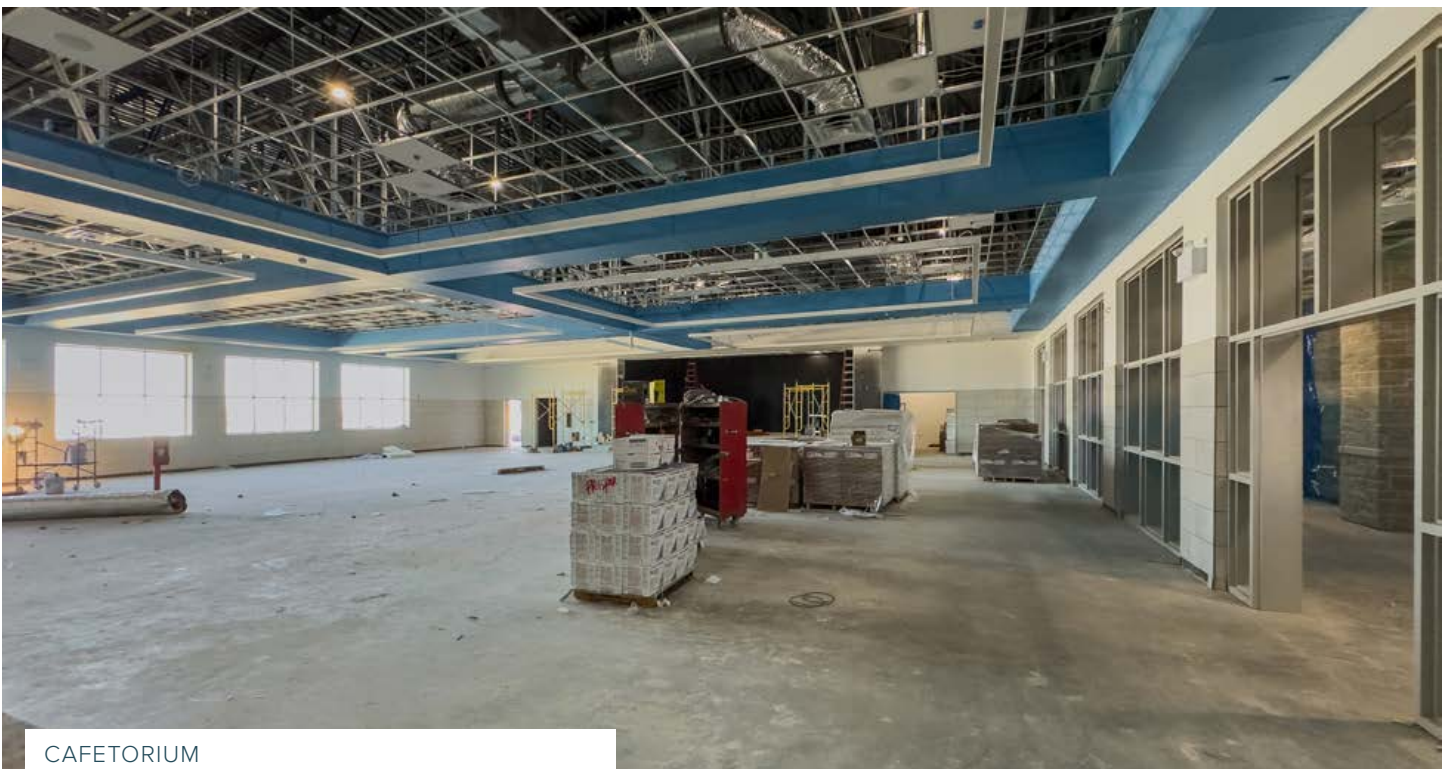

CAFETERIUM


BETTY JACKSON ELEMENTARY SCHOOL (ES #18)



AS OF APRIL 2024



KITCHEN

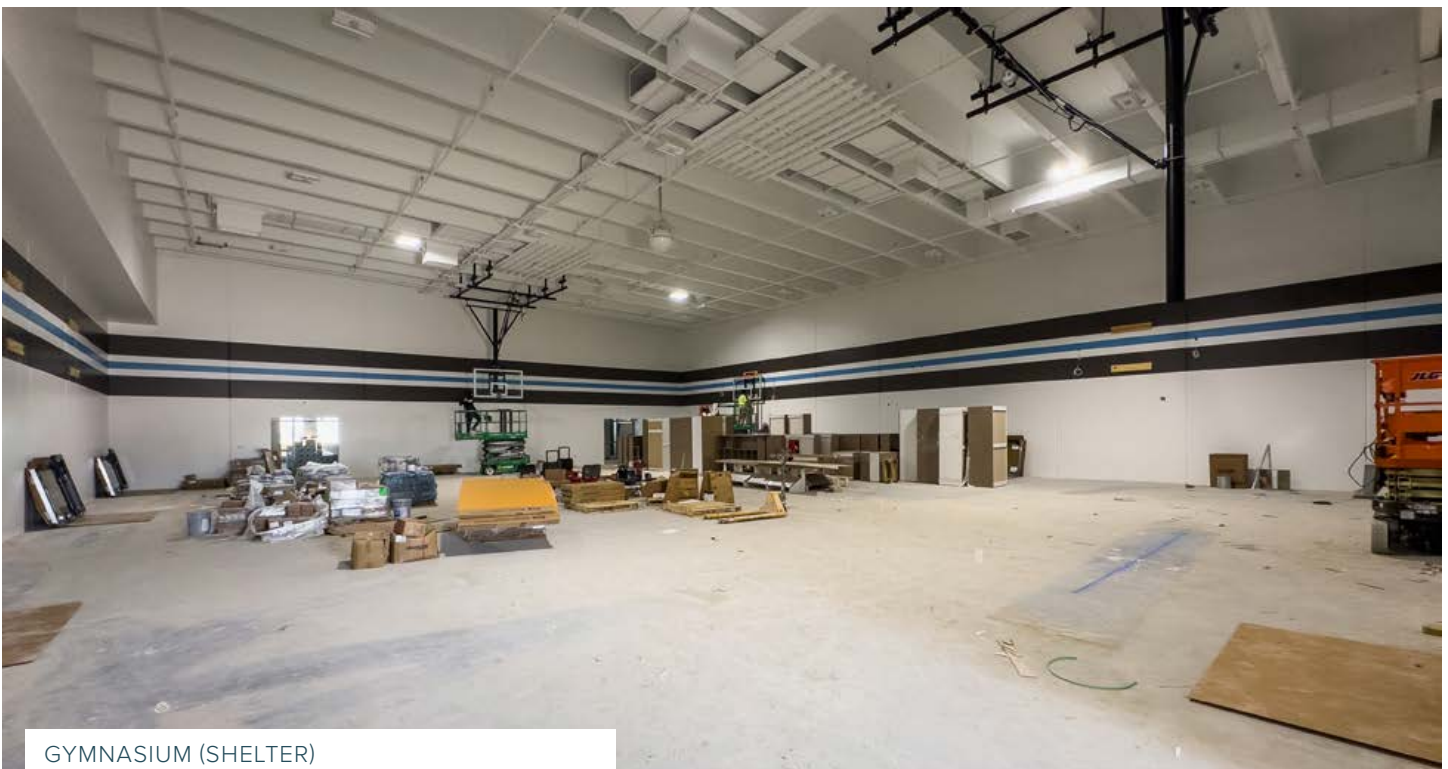

GYMNASIUM (SHELTER)

BETTY JACKSON ELEMENTARY SCHOOL (ES #18)



AS OF APRIL 2024



PLAYGROUND AREA



REAR ENTRY

BETTY JACKSON
ELEMENTARY SCHOOL
(ES #18)



AS OF APRIL 2024



HARDCOURT AREA



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT

AS OF APRIL 2024

DANIEL L. JONES MIDDLE SCHOOL (MS #5)

WORK COMPLETED AND ONGOING:


Site

- Track and field flatwork complete
- Football field and track installation ongoing
- Tennis courts awaiting surface installation
- Final grading and topsoil installation ongoing
- Irrigation installation ongoing
- Decorative metal fence installation ongoing
- Irrigation tank installation ongoing

Building

- Exterior veneer work is ongoing, moving to Area 8
- Storefront installation complete
- MEP and Technology punch list corrections ongoing – Areas 5-7

- Permanent gas and electric hookups complete
- Roof-top unit (RTU) start-up ongoing – All Areas
- Interior wall framing and two-siding complete – Area 8
- Tape, bed, texture, and paint ongoing – Area 8
- Tile installation ongoing in multi-user restrooms and academic corridors
- Classroom carpet installation ongoing
- Classroom millwork installation ongoing
- Science lab casework installation complete
- Tornado shelter finishes ongoing
- Roofing installation ongoing – Area 8
- Wood floor installation ongoing – both gymnasiums
- Resinous floor installation in locker rooms ongoing

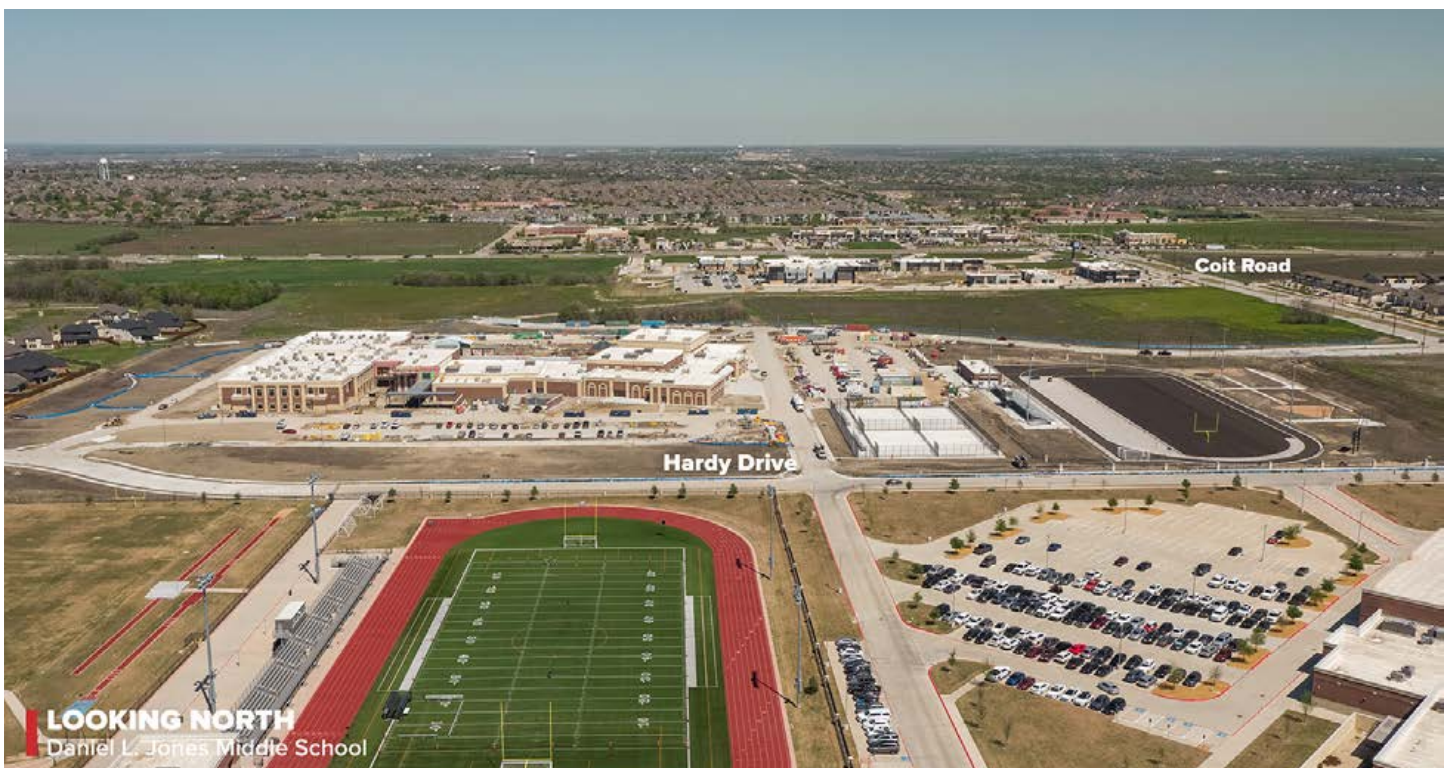

DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024



DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024



LOOKING WEST
Daniel L. Jones Middle School




MAIN ENTRY


DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024

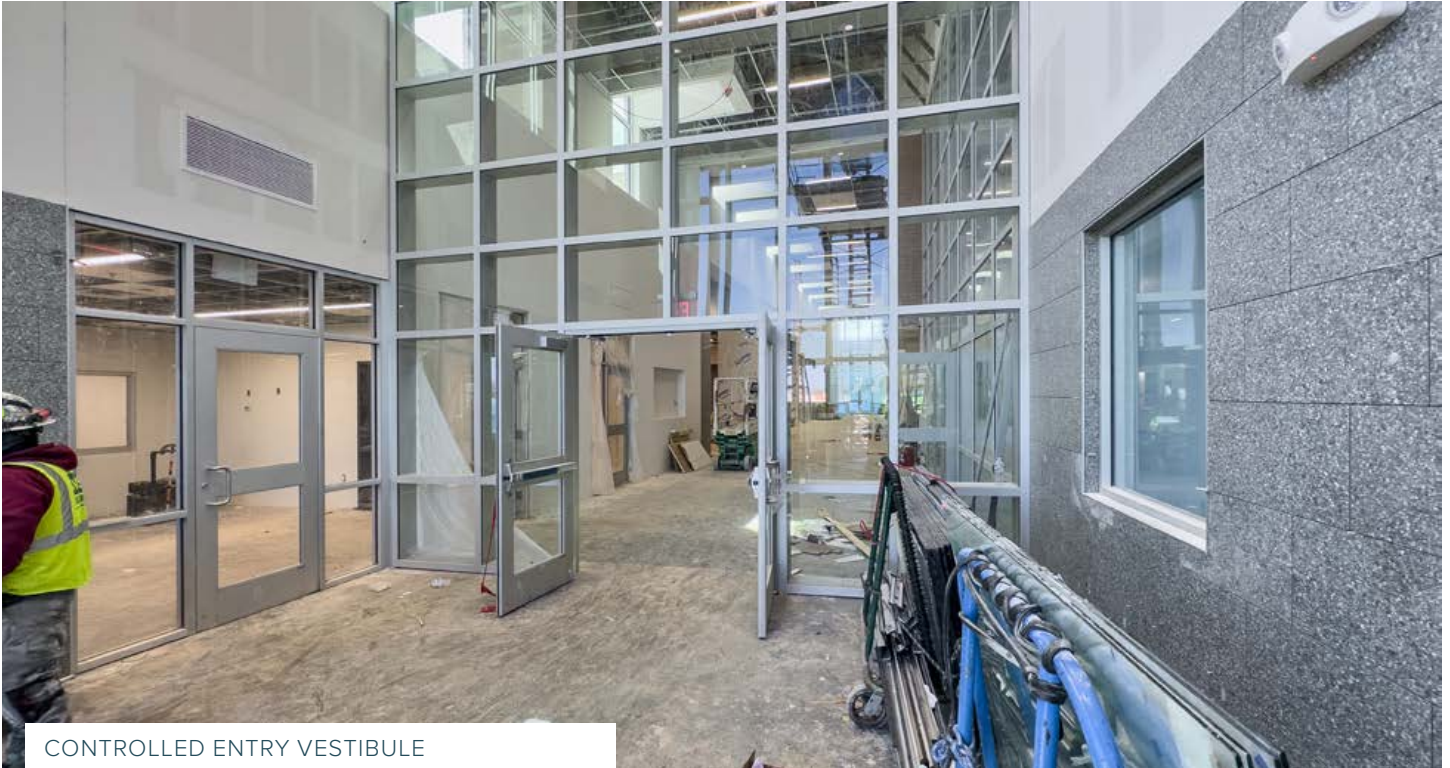

CONTROLLED ENTRY VESTIBULE

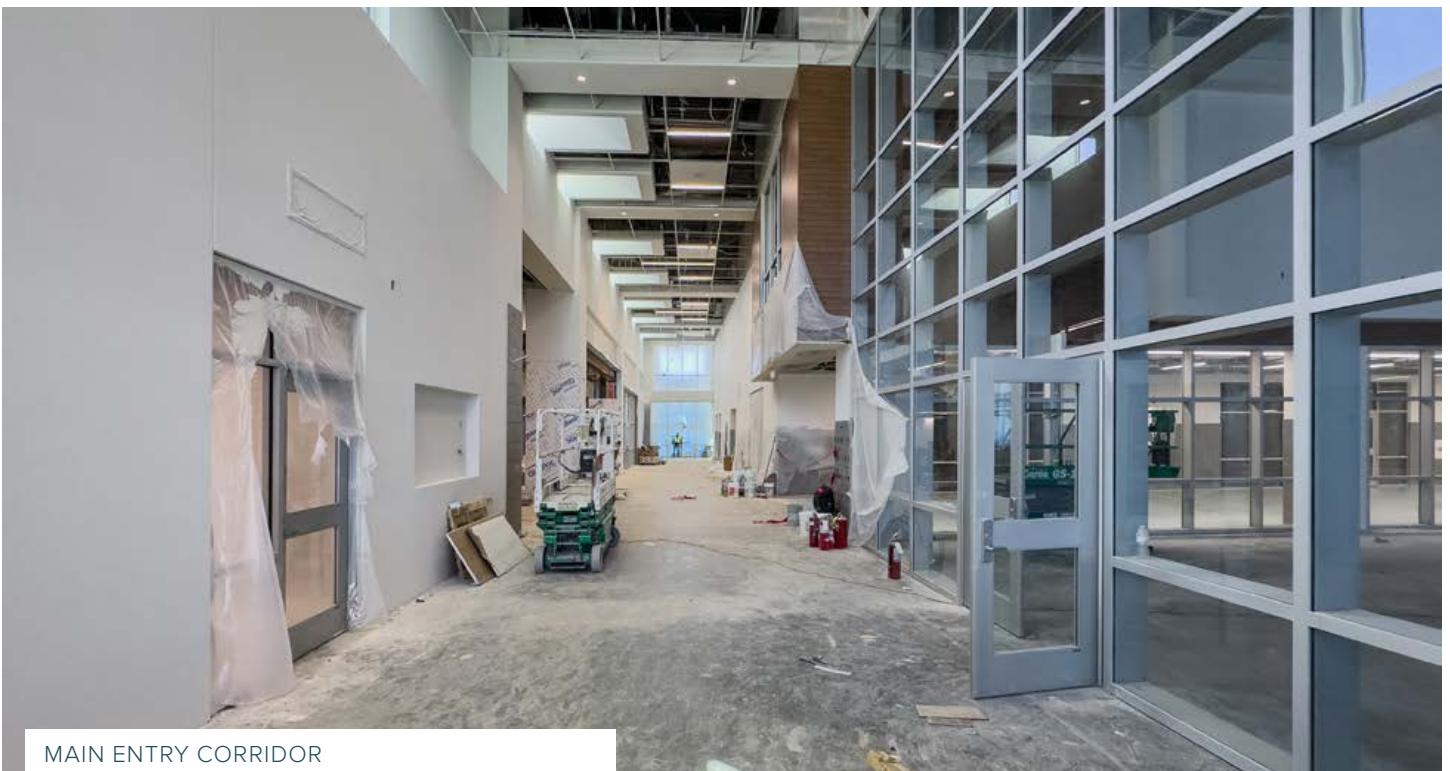

MAIN ENTRY CORRIDOR


DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024



LIBRARY

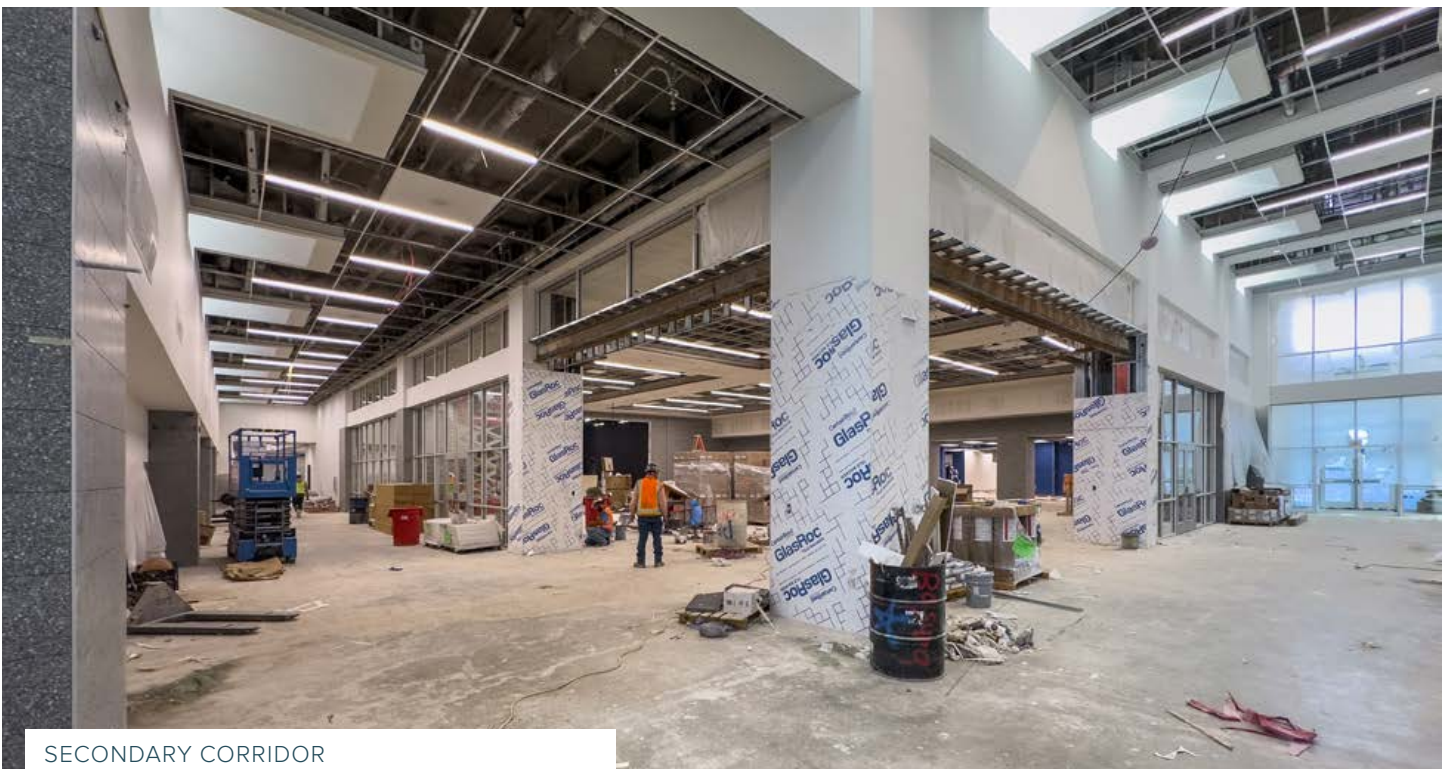


SECONDARY CORRIDOR


DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024

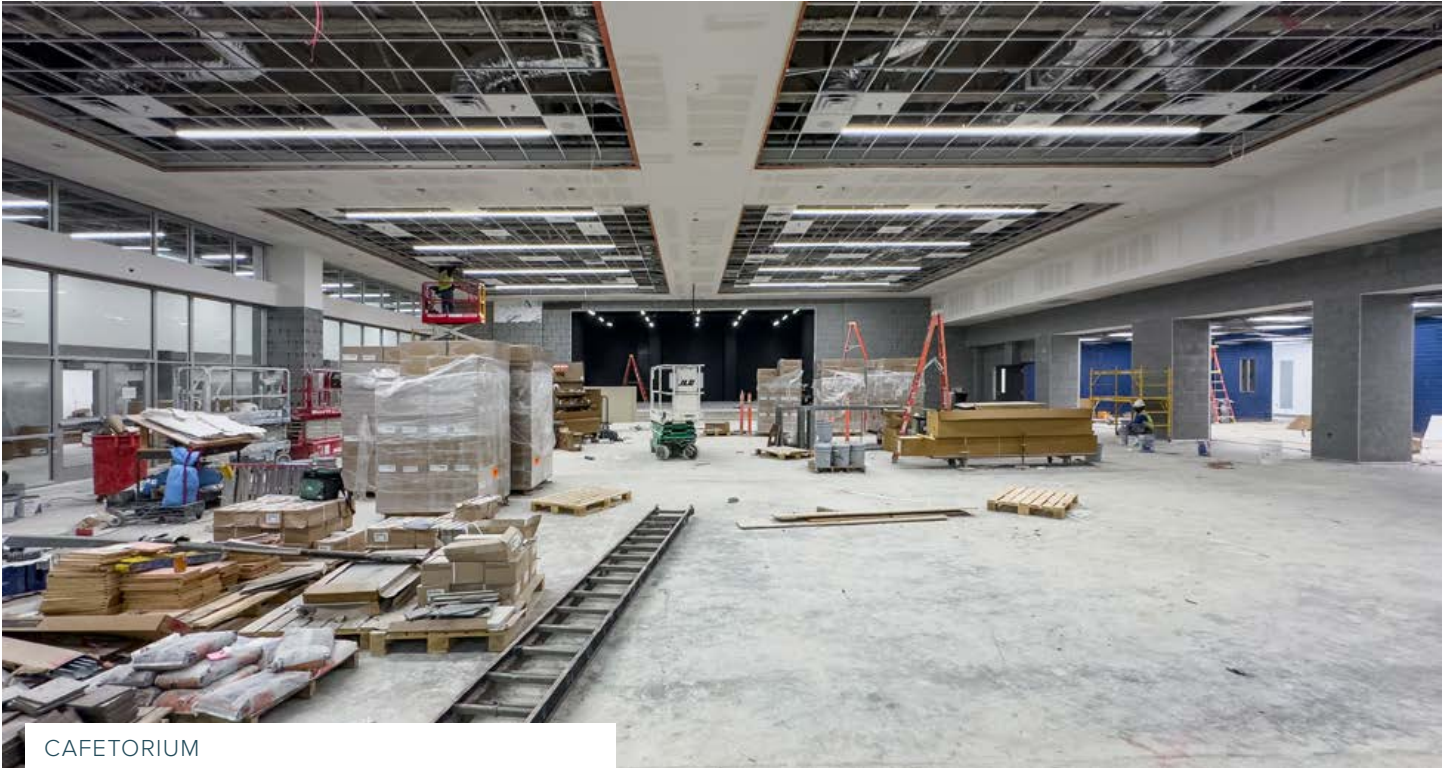

CAFETORIUM

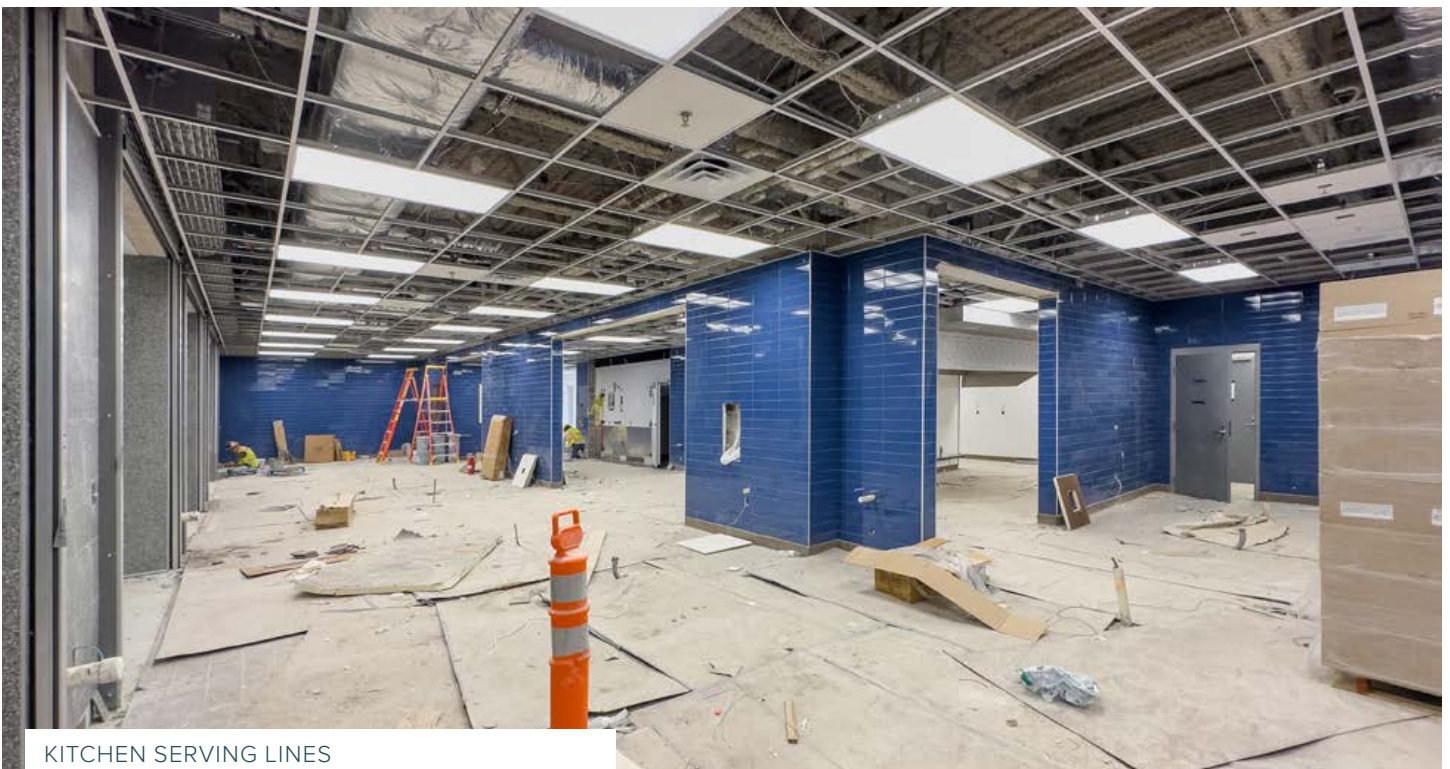


KITCHEN SERVING LINES

DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024

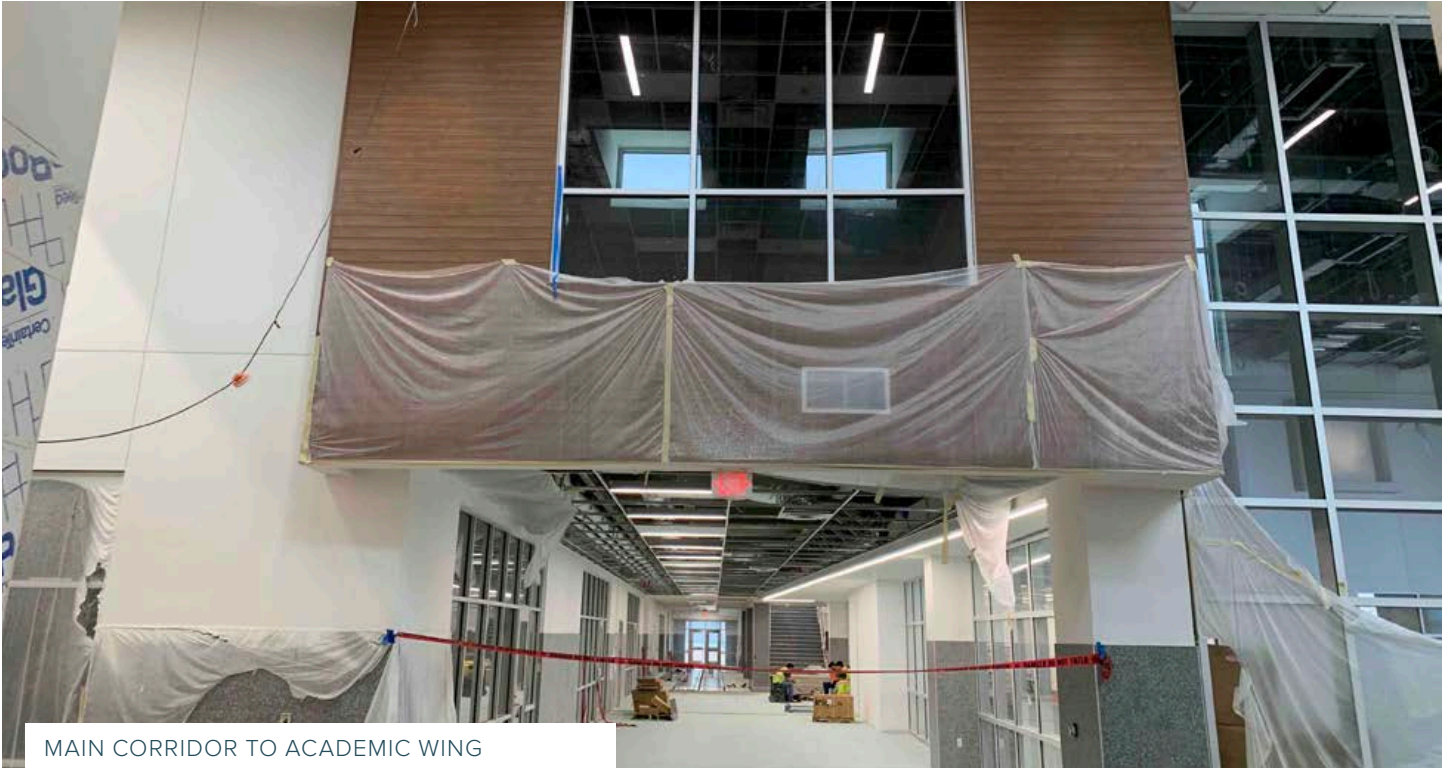

MAIN CORRIDOR TO ACADEMIC WING



STUDENT COMMONS


DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024



CLASSROOM

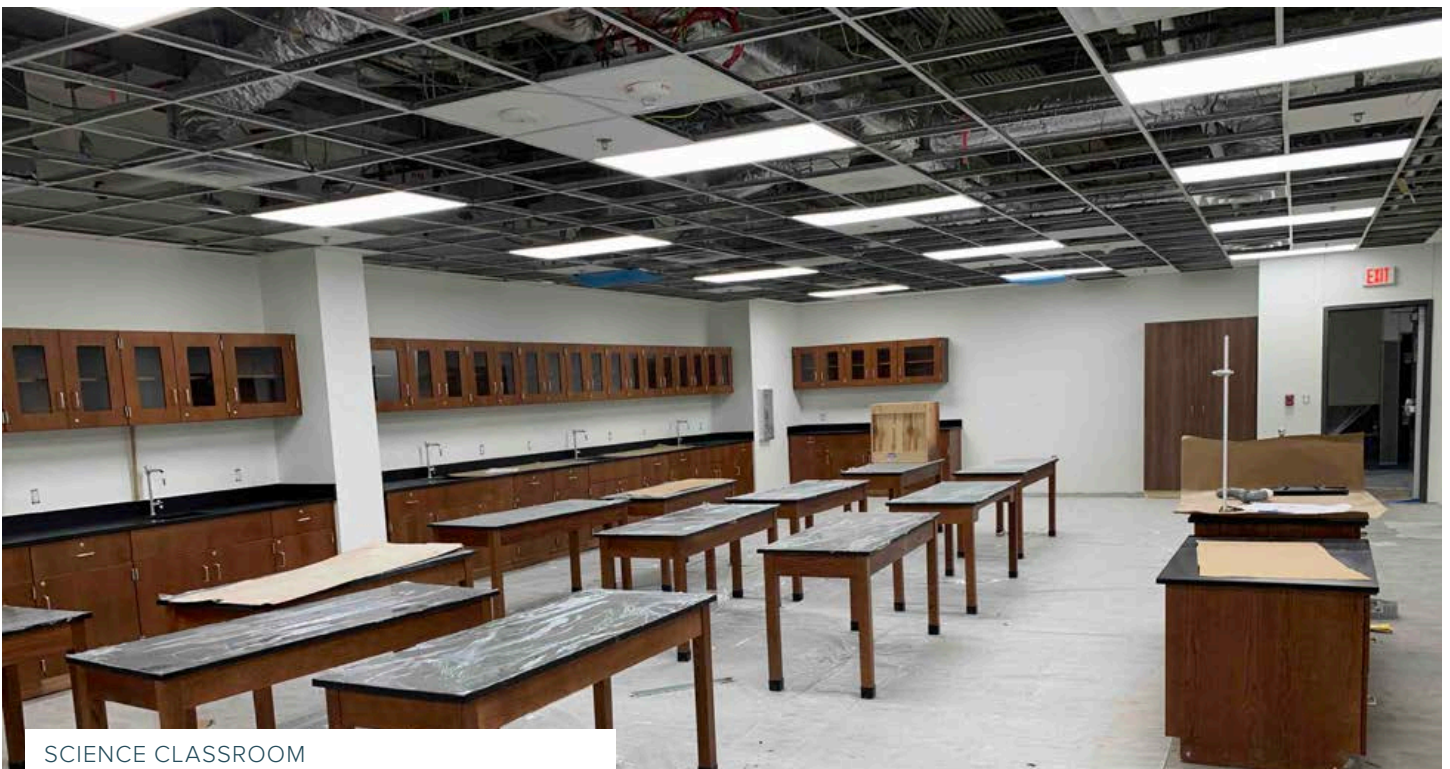


SCIENCE CLASSROOM

DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024

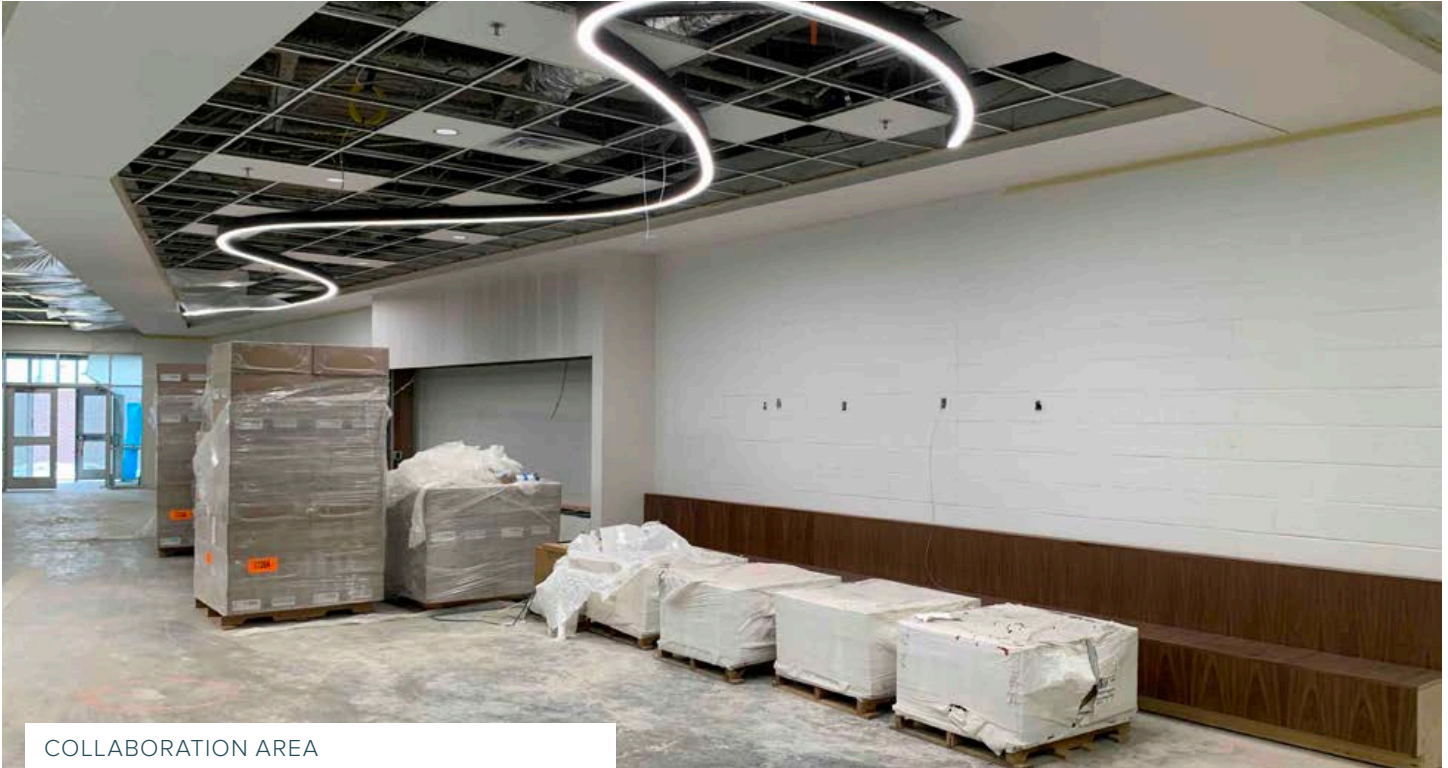

COLLABORATION AREA



ACADEMIC WING


DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024



GYMNASIUM ENTRY

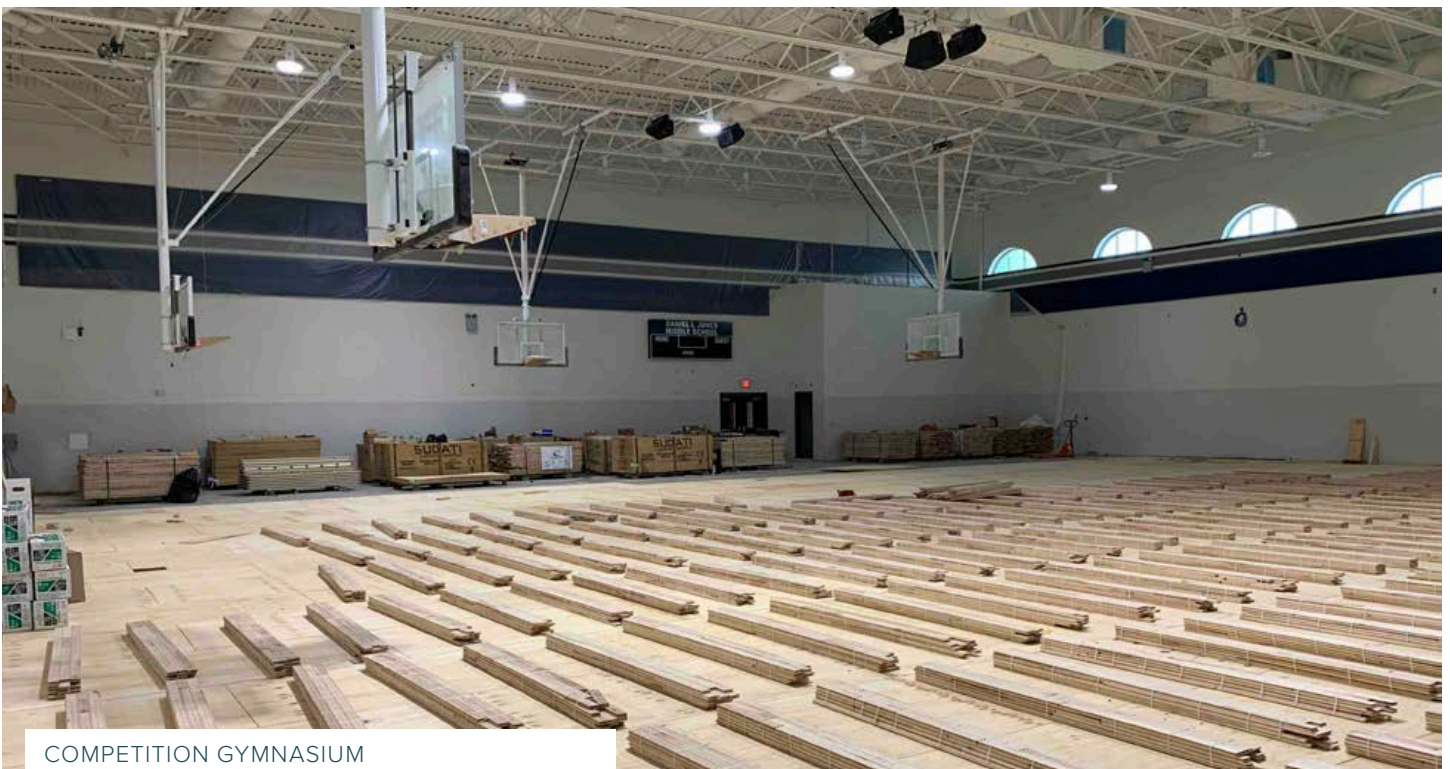


COMPETITION GYMNASIUM


DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024

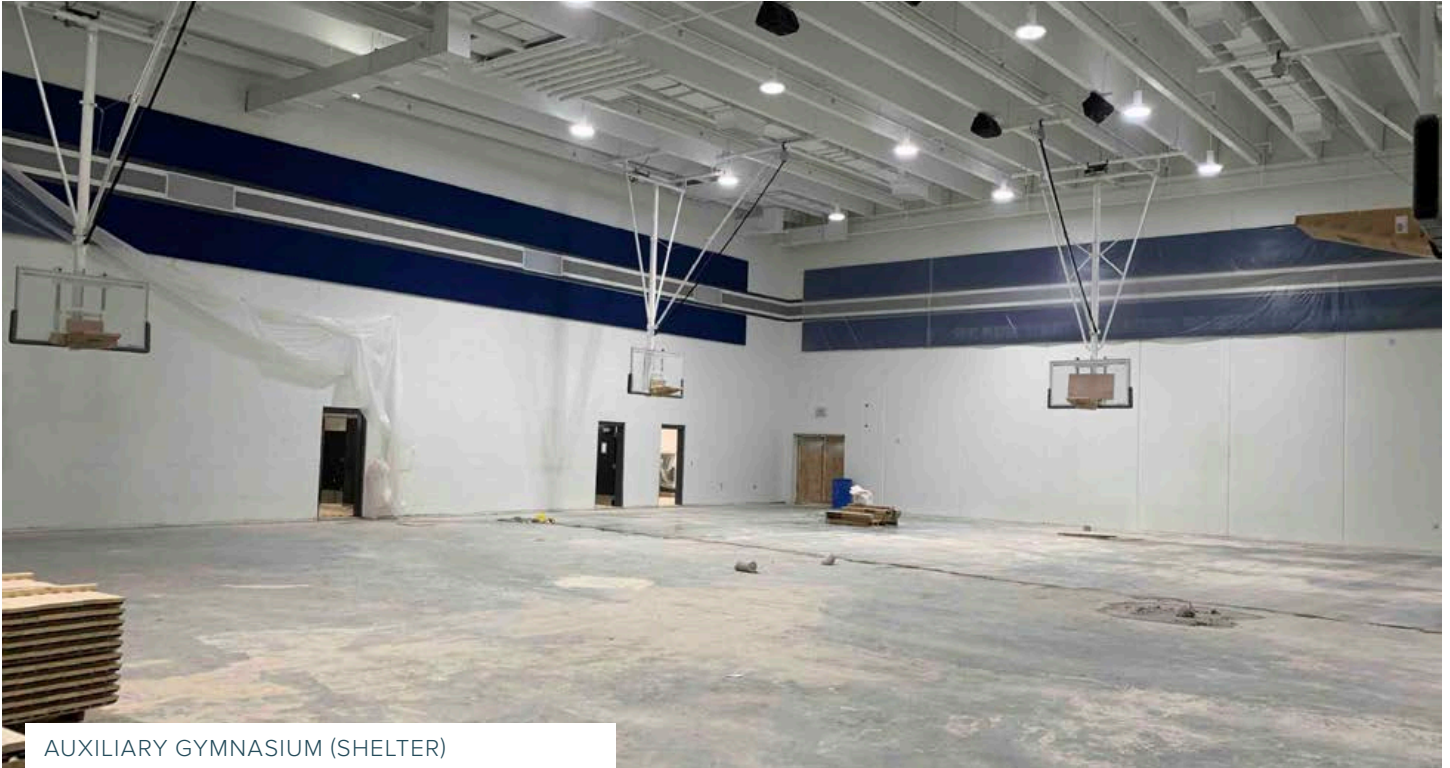

AUXILIARY GYMNASIUM (SHELTER)

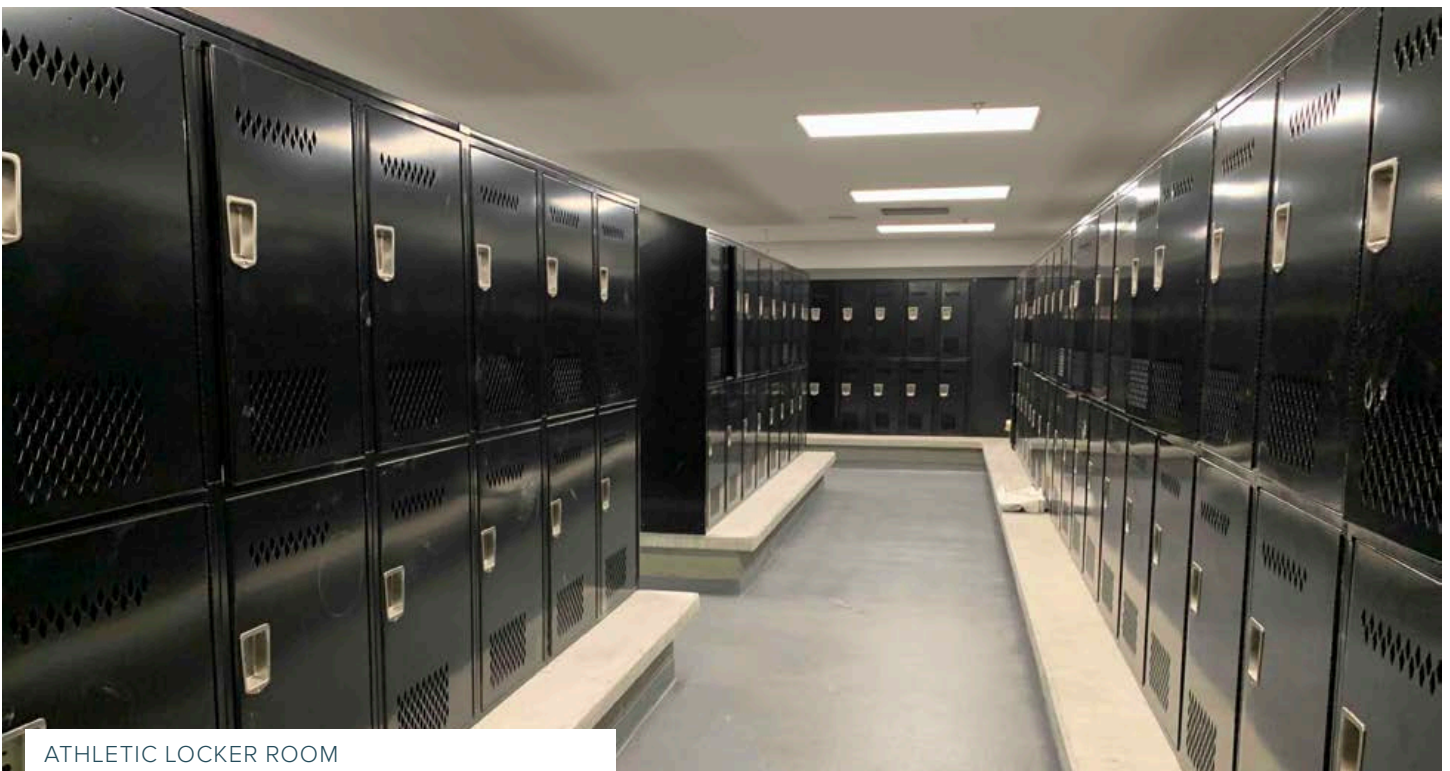

ATHLETIC LOCKER ROOM

DANIEL L. JONES MIDDLE SCHOOL (MS #5)



AS OF APRIL 2024



BUS DROP-OFF/PICK-UP CANOPY



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT

AS OF APRIL 2024

W. H. MOSELEY MIDDLE SCHOOL (MS #6)

WORK COMPLETED AND ONGOING:

Site

- Irrigation well testing ongoing
- Track asphalt installation ongoing
- Masonry at concession stand ongoing
- Fencing at tennis courts ongoing
- Site lighting pole installation ongoing
- Prepping to pour bleacher slab

Building

- CMU to be substantially complete by end of April
- Exterior masonry installation ongoing
- Second floor slab on deck prep ongoing – Areas 10 and 11
- Structural steel and metal decking erection ongoing
- Exterior CFMF and sheathing installation ongoing
- Roofing installation ongoing
- Fireproofing installation ongoing
- Interior framing and gyp board installation ongoing
- MEP overhead and rough-in ongoing
- Tape, bed, texture, and paint ongoing



**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



LOOKING WEST
W. H. Moseley Middle School



MAIN ENTRY


**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



LIBRARY ACADEMIC WING

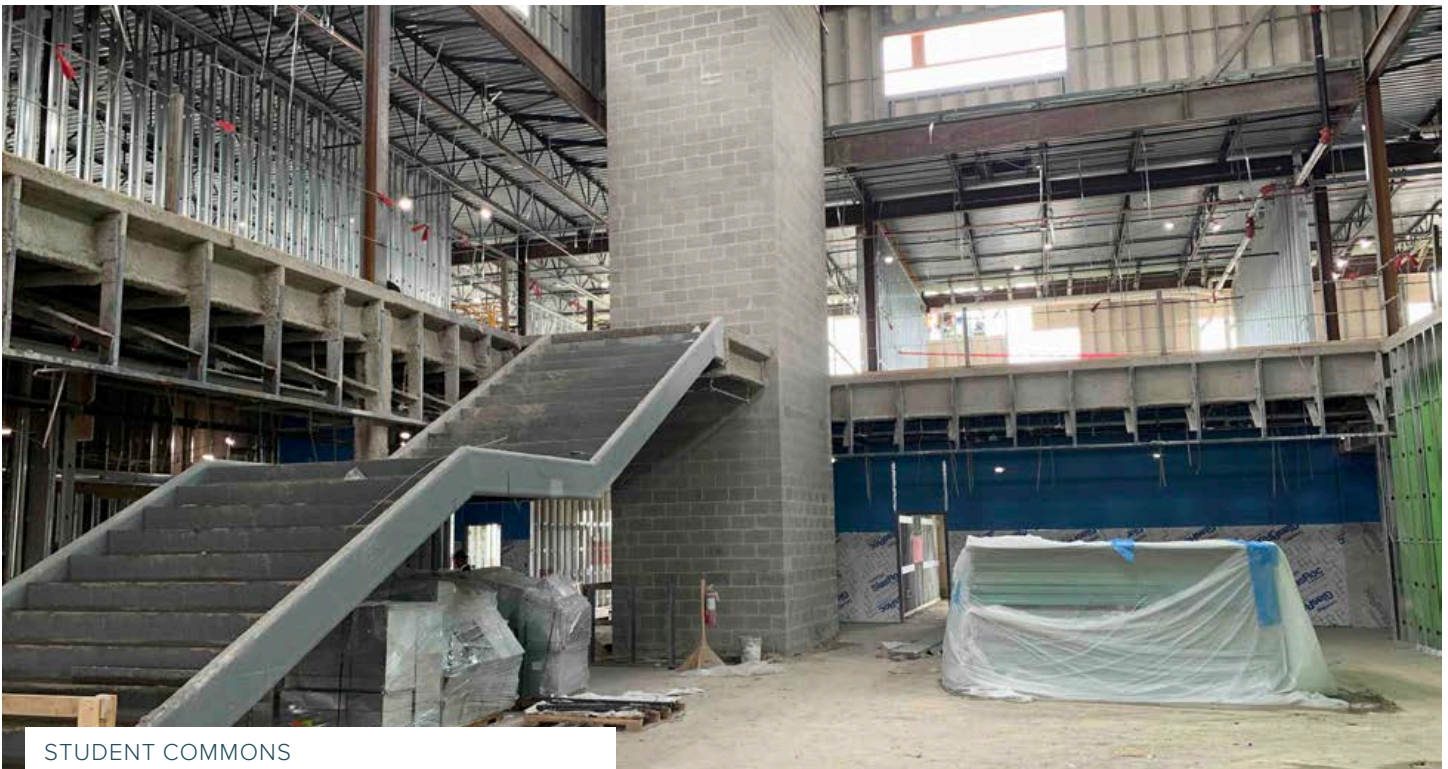


STUDENT COMMONS


**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024

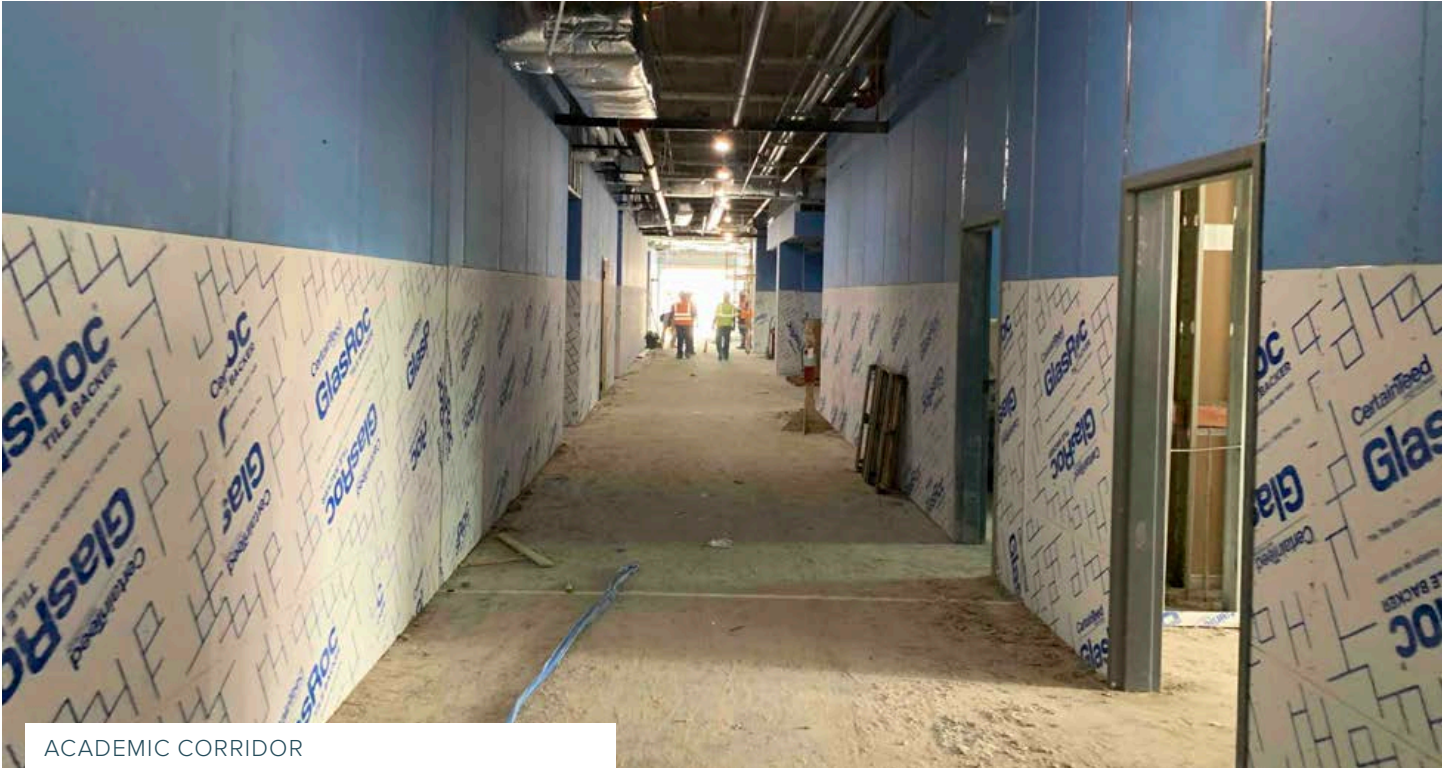

ACADEMIC CORRIDOR

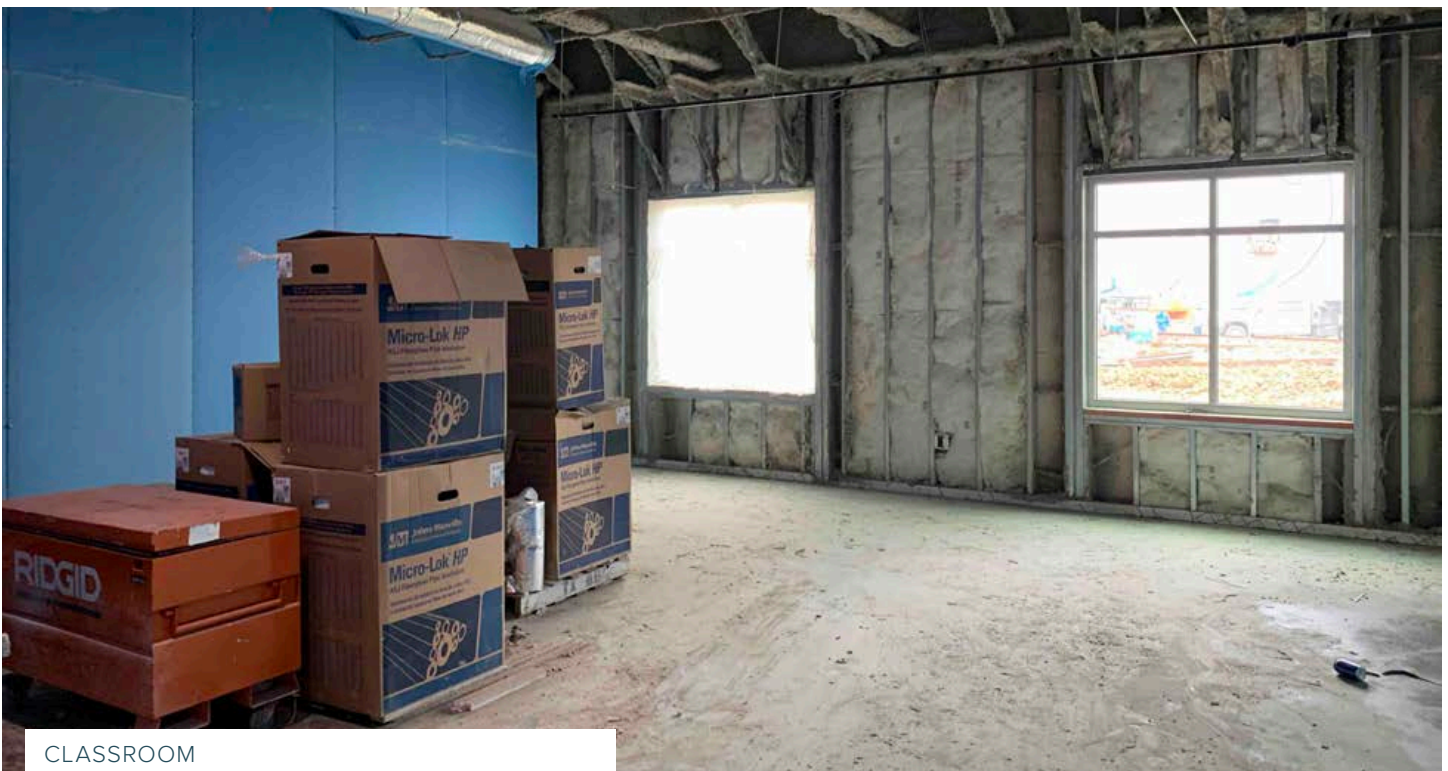

CLASSROOM


**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



COMPETITION GYMNASIUM

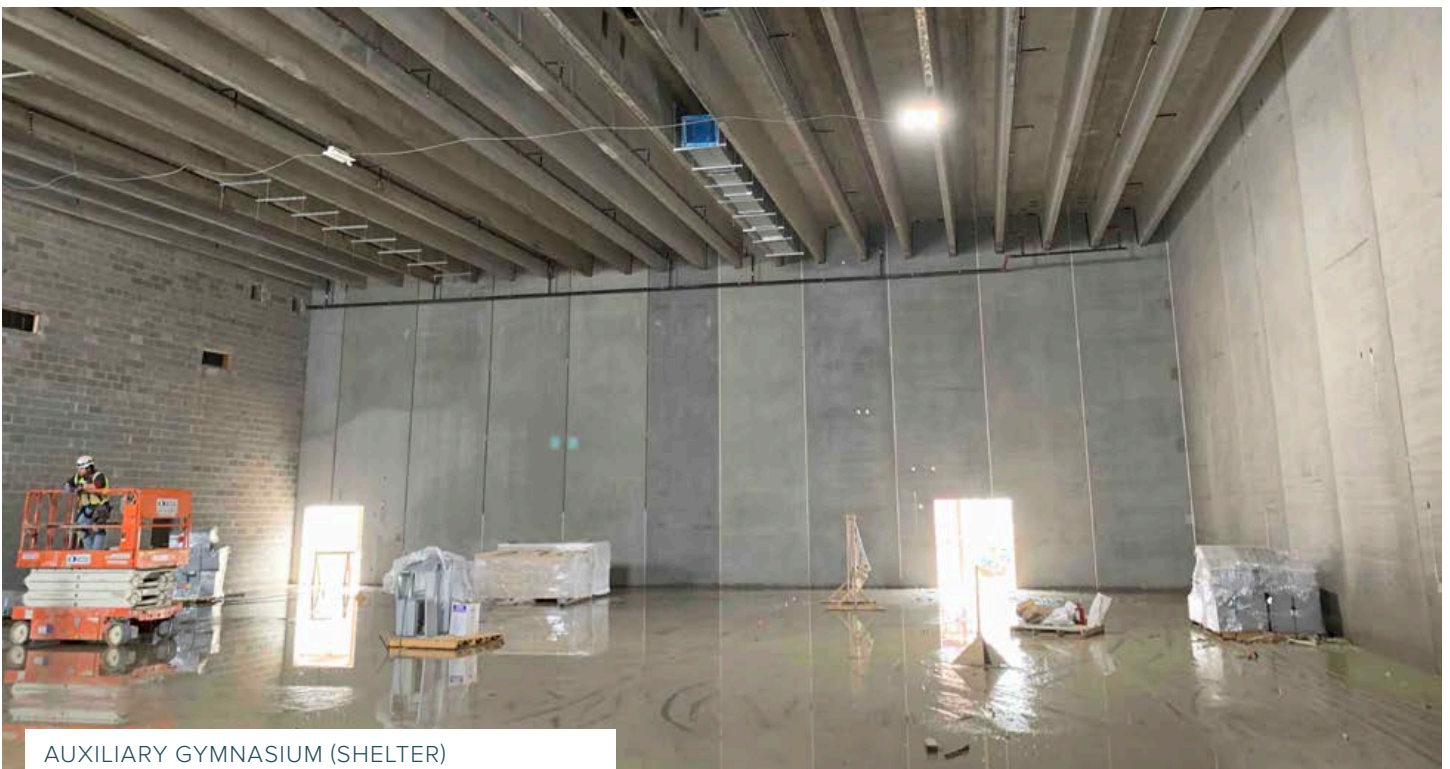

AUXILIARY GYMNASIUM (SHELTER)

**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



WEIGHT ROOM



BAND HALL

**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



GYMNASIUM ENTRY



COMPETITION GYMNASIUM

**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



WEIGHT ROOM



REAR ENTRY

**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024



CONCESSION RESTROOM BUILDING




STADIUM FLATWORK REINFORCING

**W. H. MOSELEY
MIDDLE SCHOOL
(MS #6)**



AS OF APRIL 2024

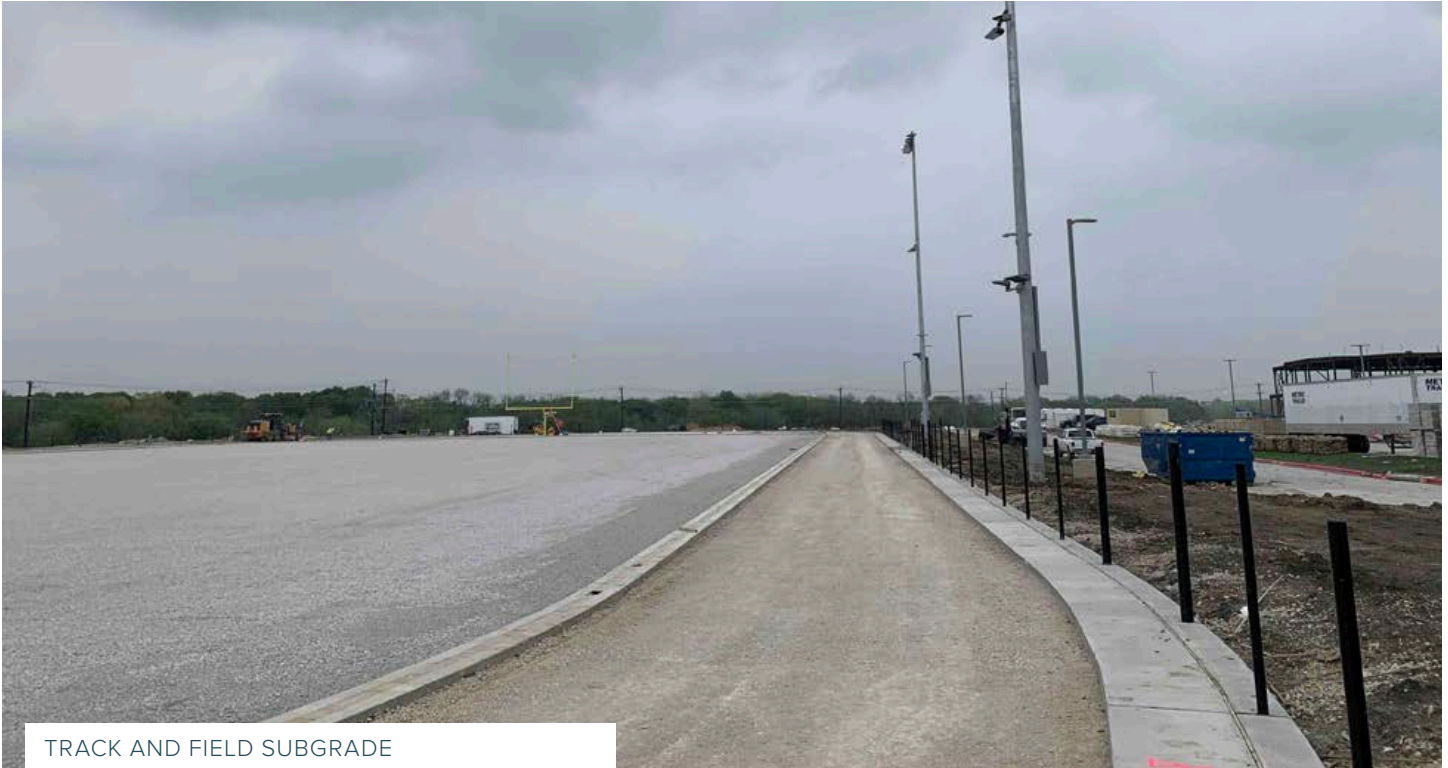

TRACK AND FIELD SUBGRADE



TENNIS COURTS



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT

AS OF APRIL 2024

RICHLAND HIGH SCHOOL (HS #4)

WORK COMPLETED AND ONGOING:

Site

- Plumbing at Multipurpose Facility (MPF) building complete – Area T; Area V was inspected on 3/27/2024
- Fire lane 17 poured 3/29/2024; fire lane 12 limed and blue topped
- Utilities at Prairie Drive are complete; moisture conditioning ongoing
- Parking lots 3 and 6 complete; blue topping parking lot 5 complete
- Parking lot 7 lime complete
- Tennis court foundations ongoing
- Moisture conditioning at football field ongoing
- Underground MEP at the concession stands and dugouts ongoing
- Footings for baseball and softball backstop walls complete; forming of walls ongoing
- All main water lines on site have been chlorinated and tested

Building

- MEP underground complete – Areas A, B, C, D, E, F, G, P, Q, R and S; ongoing – Area M
- Slabs poured – Area E; partially – Area F
- Slab ready to pour – Area G
- CMU load bearing walls complete – Area R
- Structural steel ongoing – Area R
- CMU loadbearing walls ongoing – Area Q and S
- Roof decking and detailing ongoing – Areas B and C
- Second floor slab on deck ready to pour – Area C
- Concrete columns ongoing – Areas D and N
- Structural steel ongoing – Area D
- First floor interior framings and exterior sheathing ongoing – Area Q
- First floor MEP overhead ongoing – Area A and B
- Fireproofing ongoing at exterior – Area B
- Teaching wall mock-up complete and approved – Area A

**RICHLAND
HIGH SCHOOL
(HS #4)**




AS OF APRIL 2024



**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024

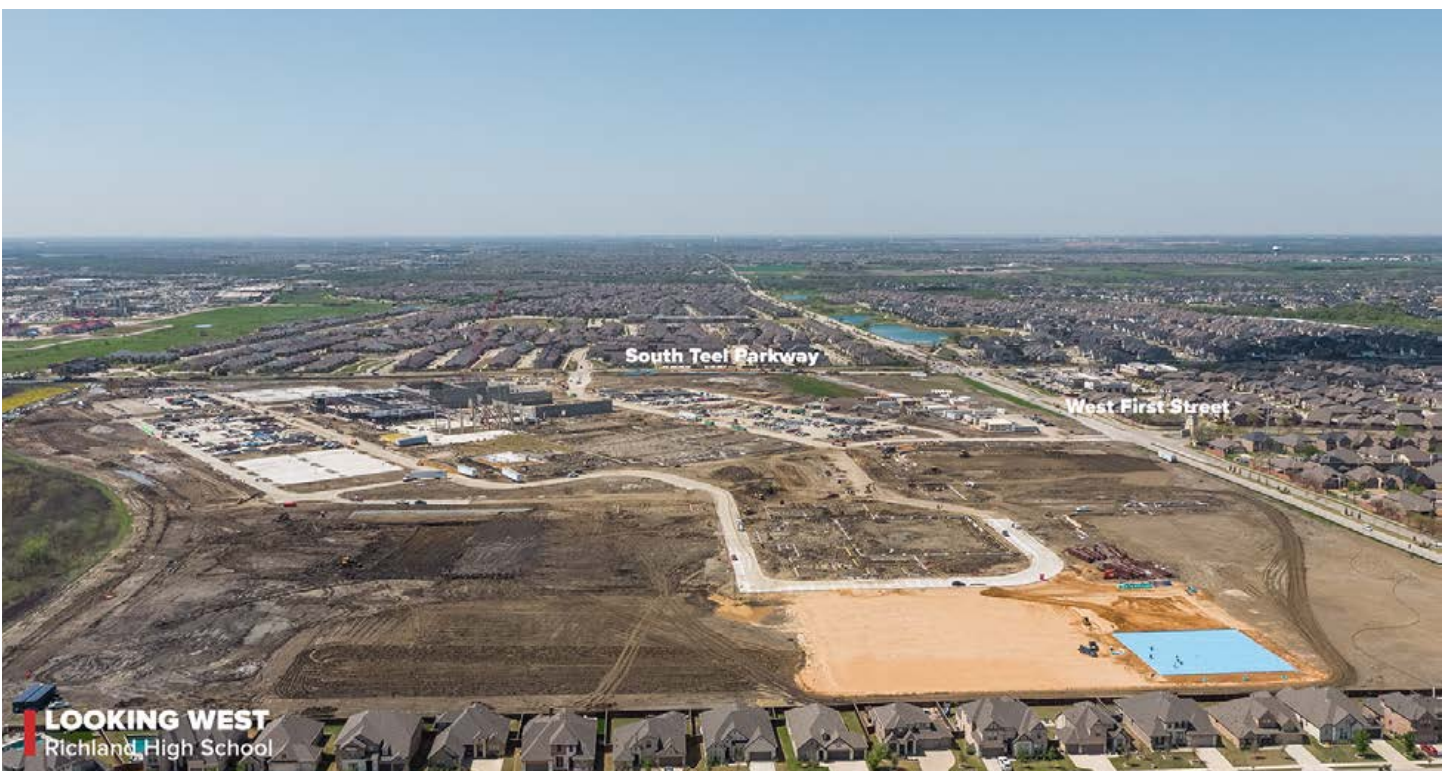


**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024



MAIN ENTRY

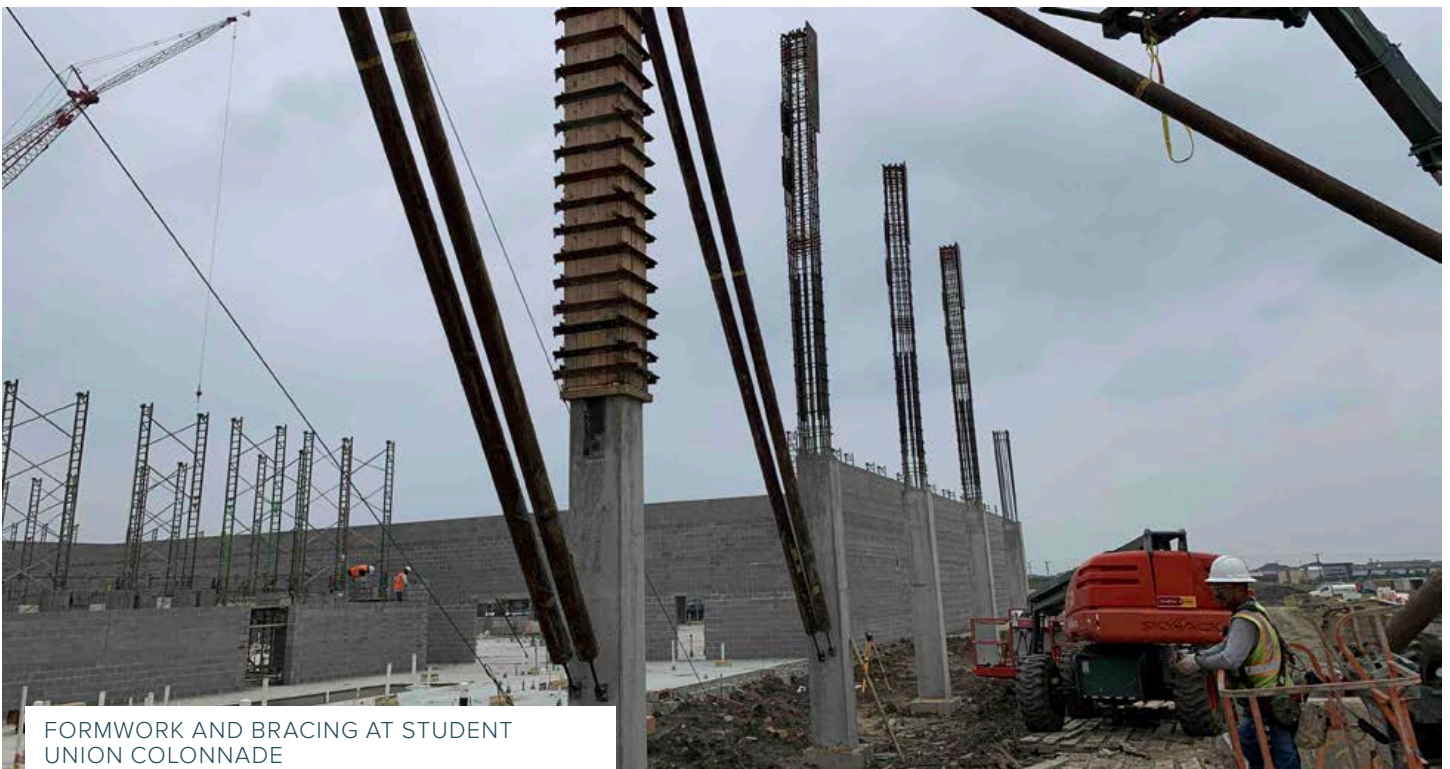


FORMWORK AND BRACING AT STUDENT UNION COLONNADE


**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024

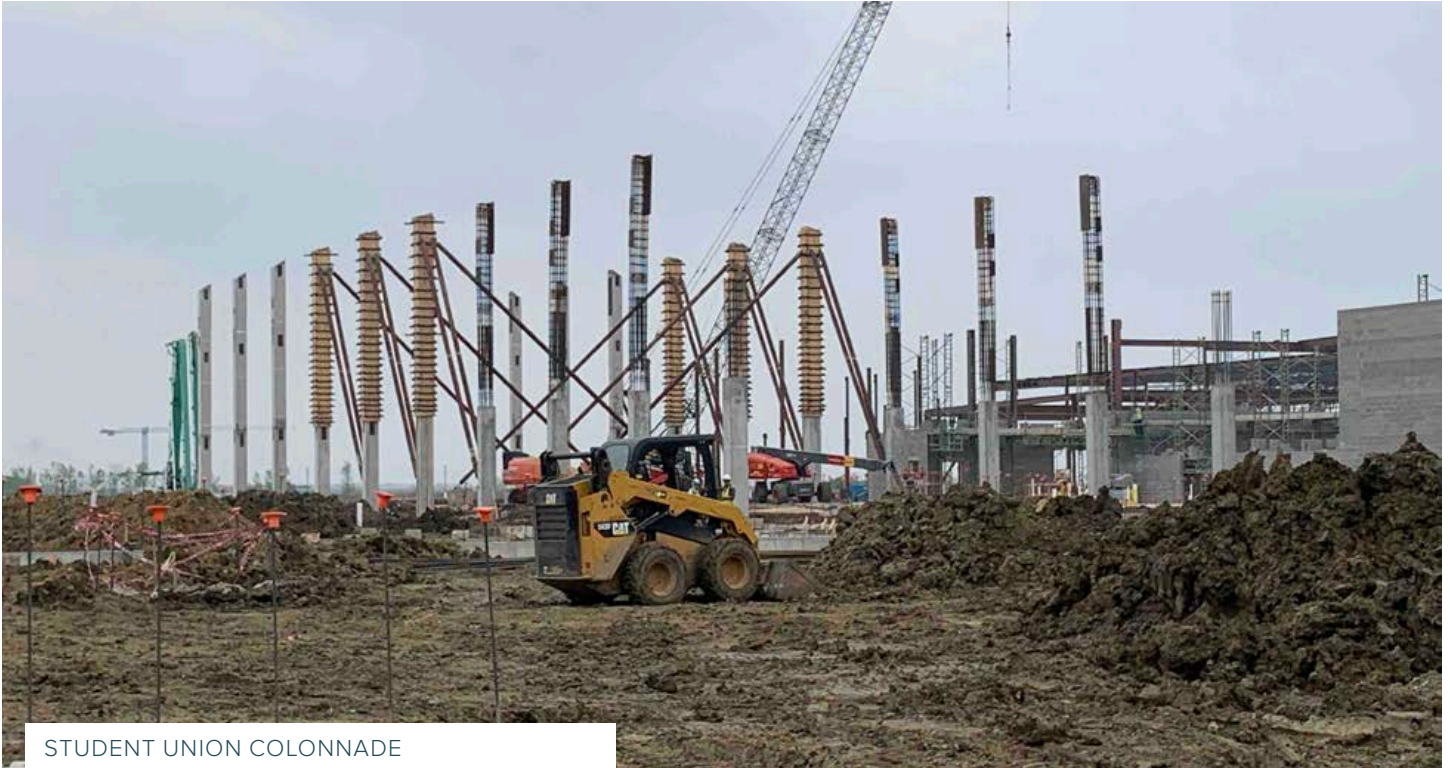

STUDENT UNION COLONNADE

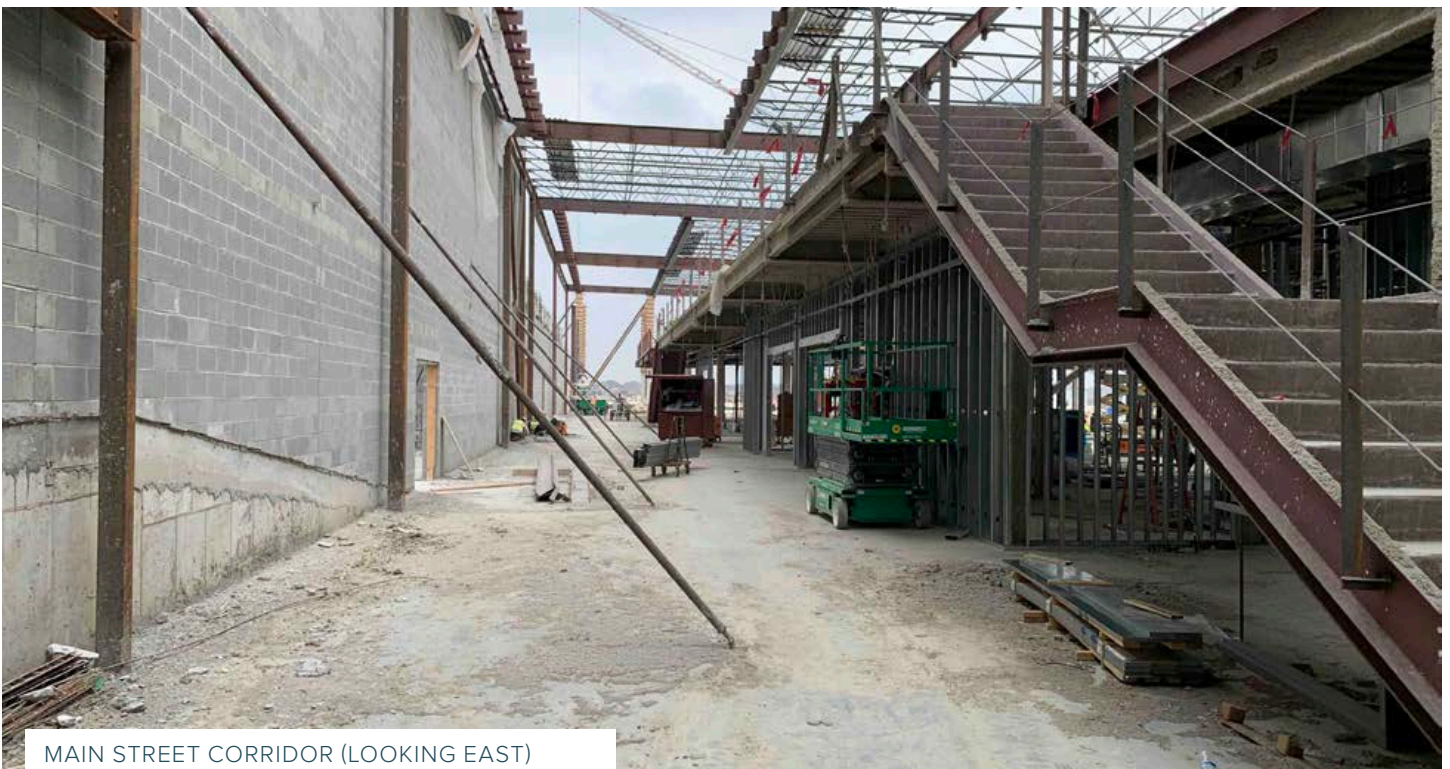


MAIN STREET CORRIDOR (LOOKING EAST)


**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024

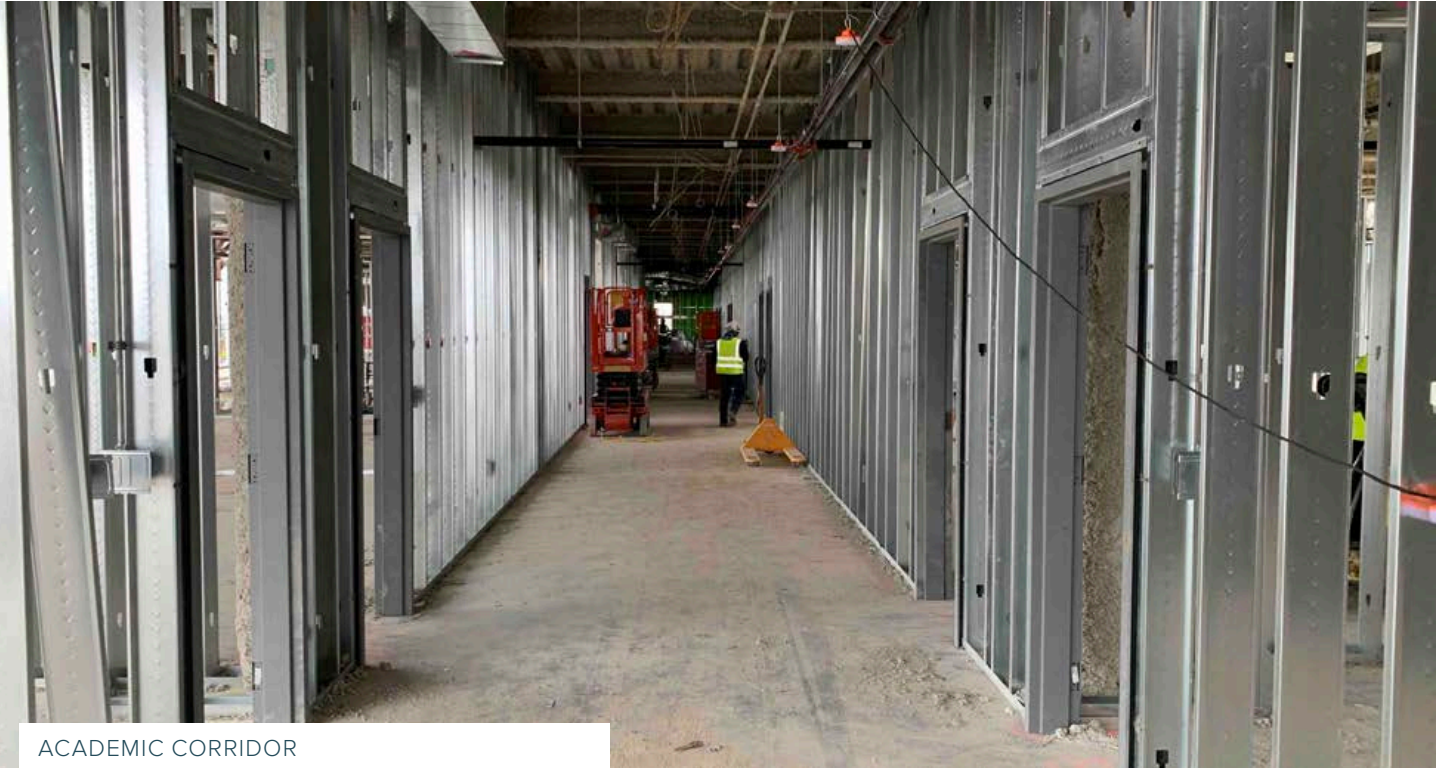

ACADEMIC CORRIDOR

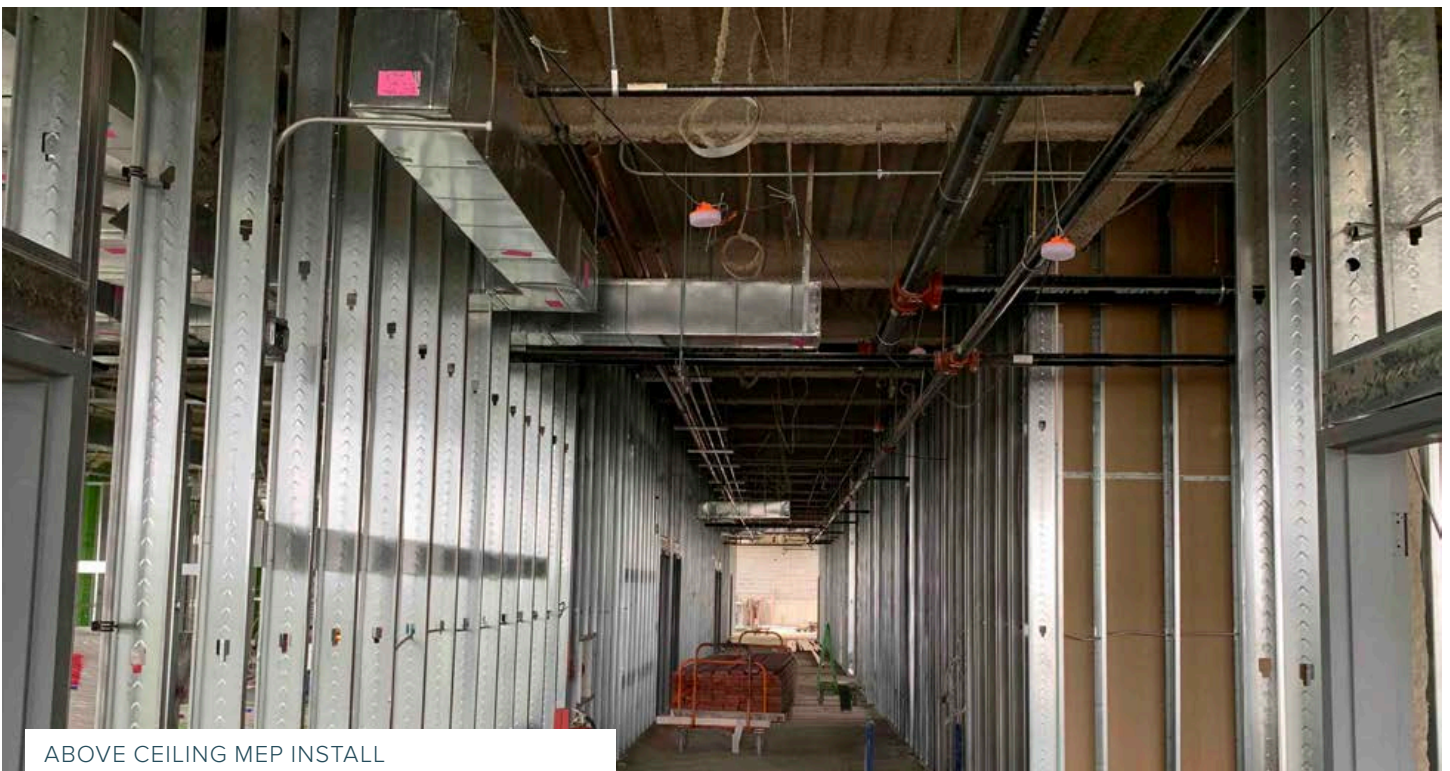

ABOVE CEILING MEP INSTALL


**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024



COURTYARD (WEST ACADEMIC WING)

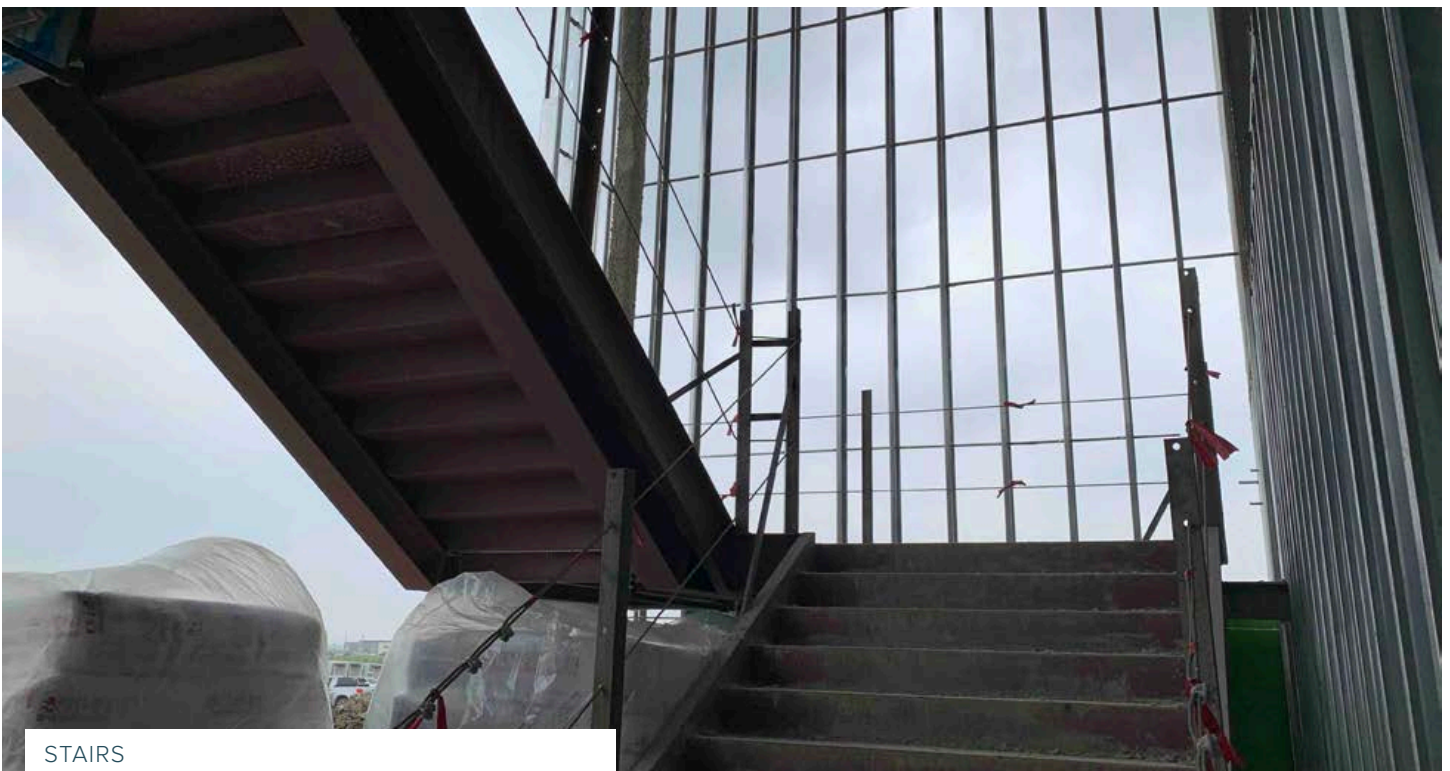


STAIRS

**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024

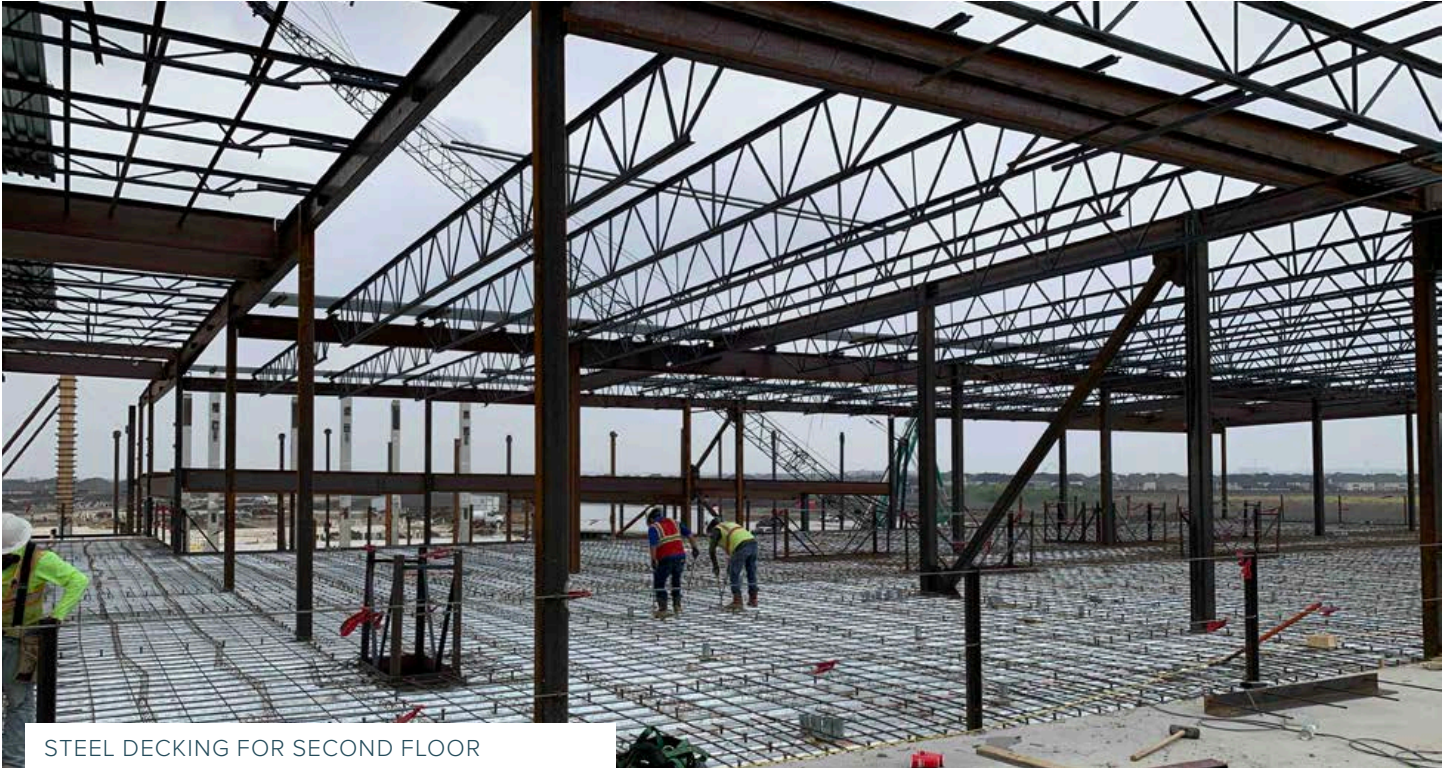

STEEL DECKING FOR SECOND FLOOR



SPRAY-ON FIREPROOFING

**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024



EXTERIOR SHEATHING (WEST ACADEMIC WING)



ART CLASSROOMS

**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024



WOOD SHOP




AUDITORIUM ENTRY

**RICHLAND
HIGH SCHOOL
(HS #4)**



AS OF APRIL 2024

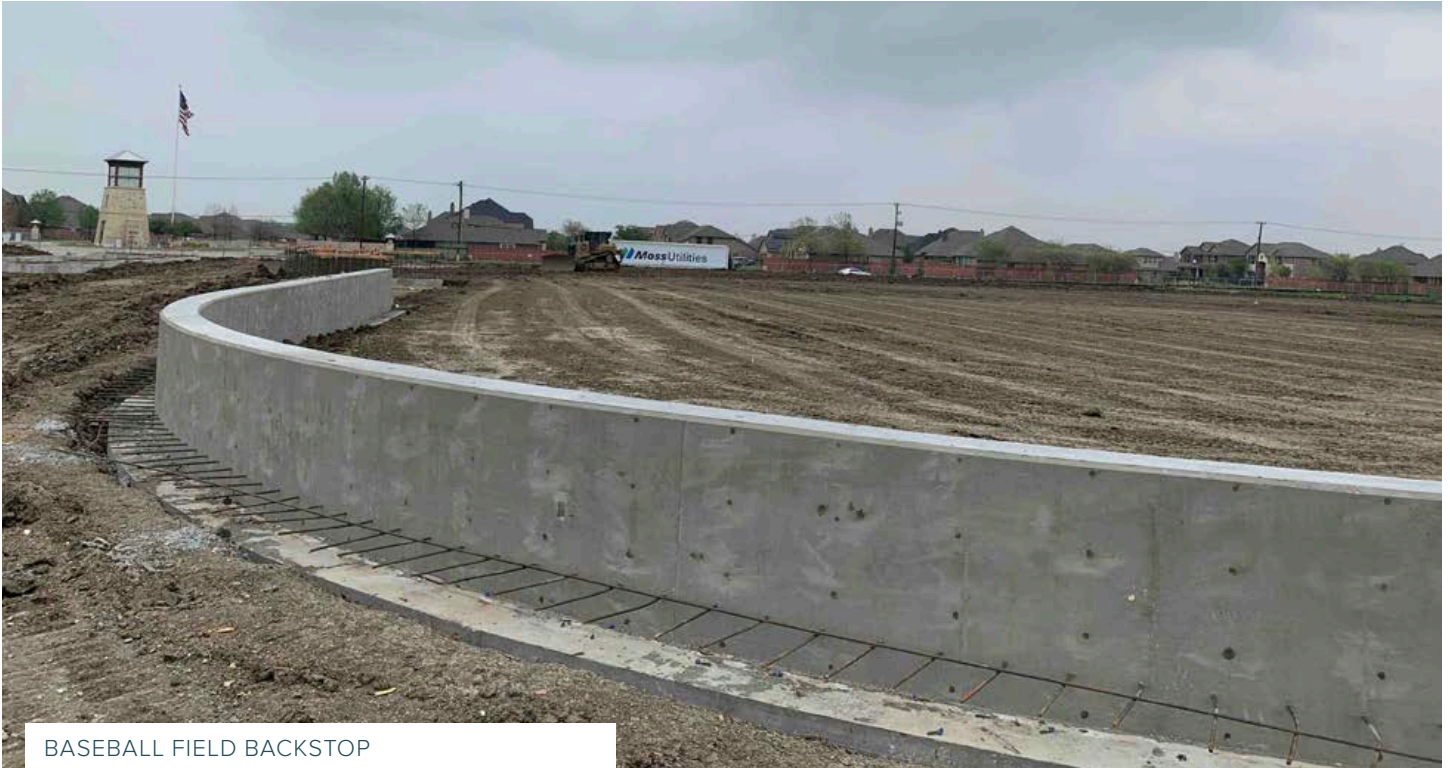

BASEBALL FIELD BACKSTOP



SOFTBALL FIELD BACKSTOP FORMWORK
