

# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

### WORK COMPLETED AND ONGOING:

#### Site

- Landscape installation ongoing
- Playground surfacing on southeast playground ongoing
- Canopy installation ongoing
- Exterior masonry installation nearing completion at the entry tower

#### Building

- Kitchen equipment deliveries and installation ongoing
- Floor tile installation complete
- Millwork installed – Areas 1 and 2
- Ceiling grid, lights and grills are being installed – Areas 1 and 2
- Plumbing fixtures and accessories being installed – Areas 1, 2, 3 and 4
- Tape, bed, and texture ongoing – Area 1
- Door installation ongoing – Areas 1, 2 and 3
- AV installation ongoing – Areas 1, 2 and 3
- Fire alarm trim-out ongoing – Areas 1 and 2
- Remaining Roof Top Units (RTU) installation to be complete by mid-month
- Punch has started – Area 4
- Low Voltage engineer walks ongoing

Aerial - Looking Northeast



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

Aerial - Looking Northwest



Aerial - Looking Southeast



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

Aerial - Looking Southwest



Main Entry Tower



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

Main Entry Corridor



Reception Area



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

Typical Academic Corridor



Typical Classroom

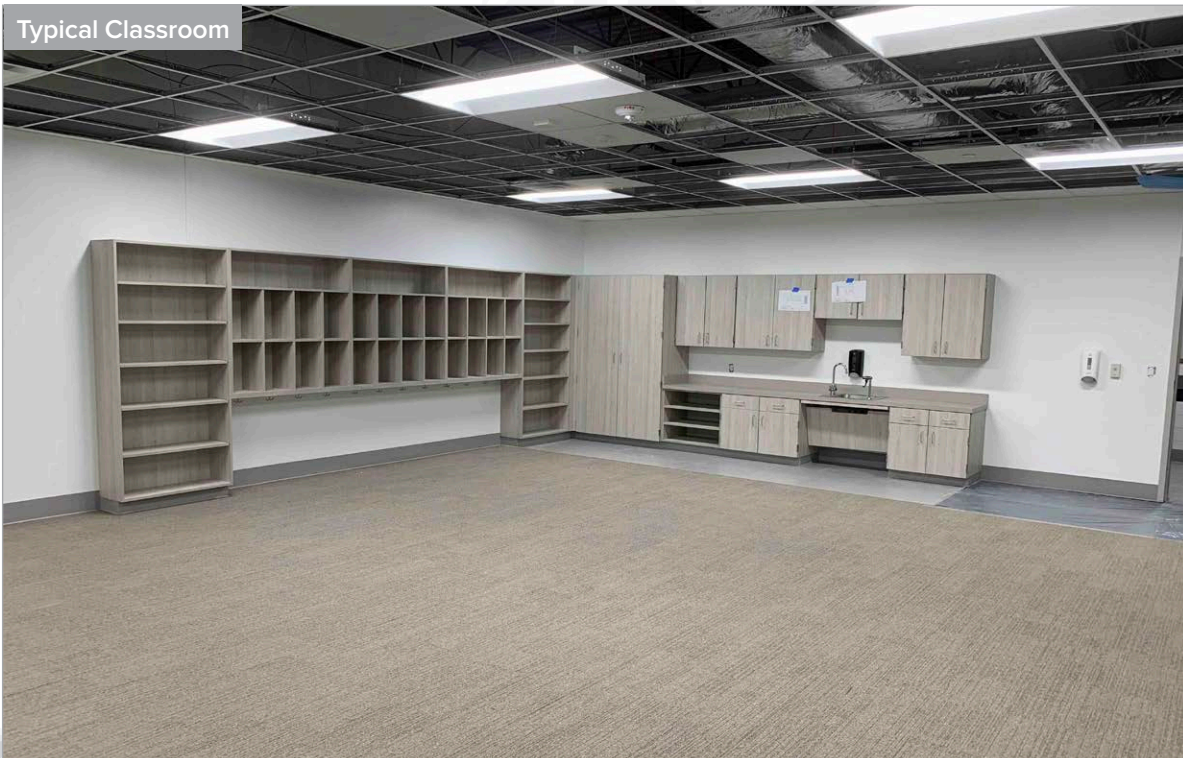

# BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT



## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

Library

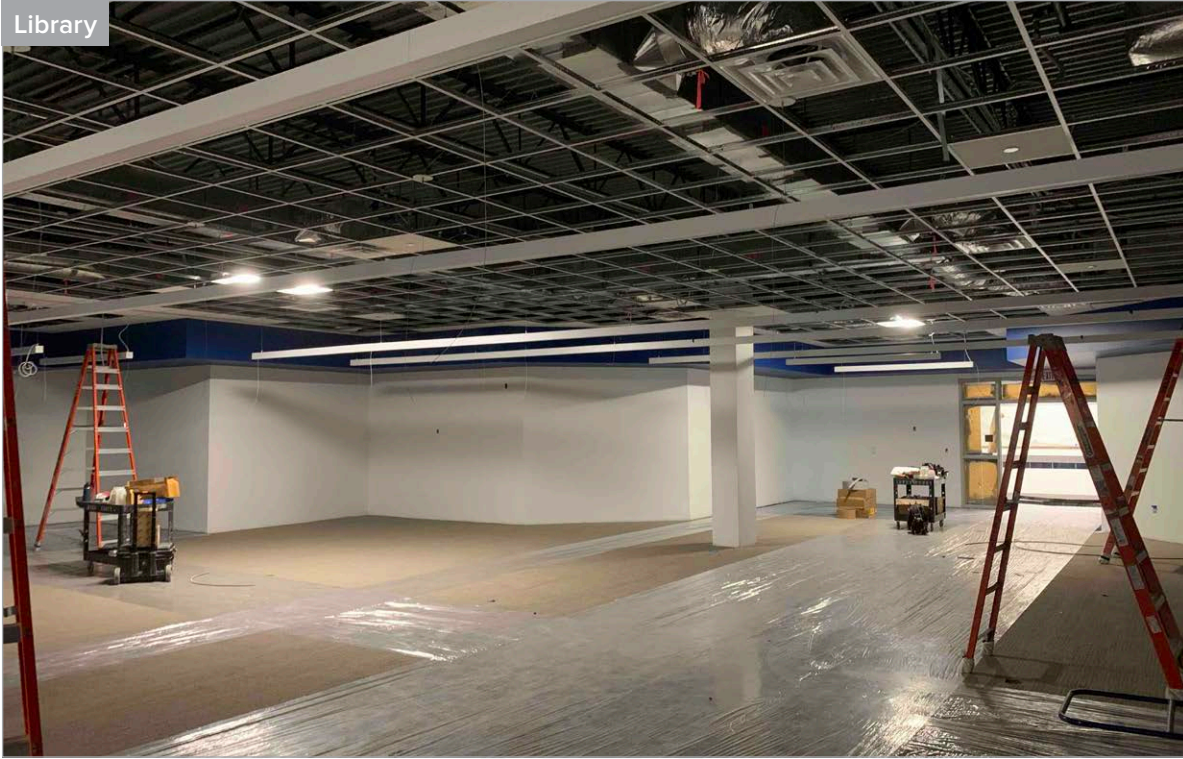

Cafetorium




# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

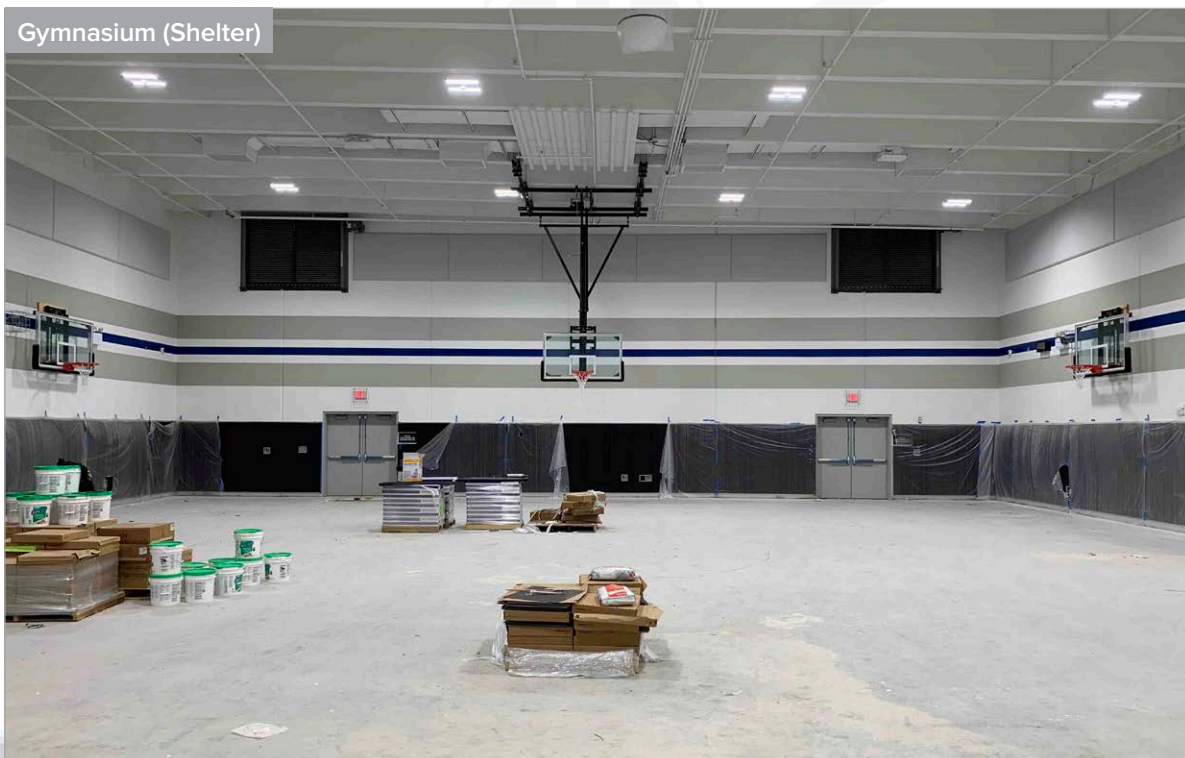

# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JUNE 2022

Rear Entry



Playground





# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



**JOYCE HALL ELEMENTARY SCHOOL (ES #15)**

AS OF JUNE 2022

Hardcourt Play Area



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

### WORK COMPLETED AND ONGOING:

#### Site

- Baseball and softball fields are ready for turf, but it will not be installed for eight months
- Retaining Walls G and F are complete
- Detention pond flume installation ongoing
- Baseball and softball batting cages ongoing
- Sports lighting installation ongoing

#### Main Building

- Steel erection complete – Areas A, B C, E, P, Q, R and S
- Steel erection is ongoing – Areas D, N and M
- MEP/Fire Sprinkler overhead ongoing – Areas A2, B2, C2, P and Q
- Framing complete (1st floor) – Areas A, B, C and D
- Framing is ongoing (2nd floor) – Area C
- CMU columns erection ongoing – Area D
- Interior CMU wall erection ongoing – Areas P, Q and R

- Roofing ongoing – Areas A, B and C are dried-in; installation ongoing – Areas Q and R
- Window/Storefront installation ongoing; Complete through – Area C
- Exterior waterproofing ongoing – Areas C and D
- Fireproofing ongoing – Areas P and Q

#### Multipurpose Facility (MPF) and Ancillary Buildings

- Interior CMU wall erection ongoing – Area T
- Exterior masonry ongoing – Area V
- Steel structure is complete; roof strapping installation ongoing – Area U
- CMU at pump house complete

Aerial - Looking Northeast



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Aerial - Looking Northwest



Aerial - Looking Southeast



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Aerial - Looking Southwest



Main Entry



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Looking South from Student Commons Area



Main Street Academic Corridor

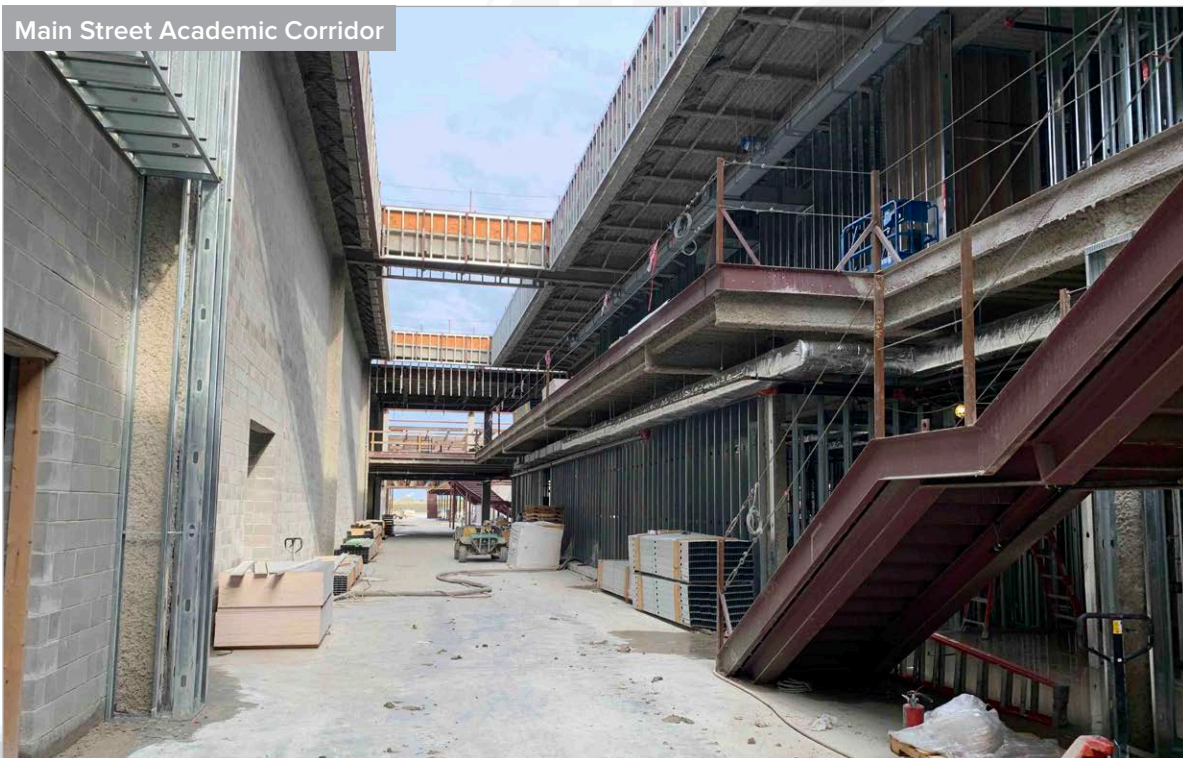

# BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Typical Academic Corridor

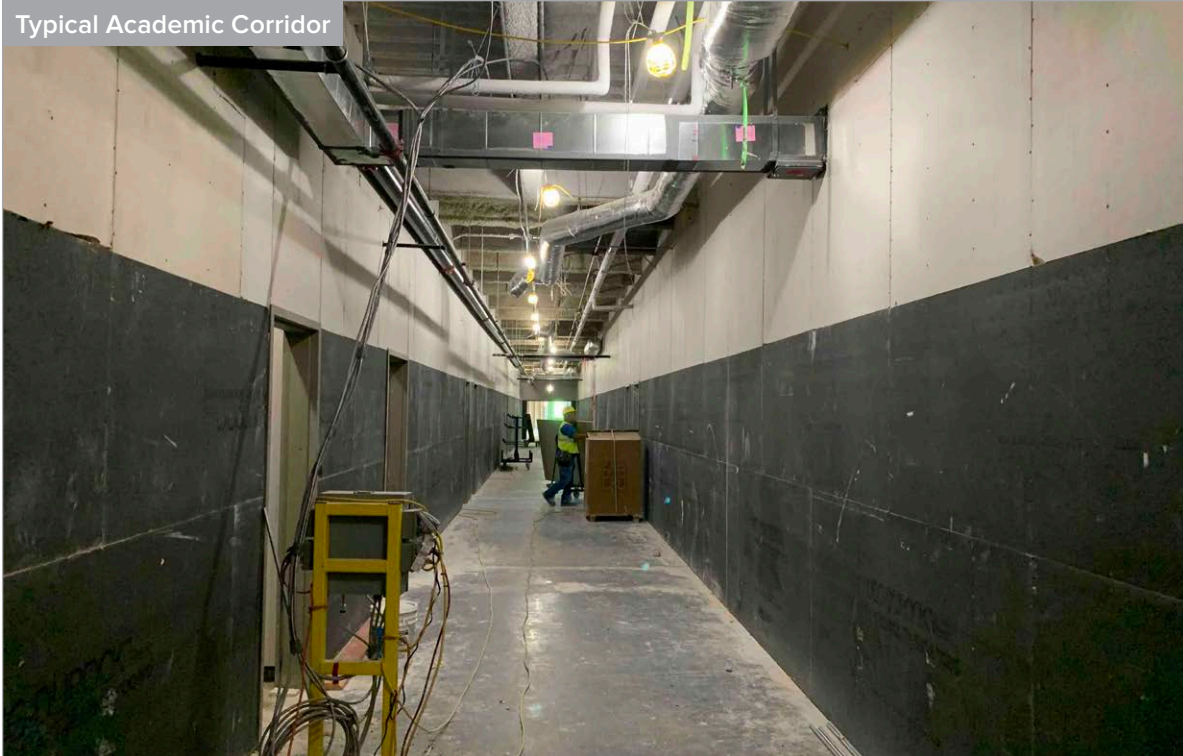

Typical Classroom



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

East Academic Courtyard



Aluminum Storefront Installed



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Masonry Veneer Installation



Auditorium Entry





# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Auditorium Lobby



Auditorium



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Multi-Purpose Facility (MPF)



Multi-Purpose Facility (MPF)



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Baseball Field



Softball Field



# BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



## WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JUNE 2022

Softball Indoor Batting Cage

