

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

WORK COMPLETED AND ONGOING:

Site

- Landscape around site ongoing
- Exterior masonry installation nearing completion at main entry tower
- Preliminary civil town inspection – Complete
- Punch item rework ongoing

Building

- Final clean ongoing
- Architectural punch completion ongoing
- Building electrical final inspection – Complete
- Building plumbing final inspection – Complete
- Building mechanical final inspection – Complete
- Fire alarm final – Complete
- Fire sprinkler final – Complete
- Health – Complete

Aerial - Looking Northeast



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

Aerial - Looking Northwest



Aerial - Looking Southeast



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

Aerial - Looking Southwest



Exterior Building Signage

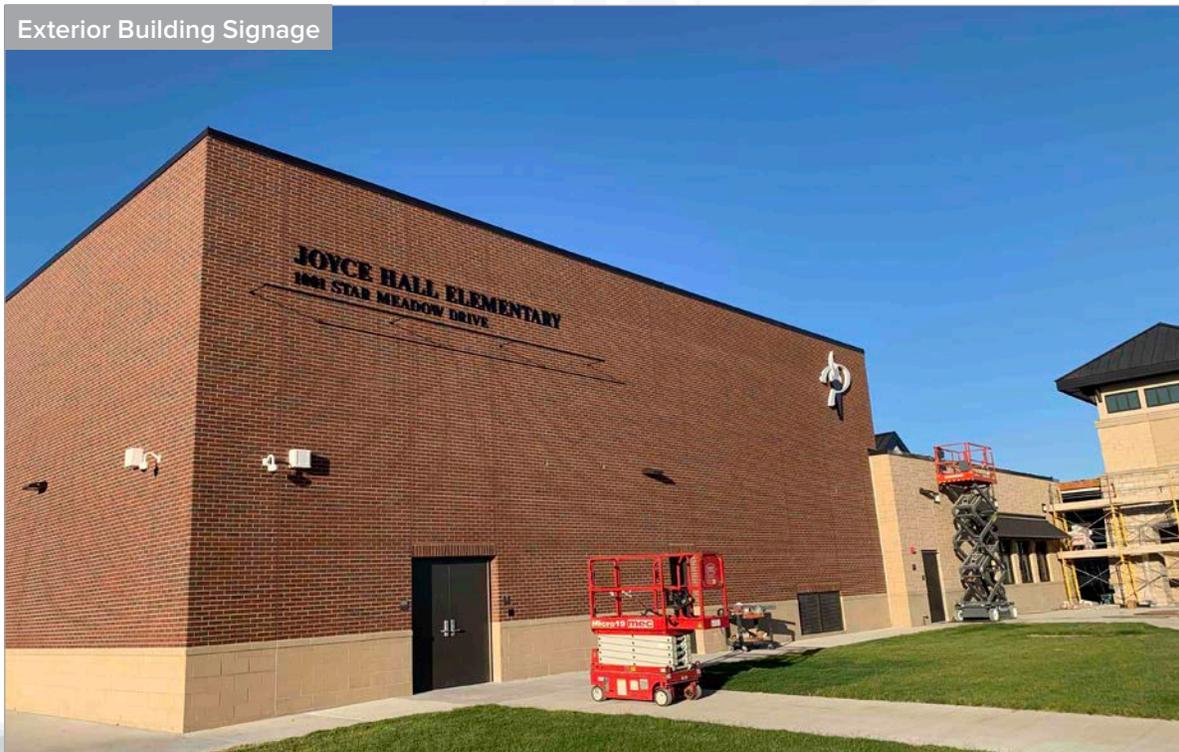

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

Main Entry View



Main Entry Corridor

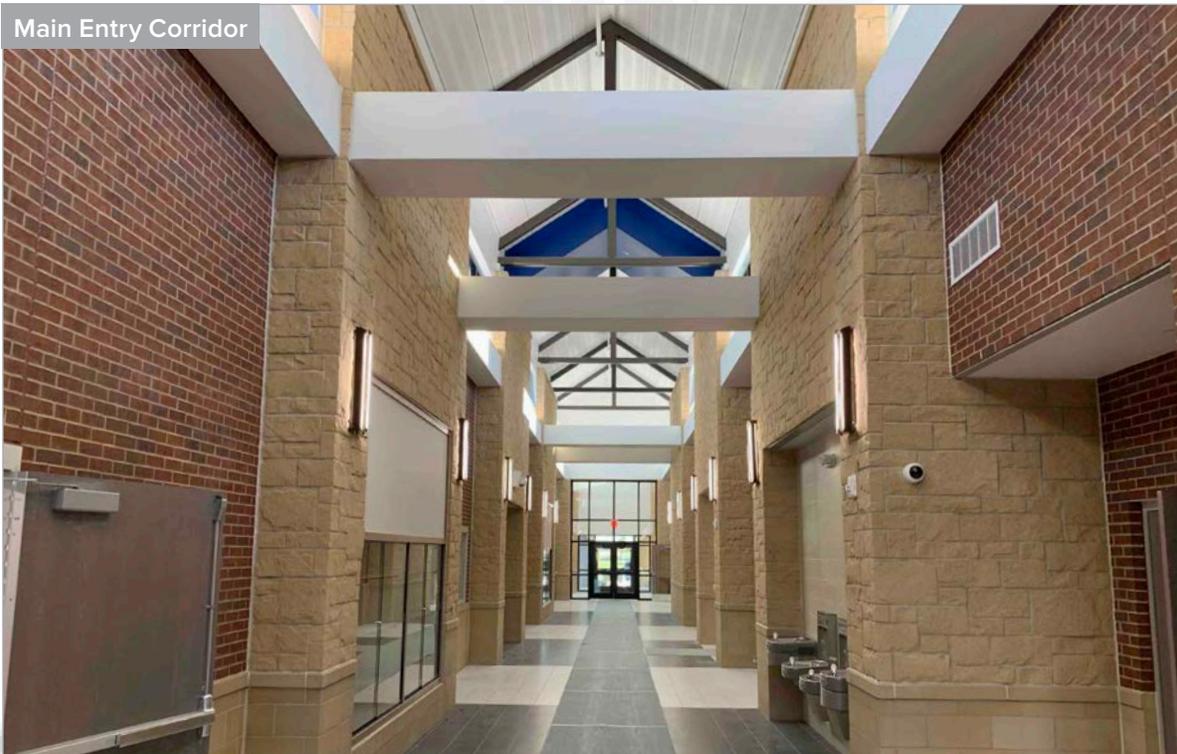

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

Administrative Reception Area



Typical Academic Corridor

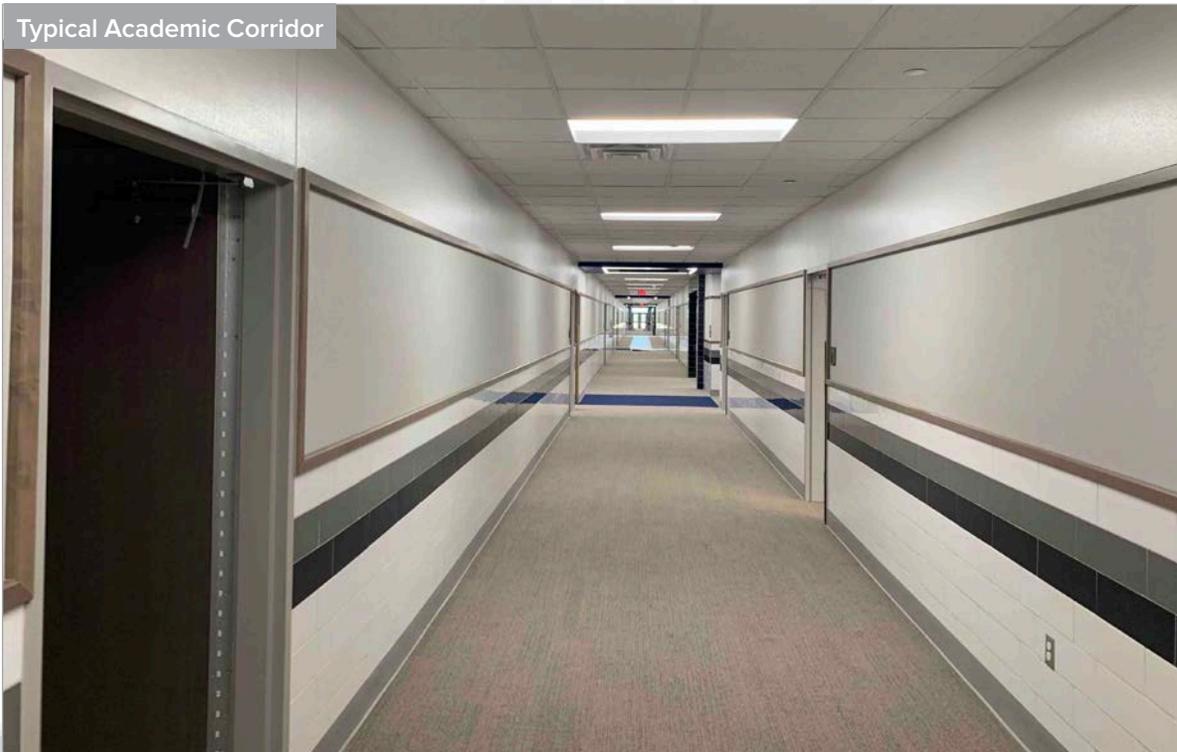

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

Typical Classroom



Typical Multi-User Restroom

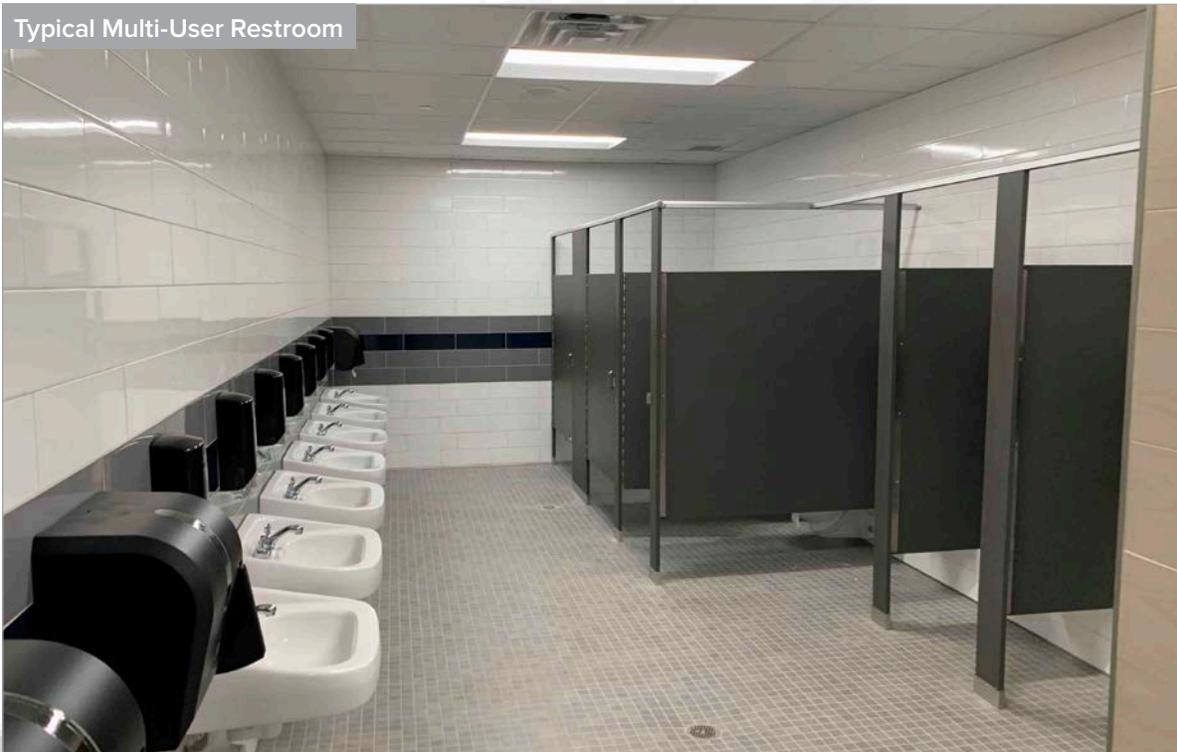


BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

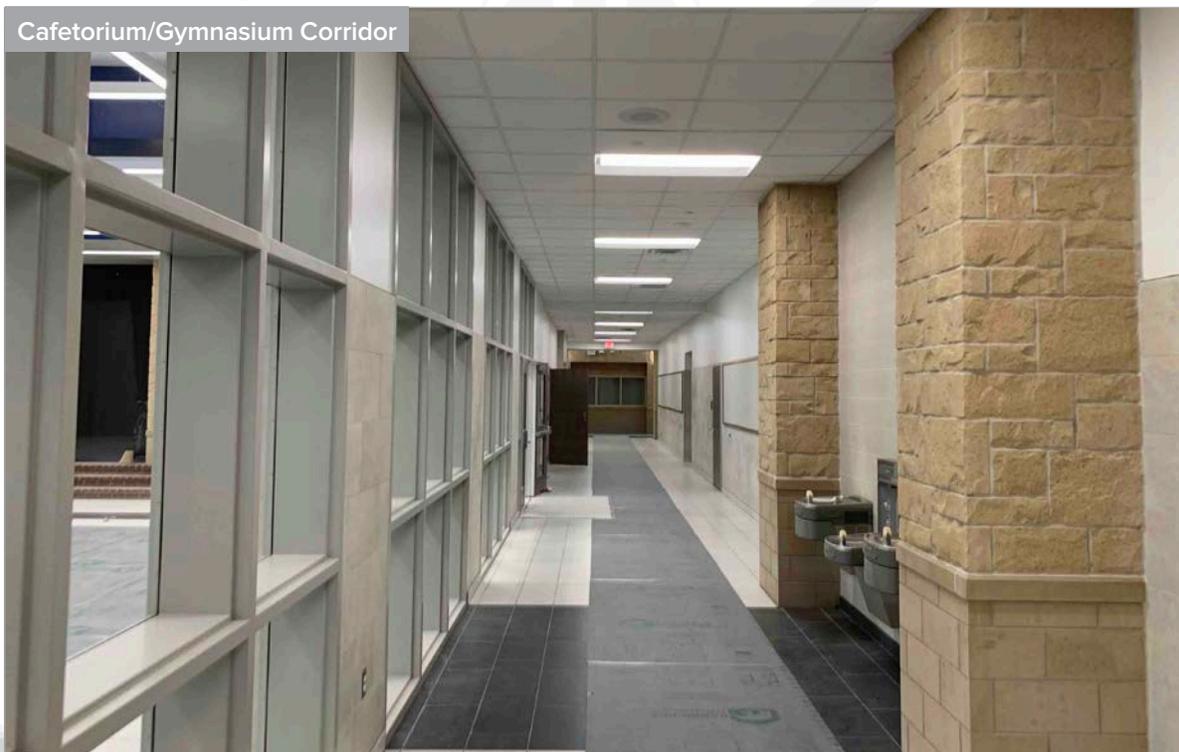

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

Cafetorium



Gymnasium (Shelter)

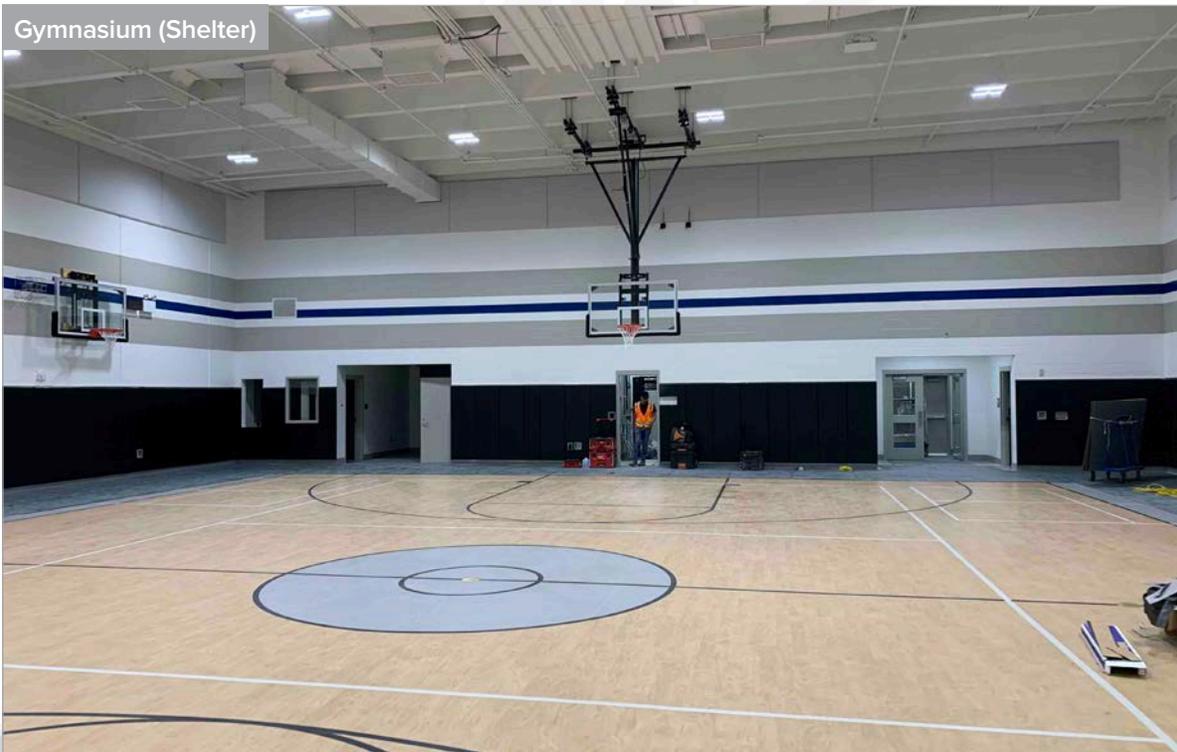

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



JOYCE HALL ELEMENTARY SCHOOL (ES #15)

AS OF JULY 2022

Rear Entry/Playground



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



ELEMENTARY SCHOOL #16 (LILYANA)

AS OF JULY 2022

WORK COMPLETED AND ONGOING:

Permits

- Civil permit has been received
- Building permit – The City of Celina has received everything and is completing final review
- City of Celina expecting to release the permit second week of this month

Submittals and Procurement

- Submittals are currently sitting at roughly 51% complete
- Preliminary panel books for the Tornado Shelter have been received
- Pogue to start storm shelter coordination

Site

- Mass grading ongoing at the building pad, retaining wall and parking areas
- Utilities have begun
- Utility material procurement ongoing
- Test pier has been completed
- Pier drilling has begun



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



ELEMENTARY SCHOOL #16 (LILYANA)

AS OF JULY 2022



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



ELEMENTARY SCHOOL #16 (LILYANA)

AS OF JULY 2022



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



ELEMENTARY SCHOOL #16 (LILYANA)

AS OF JULY 2022

Earthwork



Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



ELEMENTARY SCHOOL #16 (LILYANA)

AS OF JULY 2022

Earthwork



Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



ELEMENTARY SCHOOL #16 (LILYANA)

AS OF JULY 2022

Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF JULY 2022

WORK COMPLETED AND ONGOING:

Permits

- Civil Permit – Issued
- Building Permit – City comments have been received and resubmitted

Site

- Mobilization of earthwork equipment
- Stripping topsoil ongoing
- Preparing to bring water service to the site from Virginia Parkway for earthwork operations
- Grading is ongoing
- Coordinating site utilities and earthwork operations

Building

- Grading for foundation pad ongoing
- Preparing to drill test pier holes
- Coordinating pier drilling and chemical injection operations



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF JULY 2022



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF JULY 2022



Earthwork

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF JULY 2022

Earthwork



Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF JULY 2022

Earthwork



Earthwork



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF JULY 2022



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

WORK COMPLETED AND ONGOING:

Site

- Detention pond flume complete
- Detention pond grading ongoing
- Baseball and softball fields are ready for turf (installation to occur in about eight months)
- Baseball and softball fencing complete
- Baseball batting cage complete
- Sports lighting at baseball, softball, and football complete
- Sports lighting installation at tennis courts ongoing
- Irrigation installation ongoing – West side of the property
- Pier caps for decorative fence are complete

Building

- Steel erection complete – Areas A, B, C, E, L, M, P, Q, R and S
- Steel erection ongoing – Areas D, F and N
- MEP/Fire Sprinkler overhead ongoing – Areas D1, P, Q, R and S

- Framing complete – Areas A, A2, B, B2, C, C2 and D
- Framing ongoing – Areas E1, Q and R
- CMU columns complete – Area D
- Interior CMU walls ongoing – Areas M, P and Q
- Roofing installation ongoing – Areas A, B, C, P, Q and R are dried-in
- Window/Storefront installation ongoing; Complete through Area C
- Exterior waterproofing ongoing – Area D
- Brick Veneer installation ongoing - Area A (East side) and Area B (Courtyard)
- Fireproofing ongoing – Areas D1, R and S
- Fire alarm installation ongoing – Areas A1 and B1
- Painting ongoing – Areas A1, A2, B1 and B2
- Tornado shelter structure is complete

Multipurpose Facility (MPF) and Ancillary Buildings

- Masonry ongoing – Areas U and V
- Roof panel strapping installation ongoing – Area U

Aerial - Looking East



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Aerial - Looking Northwest



Aerial - Looking Southeast



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Aerial - Looking Southwest



Aerial - Looking West



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Main Entry



Student Commons



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

West Academic Wing Steel



Main Street Corridor

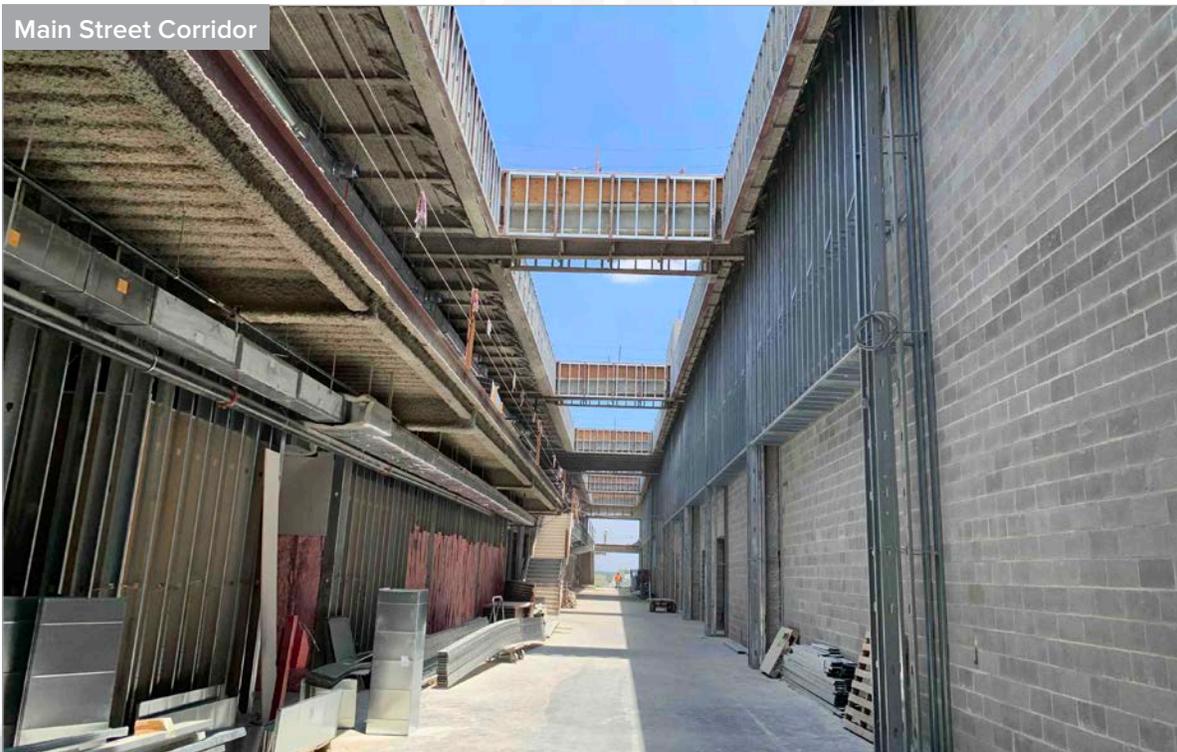

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Academic Corridor



Academic Courtyard

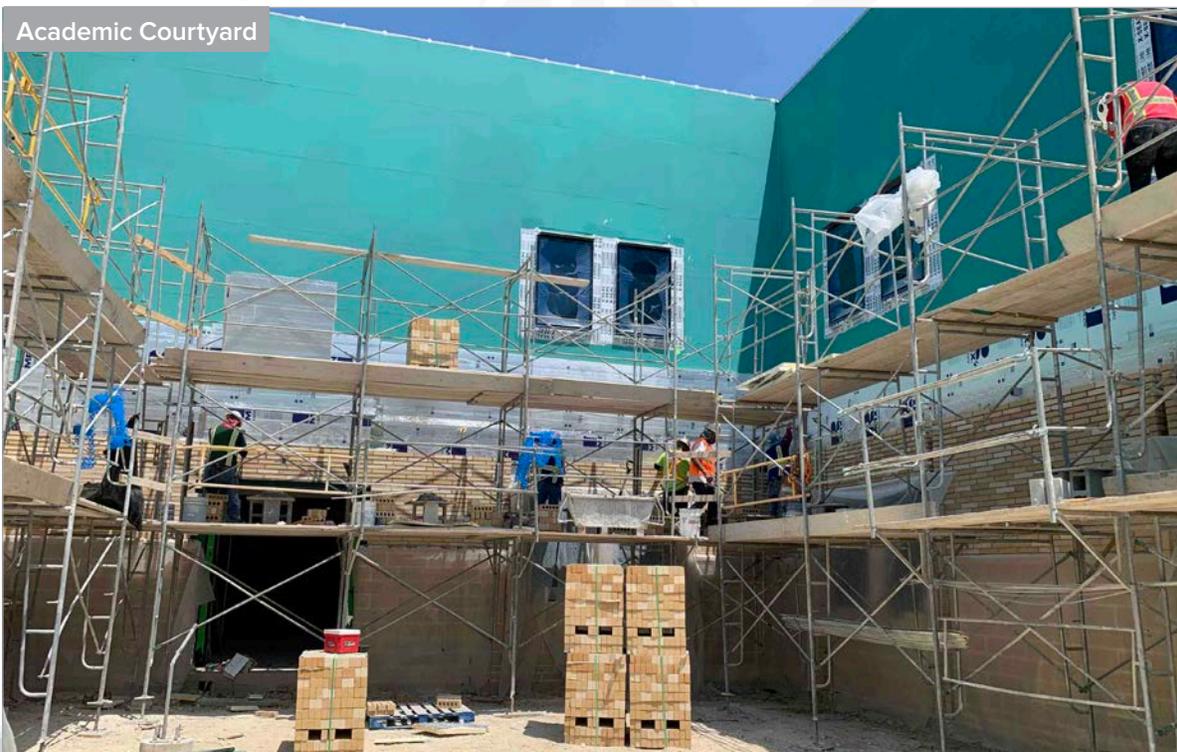

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Exterior Masonry Progress



Auditorium Entry



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Auditorium Lobby



Auditorium Scaffolding

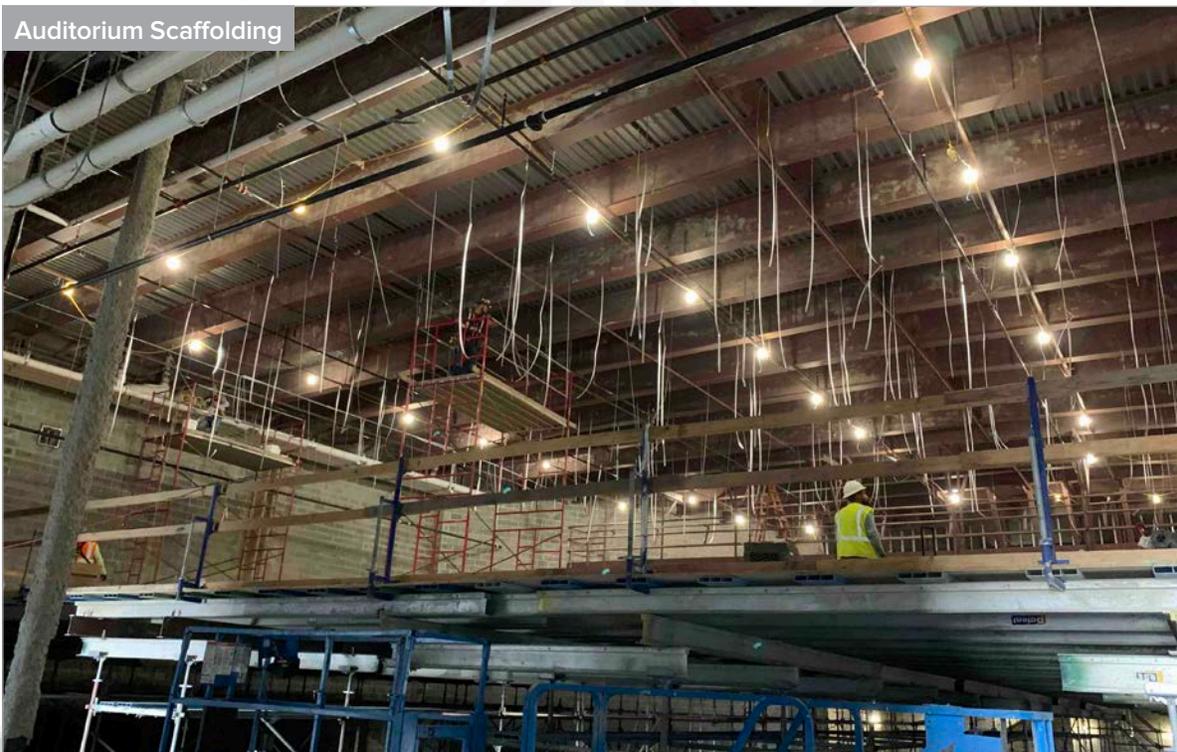

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Exterior Auxiliary Gymnasium (Tornado Shelter)



Interior Auxiliary Gymnasium (Tornado Shelter)



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Multi-Purpose Facility (MPF)



Interior Multi-Purpose Facility (MPF)



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Outdoor Multi-Purpose Field/Track Lighting



Baseball Field Progress

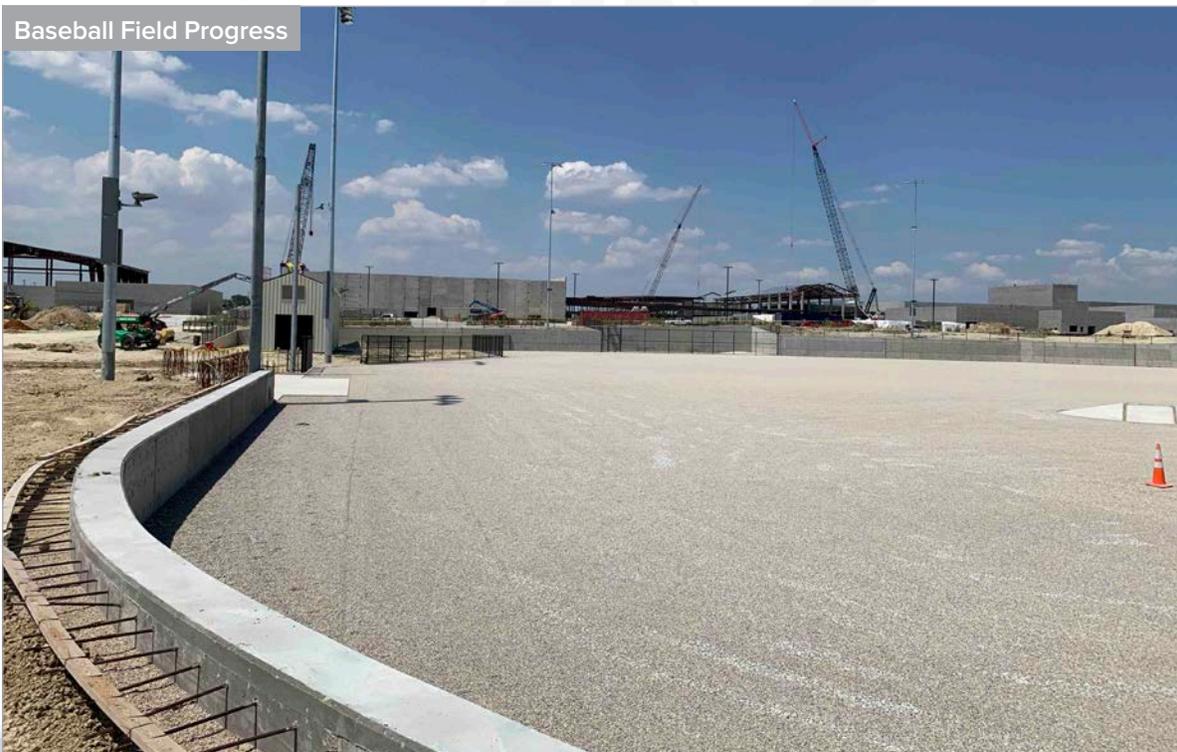

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF JULY 2022

Baseball and Softball Concession/Restroom Building



Outfield Fence at Softball Field

