

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF SEPTEMBER 2022

WORK COMPLETED AND ONGOING:

Site

- Water line 100% complete
- Storm sewer lines 90% complete
- Excavation of retaining walls complete

Building

- All grade beams complete
- Underground electrical and plumbing complete – Area 4
- Preparing for slab placement this week – Area 4
- Underground utilities ongoing – Area 3



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF SEPTEMBER 2022



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF SEPTEMBER 2022



Retaining Wall Foundation and Reinforcing



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF SEPTEMBER 2022

Subgrade Preparation at Concrete Paving (Fire Lanes)



Trenching for Underslab Utilities

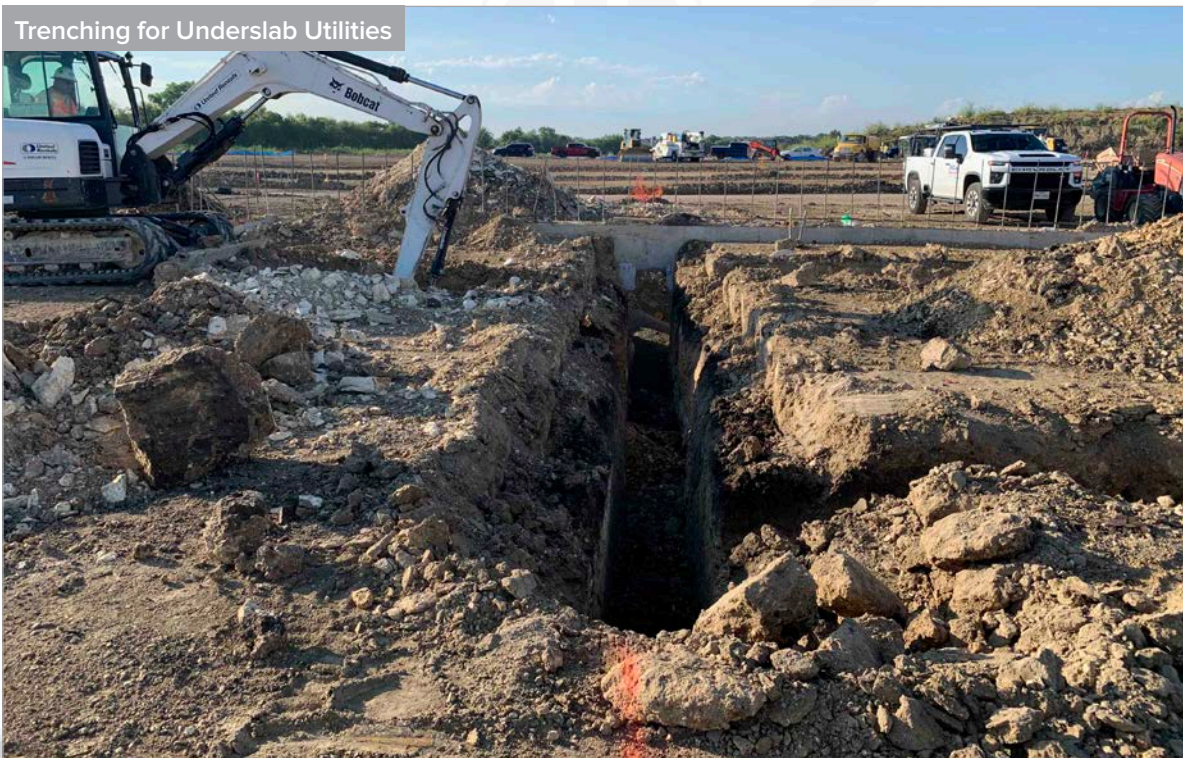

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF SEPTEMBER 2022

Underslab Electrical



Underslab Electrical at Main Electrical Room

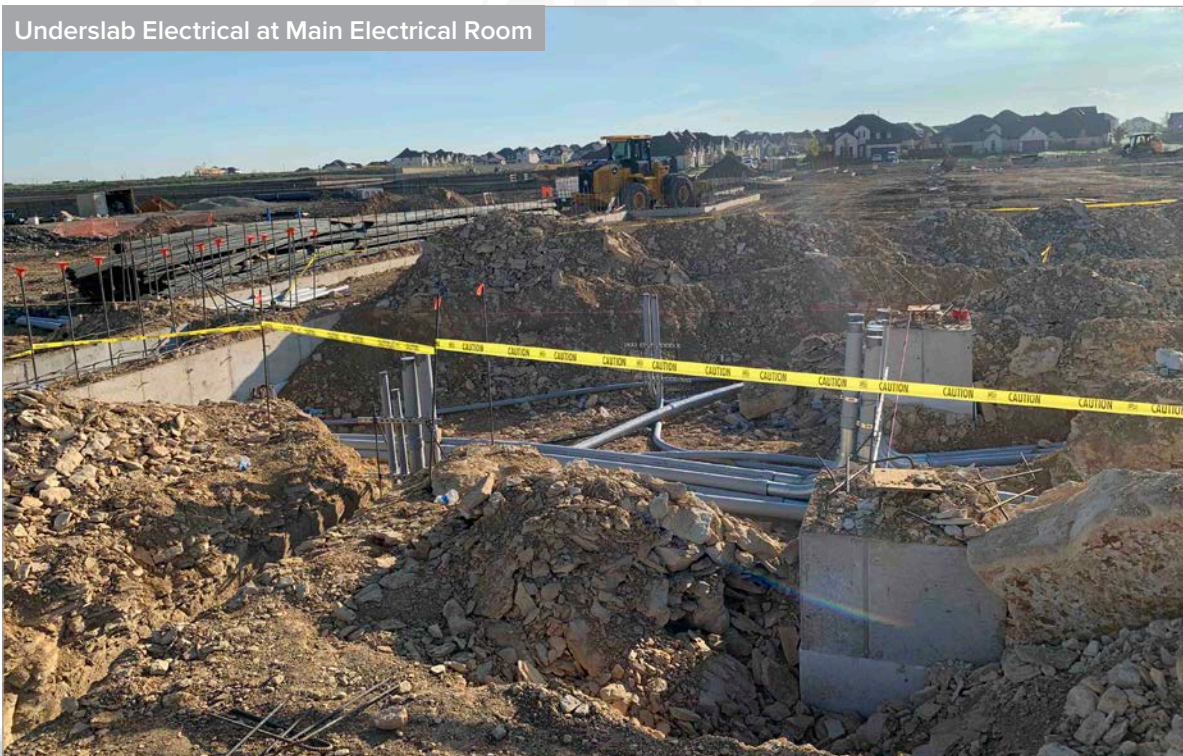

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF SEPTEMBER 2022

Back Filling at Grade Beams



Preparing for Carton Form Placement



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



LILYANA ELEMENTARY SCHOOL (ES#16)

AS OF SEPTEMBER 2022

Cafetorium and Gymnasium Corridor



Underslab Plumbing at Kitchen Area



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DAN CHRISTIE ELEMENTARY SCHOOL (ES#17)

AS OF SEPTEMBER 2022

WORK COMPLETED AND ONGOING:

Permits

- Grading Permit – Permit to be issued by the middle of September
- Building Permit – Town has the documents for review
- Building Permit will not be issued prior to the civil permit release

Site

- SWPPP – Laying out for erosion control measures complete; SWPPP to follow
- Grading tentatively on schedule for 9/17 (grading permit to be issued 9/15)




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DAN CHRISTIE ELEMENTARY SCHOOL (ES#17)

AS OF SEPTEMBER 2022

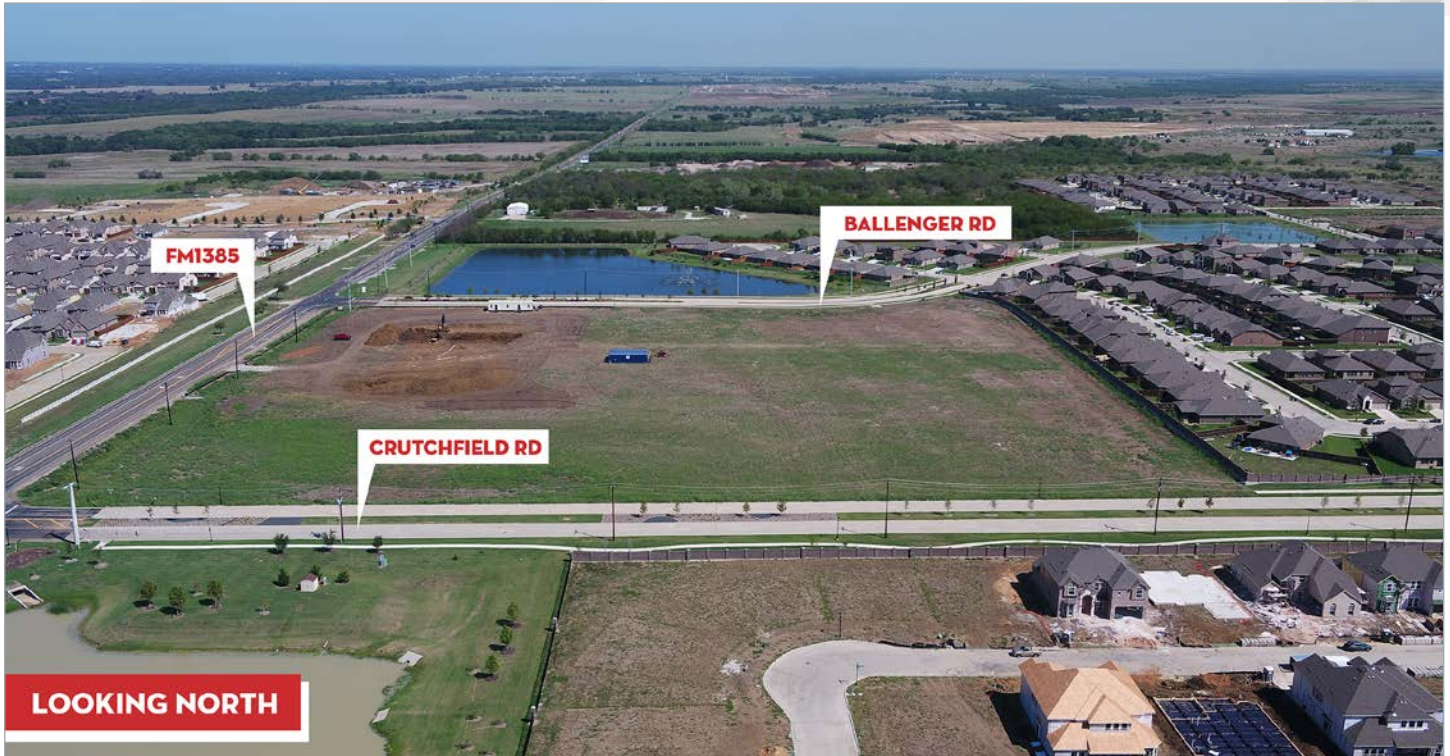

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



DAN CHRISTIE ELEMENTARY SCHOOL (ES#17)

AS OF SEPTEMBER 2022



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF SEPTEMBER 2022

WORK COMPLETED AND ONGOING:

Permits

- Received permission from city to proceed with MEP underground in building
- Building Permit – Pending City Approval

Site

- Sanitary sewer, storm sewer and water under fire lanes complete
- Preparing for formwork, reinforcing, and pouring of pavement – Drive B
- Preparing to lime stabilize subgrade at northwest parking lot and associated fire lane
- Lime stabilizing pavement subgrade to continue
- Pour pavement at fire lanes after subgrade is limed and underground utilities are tested

Building

- Underground MEP underway – Area A
- Backfilling grade beams - Area A
- Chemically treating soil – Area A
- Forming and reinforcing grade beams – Area B
- Grade beam work to be complete this month
- Will start pouring building slabs this month
-
- Drilling piers – Areas B and C
- Chemically treating soil – Area A




BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF SEPTEMBER 2022

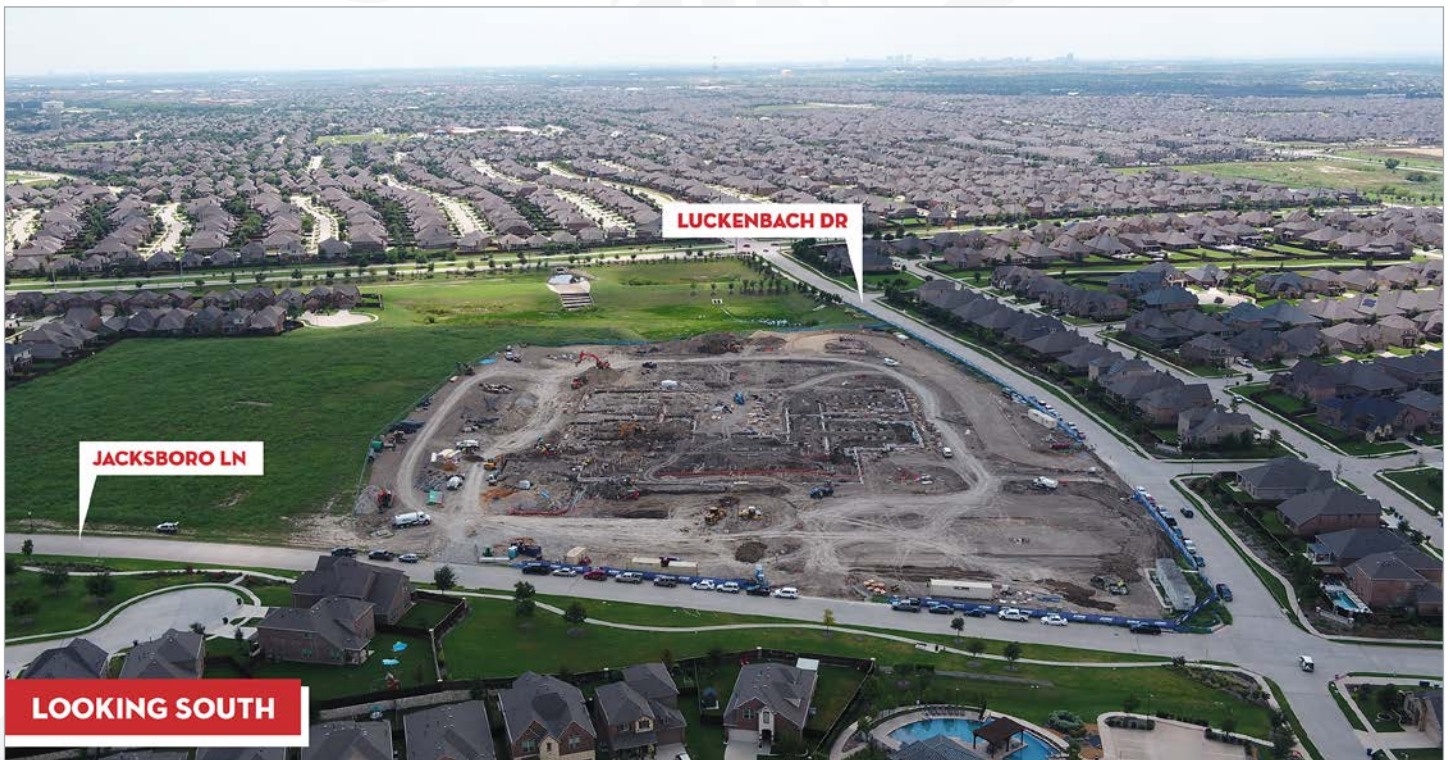

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF SEPTEMBER 2022



Formwork for Concrete Paving (Fire Lanes)



BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF SEPTEMBER 2022

Formwork for Concrete Paving (Fire Lanes)

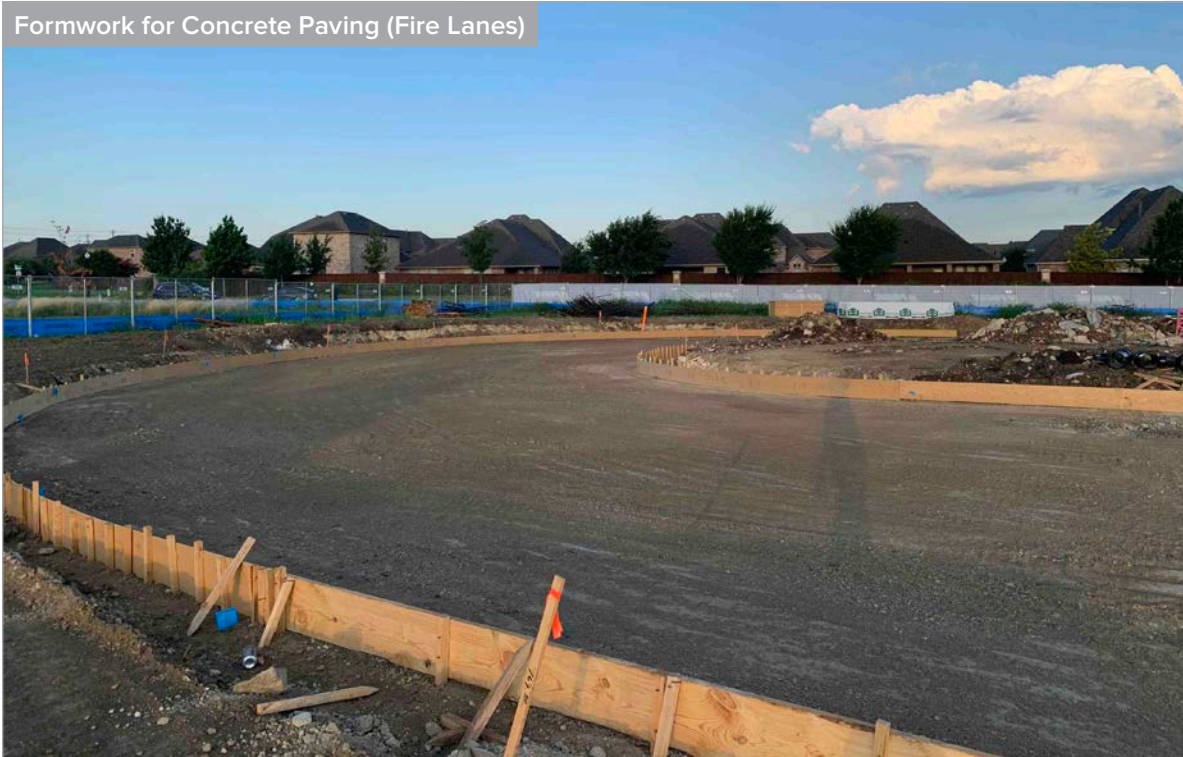

Reinforcing and Formwork for Concrete Paving (Fire Lanes)

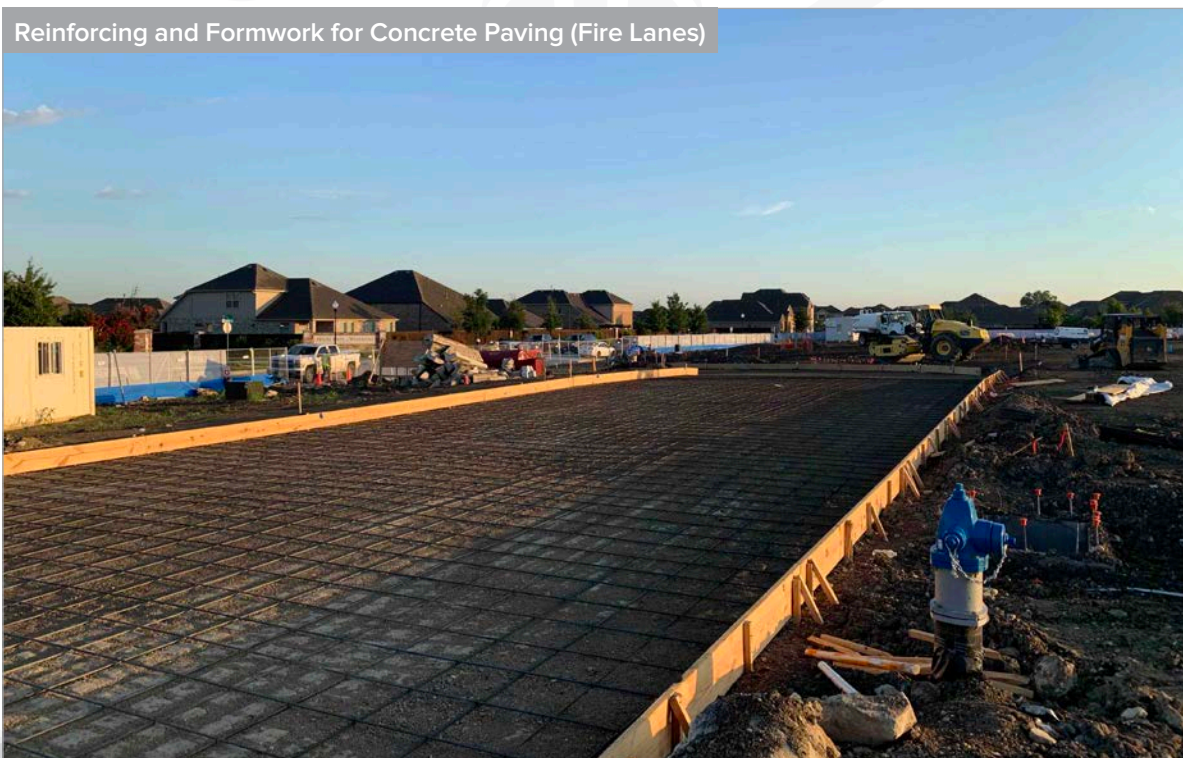

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF SEPTEMBER 2022

Reinforcing and Formwork for Concrete Paving (Fire Lanes)



Completed Piers



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF SEPTEMBER 2022

Grade Beam and Pier Cap Formwork



Grade Beam Reinforcing and Formwork

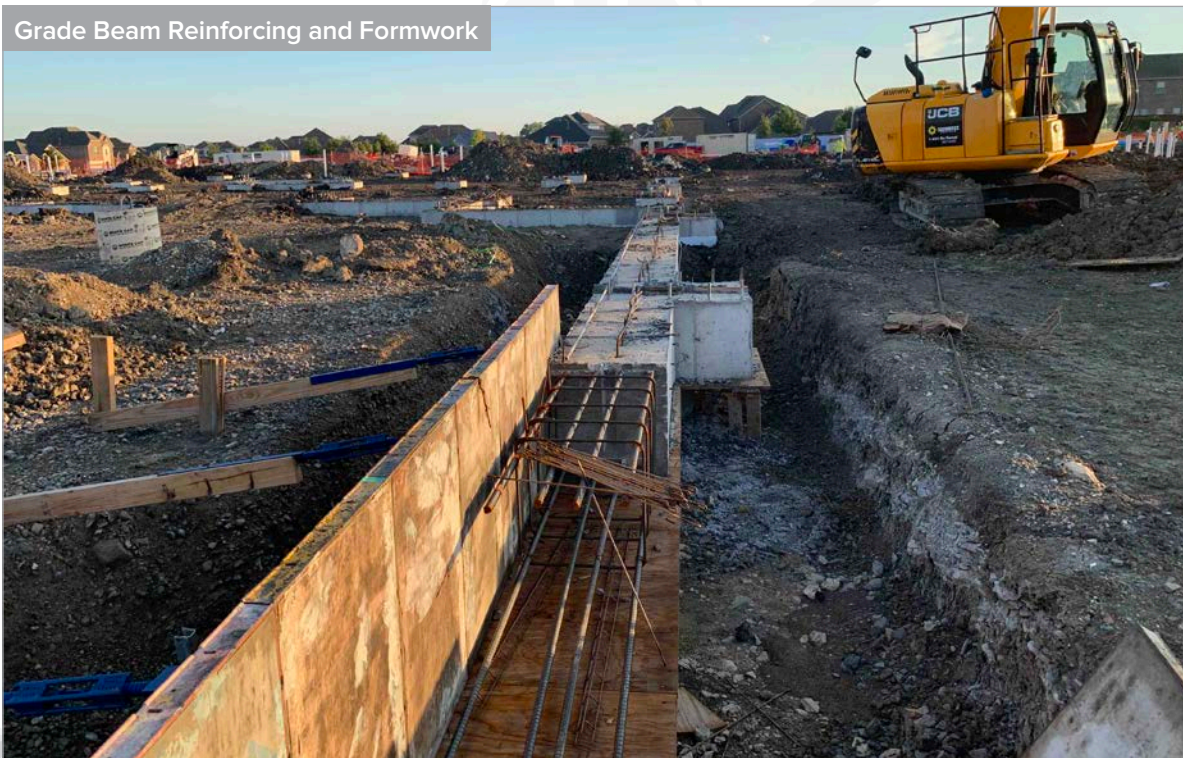

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




EARLY CHILDHOOD SCHOOL (WESTRIDGE)

AS OF SEPTEMBER 2022

Completed Grade Beams and Pier Caps



Underground Utilities

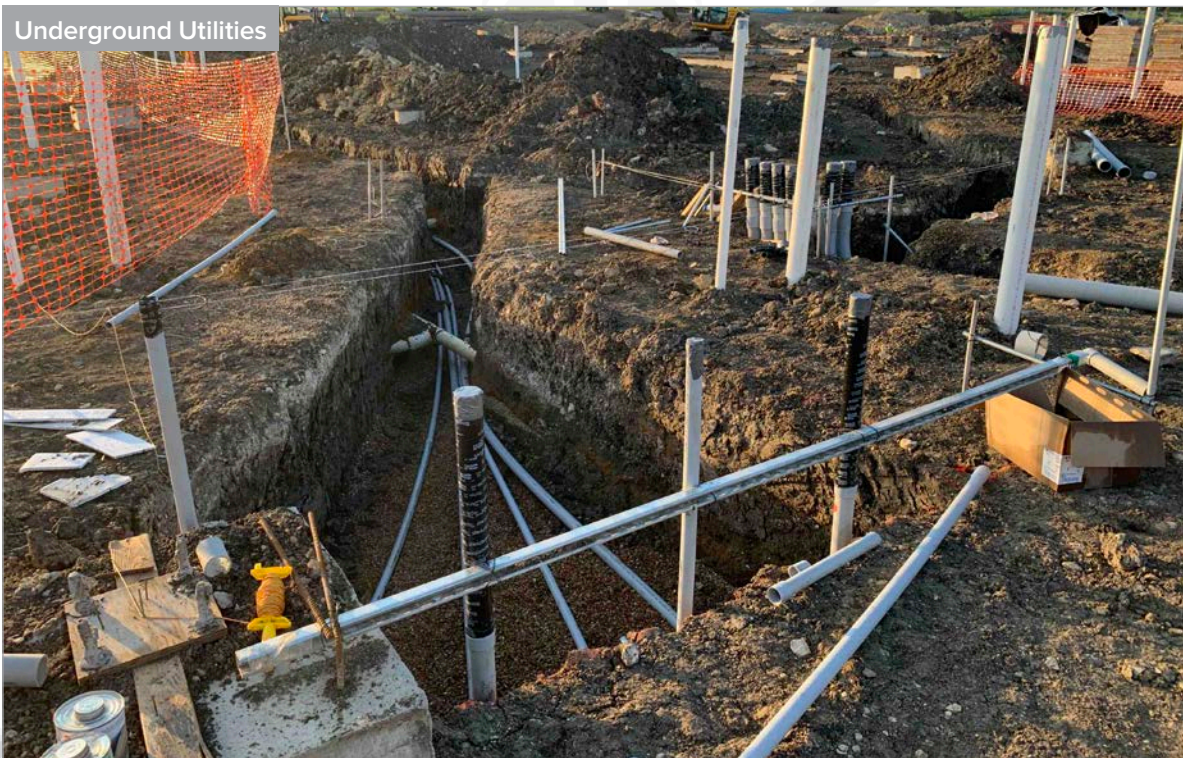

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

WORK COMPLETED AND ONGOING:

Site

- Baseball and softball fields are ready for turf (installation to occur in about four months)
- Detention pond irrigation ongoing
- Sports lighting installation at tennis courts ongoing
- Irrigation installation ongoing on west and east side of the property
- Irrigation well installation ongoing
- Track excavation and installation ongoing

Building

- Steel erection complete – Areas A, B, C, E, L, M, P, Q, R, and S
- Steel erection is ongoing – Areas D, F, G and N
- MEP/Fire Sprinkler overhead ongoing – Areas D, E, M, P, Q, R, and S
- Fire Sprinklers approved first and second floors – Areas A, B and C
- Framing complete – Areas A, A2, B, B2, C, C2, and D
- Framing ongoing – Areas E1, E2, Q, and R
- Interior CMU walls are ongoing – Areas L, M and P

- Roofing started – Areas A, B, C, P, Q, R and S
- Exterior waterproofing ongoing – Areas D and E
- Brick Veneer installation ongoing north side – Areas A, B, C and R
- Fireproofing ongoing – Areas D2 and E
- Fire alarm has started – Areas A1, B1 and C1
- Painting has started – Areas A, B and C
- Low-voltage rough-in ongoing – Areas A1, B1 and C1
- Security and access control ongoing – Areas A1 and B2
- Tile installation ongoing in halls – Areas A, B and C
- Display case framing in main corridor ongoing
- Wood wall and bench framing ongoing at east side of main street corridor

Multipurpose Facility (MPF) and Ancillary Buildings

- Masonry ongoing – Areas U and V
- Masonry skin installation ongoing – Area T
- Waterproofing ongoing – Area V and concession stands



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022



PROSPER ISD CHILDREN'S HEALTH STADIUM

E 1ST ST

LOOKING NORTHWEST



E 1ST ST

LOOKING SOUTHEAST

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Exterior Masonry Progress



Exterior Masonry Progress



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Auditorium Entry



Student Commons (Library)

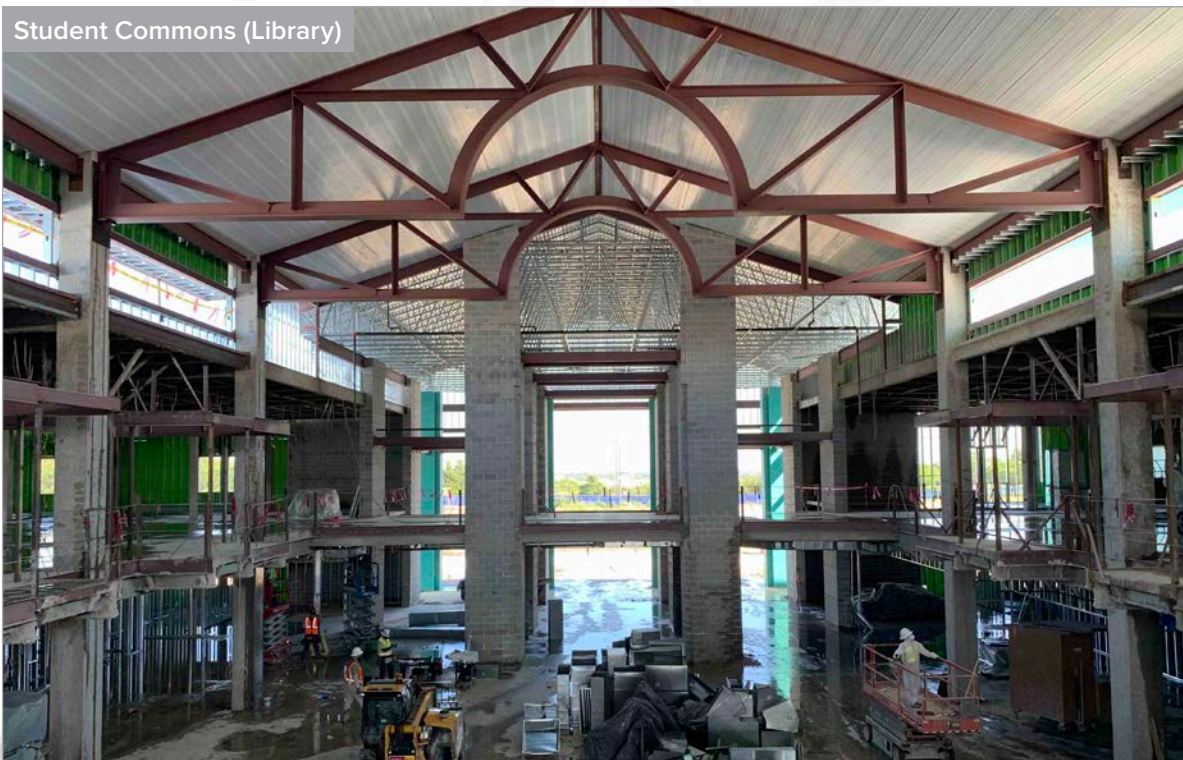

BOARD UPDATE


PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Student Commons (Cafeteria)

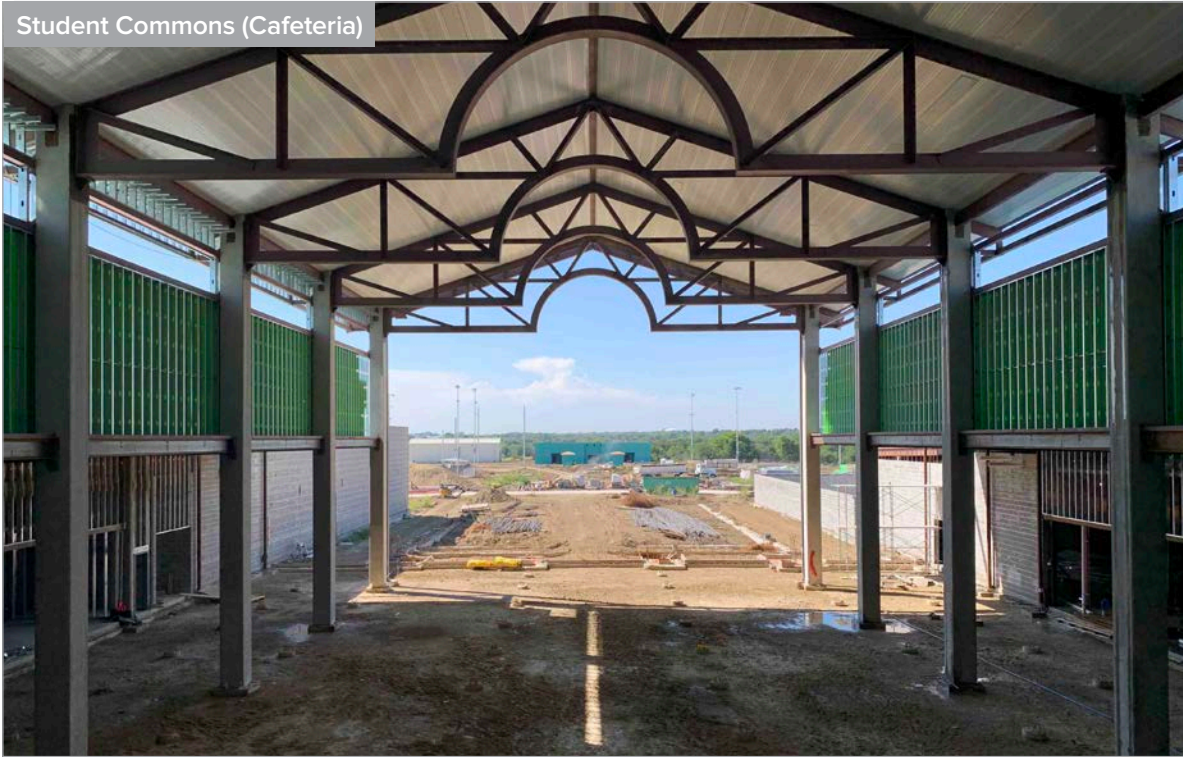

Main Street Corridor (East Academic Wing)

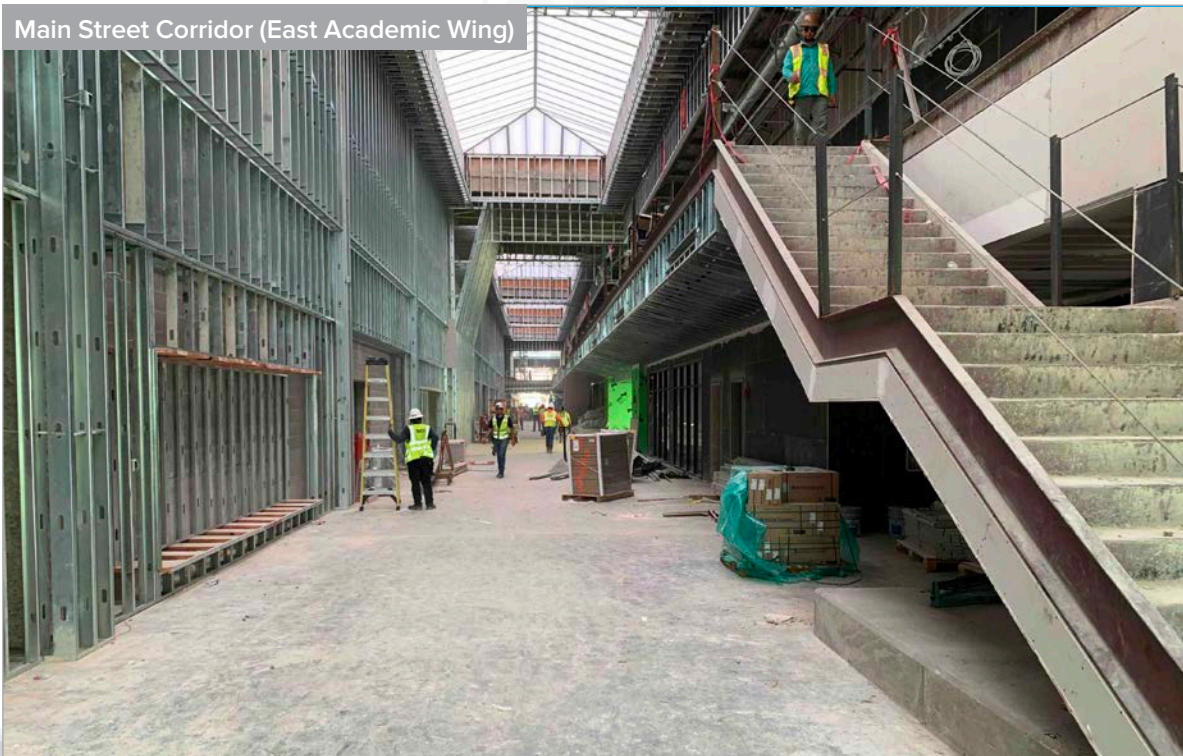

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

East Academic Wing Courtyard



Typical Academic Corridor

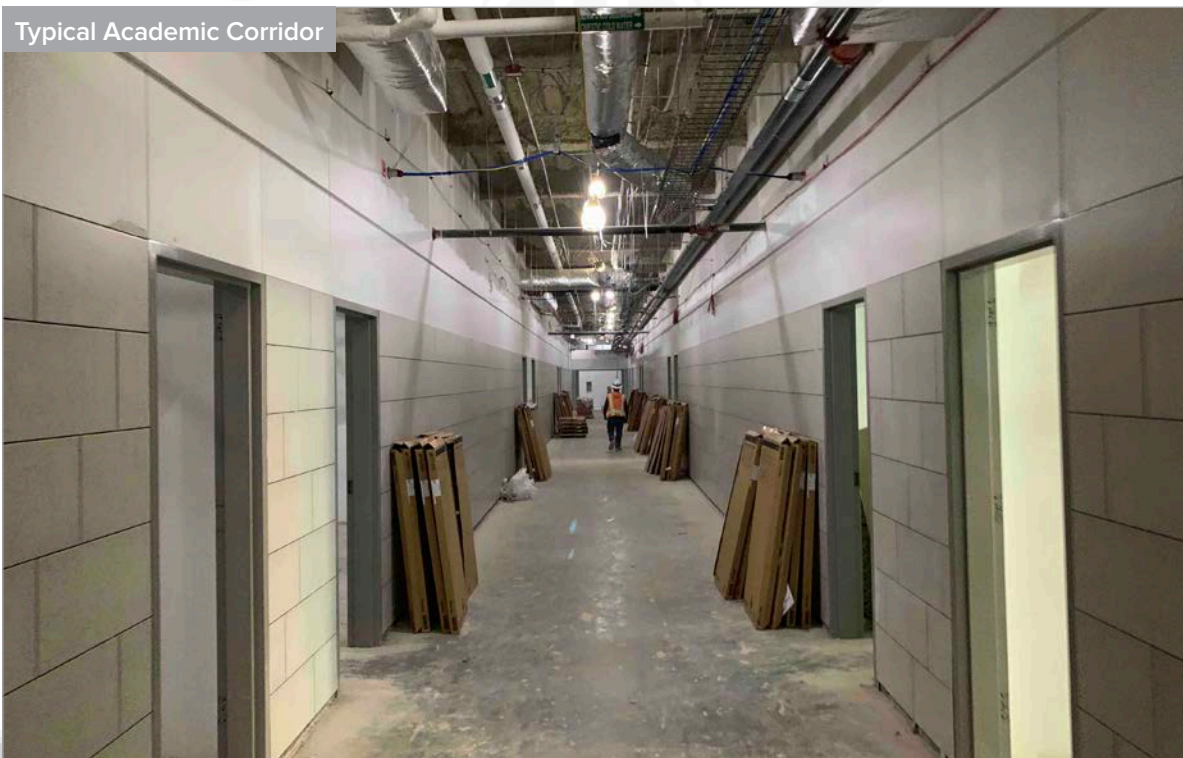

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Typical Academic Corridor



Main Street Corridor (East Academic Wing)

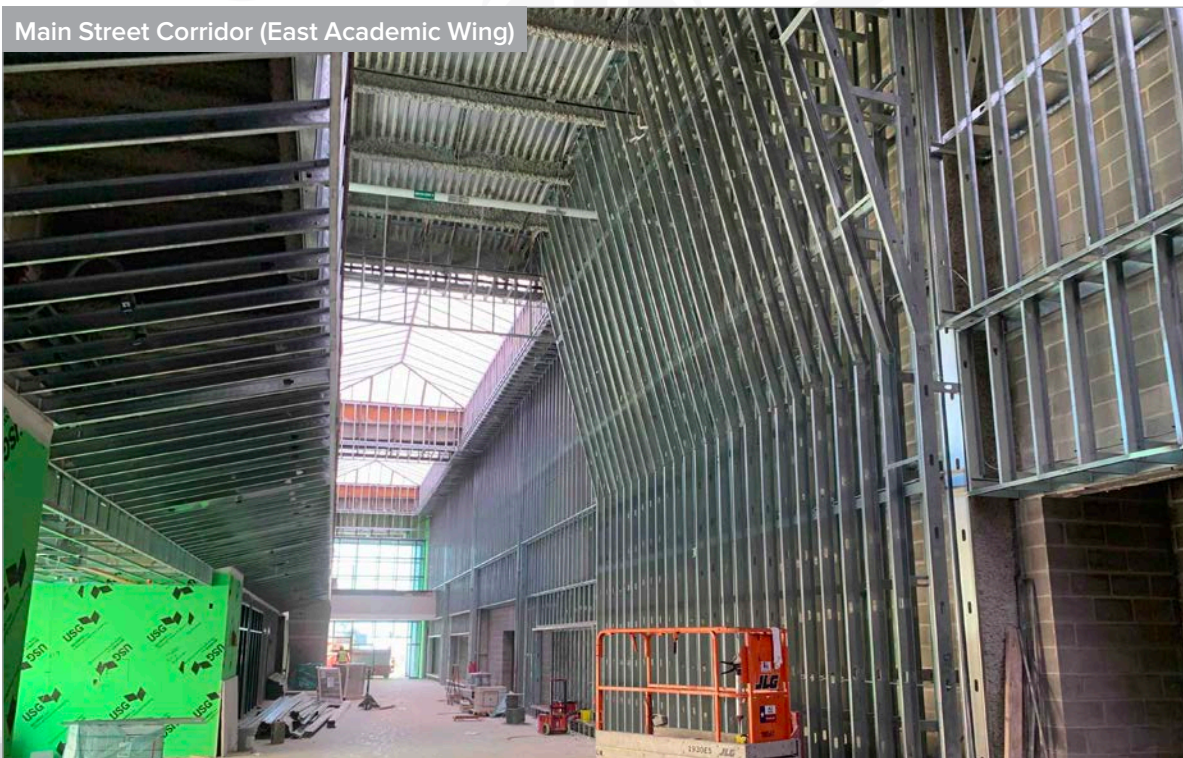

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

West Academic Wing Courtyard



Structural Steel Erection at Arena

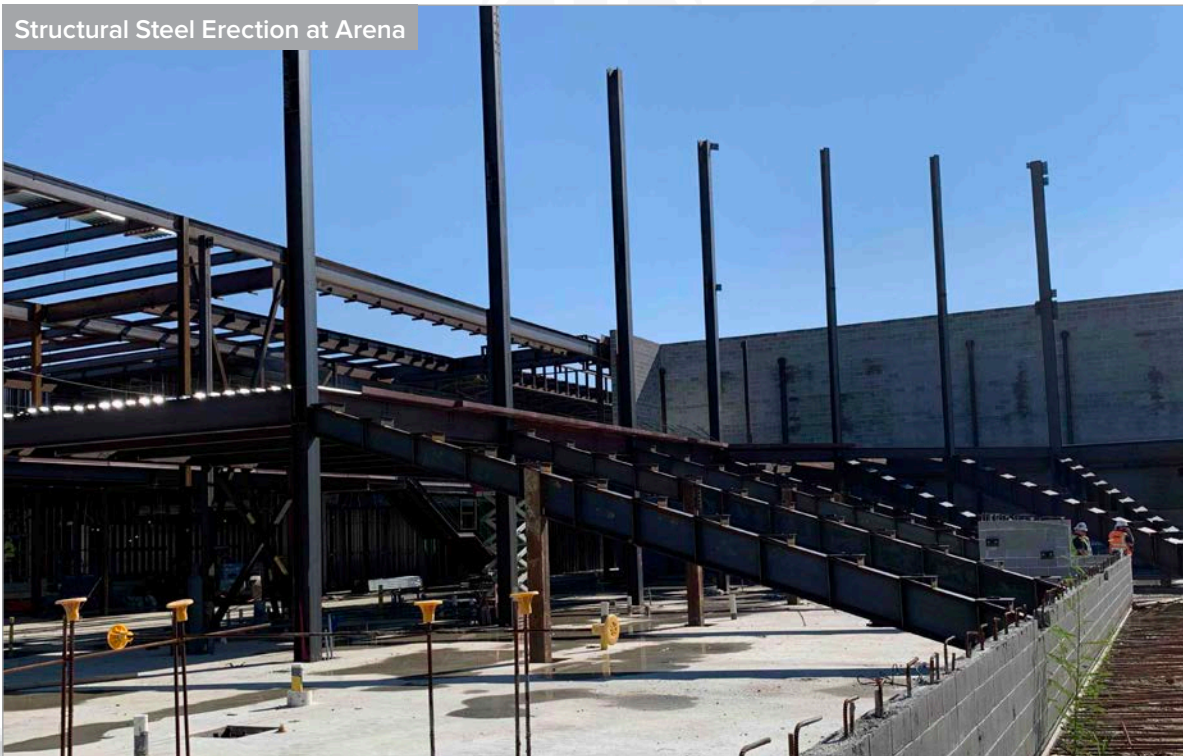

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Structural Steel Erection at Arena



Exterior Progress at MPF



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Interior Progress at MPF



Weight Room at MPF

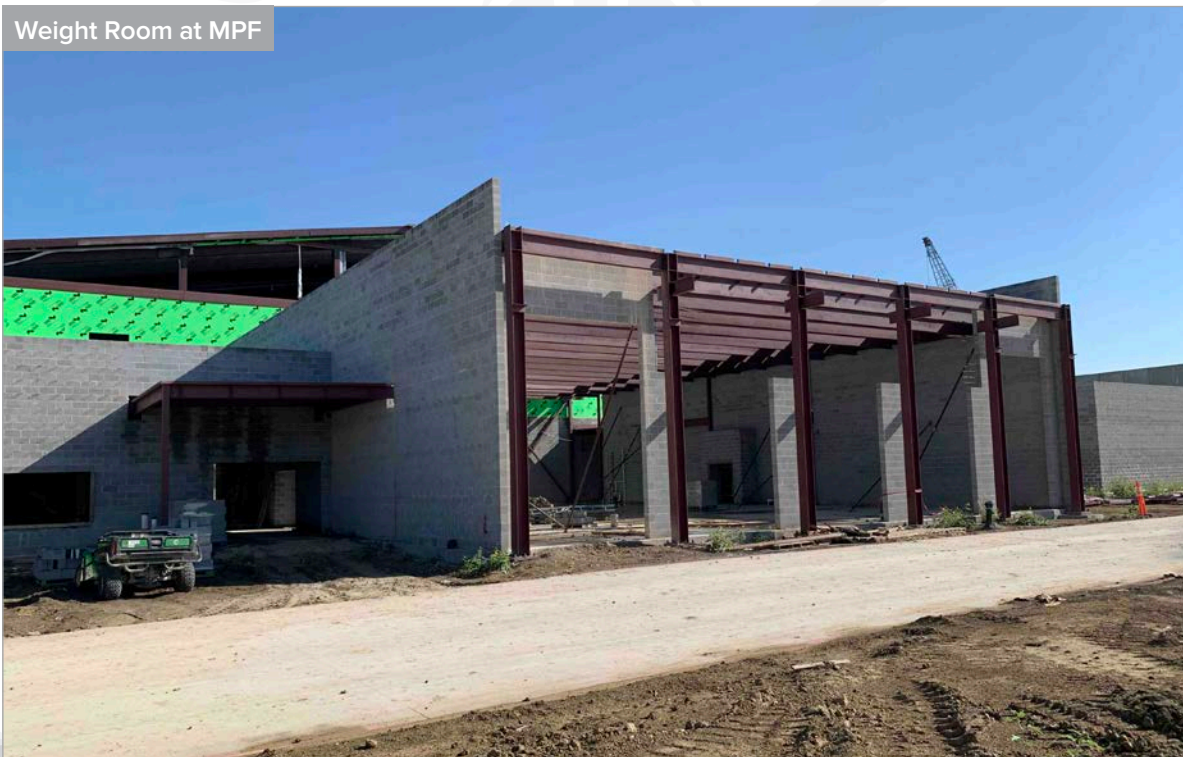

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT




WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Track/Tennis Concession/Restroom



Subgrade Prep at Track

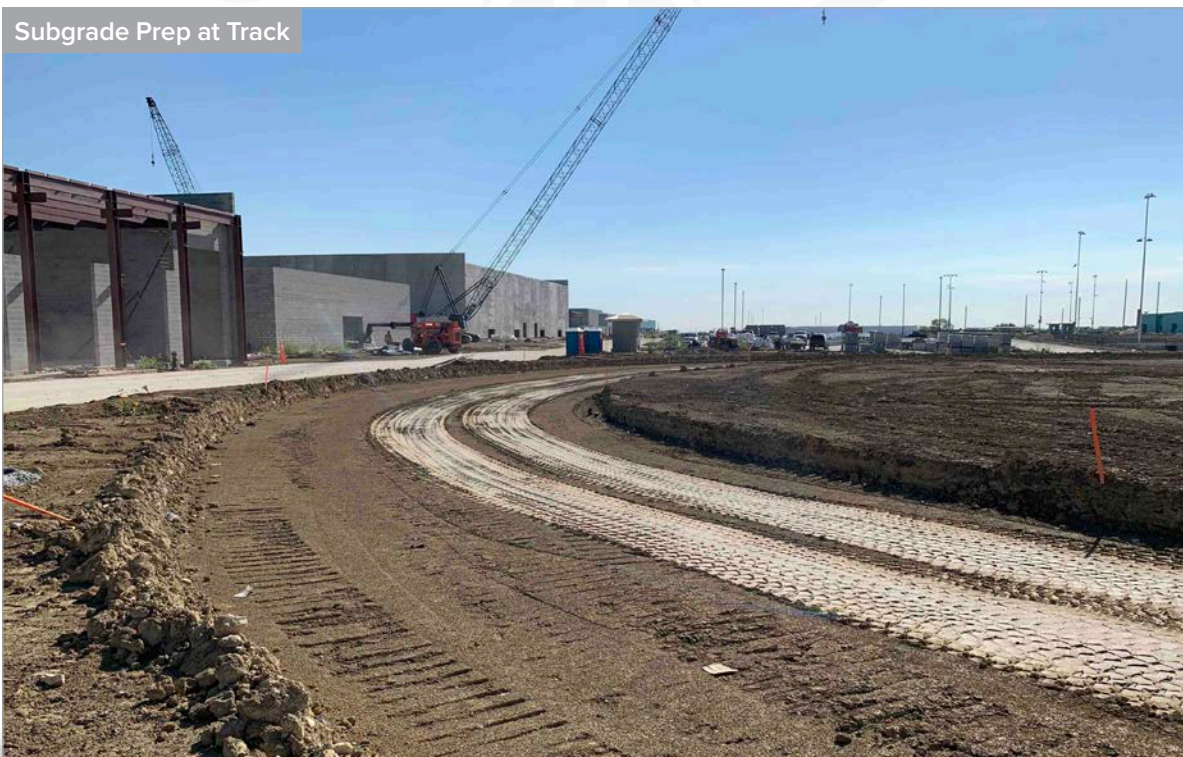

BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Site Retaining Walls



Baseball/Softball Ticket Booths



BOARD UPDATE

PROSPER INDEPENDENT SCHOOL DISTRICT



WALNUT GROVE HIGH SCHOOL (HS#3)

AS OF SEPTEMBER 2022

Baseball/Softball Concession/Restroom

